

# UTILITIES UNDERGROUNDING PROGRAM SKYLINE - PROJECT BLOCK 4Z

October 2012

### WELCOME TO THE UTILITIES UNDERGROUNDING PROGRAM E-NEWS #4

This is the fourth e-news update to inform you of the progress of the Utilities Undergrounding Program in the Skyline/4Z Project Block area. Approximately once a month during construction, or when significant events occur, you will receive an e-mail update.

# UTILITIES UNDERGROUNDING PROGRAM DESCRIPTION

The City of San Diego has been undergrounding utility lines since 1970. Approximately 1,200 miles of overhead utility lines remain to be undergrounded. The City, in cooperation with SDG&E, Cox Communications, Time Warner and AT&T, is currently undergrounding the utility lines in your community.

# PROJECT BLOCK 4Z HIGHLIGHTS


- 2.70 miles of utilities will be undergrounded
- 374 private residences will have their utilities undergrounded
- 55 street lights will be installed
- 30 shade trees will be installed
- 30 curb ramps will be installed
- Streets will be resurfaced or slurry sealed curb-to-curb

# PROJECT BLOCK 4Z CONSTRUCTION ACTIVITY PHASES

- Construction start: March 2012
- Panel work: March 2012 February 2013
- Trench work: May 2012 March 2013
- Cabling, cut-overs and streetlights: May 2014 January 2014
- Overhead line removal: Spring 2014
- Street resurfacing: 2014

# PROJECT BLOCK 4Z CONSTRUCTION ACTIVITIES

- Trenching activities are currently taking place on Woodbine Way between Siena Street and Arrowwood Drive.
- Trenching activities are currently taking place on Arrowwood Drive, north of Brookhaven Road.

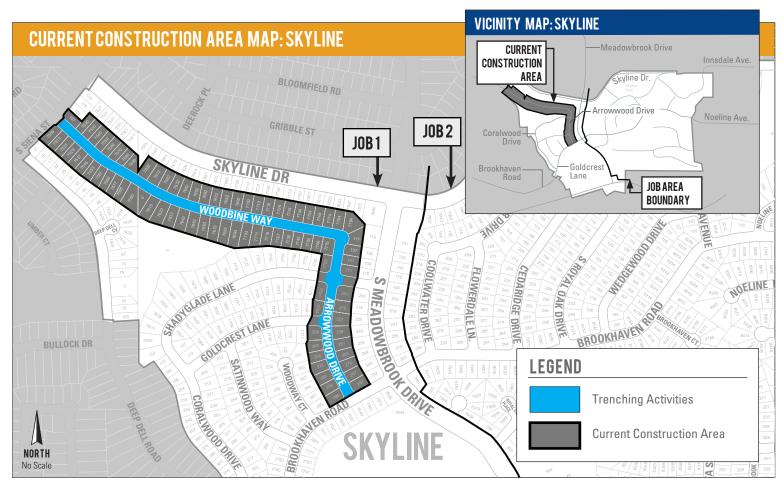



CONTACT

INFORMATION

Information Line: (619) 533-3841 Email: undergrounding@sandiego.gov Website: www.sandiego.gov/undergrounding



### PANEL AND TRENCHING ACTIVITIES

Panel work by Southern Contracting is well underway. Panel work is when electricians prepare the electrical panel at your home to receive underground service. Approximately two weeks prior to any work being performed on your property, you should receive a door hanger with the electrical contractor's name and phone number on it. If you have any questions or concerns about the work, please do not hesitate to contact the electrical contractor. **To date, approximately 98% of the panel work has been completed.** 

You have likely seen trenching crews working in the streets. **Trench work is approximately 50% complete in Job 1** of the Project Block 4Z. We ask for your patience as they complete this work, as it can be disruptive and distracting. Approximately two weeks prior to the start of the trench work on your property and in the street, you will receive a door hanger with the trenching contractor's name and phone number on it. If you have any questions or concerns about the work, please do not hesitate to contact the contractor.



Southern Contracting installed their panel work to the electrical panel so that the underground service can be installed.

# CABLING. CUT-OVER AND OVERHEAD LINE REMOVAL

After all trenching operations were completed, the cabling portion of the work began. Cabling involves technicians placing new utility lines in the new conduits, so that the new lines can be "energized" and brought into service. Once the new system has been energized, the process to "cut-over" customers from overhead to underground services will begin. Once customers have been cut-over, the overhead lines will be removed. We anticipate this process will move very swiftly and it's not nearly as disruptive or distracting as the trenching work, which is why you may not even see us working. A door hanger will be left prior to the contractor visiting your property.

### **CORRECTION NOTICES**

Currently, there are 73 residences in Jobs 1 that need to make corrections to their services or properties in the 4Z/ Skyline Project Block. Most of these corrections will be minor and are the responsibility of the property owner. Corrections need to be complete before we can cut customers over to the new underground system. Customers who are not cut-over to the new underground system risk loss of service when the overhead system is removed.

If you need to make a correction to your property in order to pass final inspection, you will receive a door hanger or letter from a City of San Diego inspector. The door hanger and letter have a description of the correction needed. Most of these corrections will be minor. Please do not delay in contacting the inspector whose name and phone number appear on these notices, so that the problem can be resolved.

# **SAFETY**

If you see anyone on your property that is not visibly wearing an identification badge, or if they are in a vehicle that is not marked with a contractor or utility company name, please call the Information Line at (619) 533-3841 or the San Diego Police Department. The construction crew must travel in marked vehicles and have proper identification at all times on the jobsite.

### **CONTACT US**

In the event that you are not satisfied or pleased with the work that was done on your property or your street, please let us know. **Please do not attempt to make corrections, adjustments or improvements yourself.** We promise to work with you on reaching a solution or creating an outcome that meets your needs and ours in this process. We will not be able to switch your services to the new underground system if any modifications were done to our work. If you are unsure about the status of the work that has taken place on your property or your street, contact us at:

- Information Line: (619) 533-3841
- Email: undergrounding@sandiego.gov

### UTILITIES UNDERGROUNDING PROGRAM VIDEO

A video about the Utilities Undergrounding Program can be seen by visiting our web site at www.sandiego.gov/undergrounding and clicking on video. By watching it, you can see all the processes associated with our work and gain a better understanding of what is involved in completing those processes.

We thank you in advance for your patience and support while we complete the Utilities Undergrounding Program project in the Skyline community.
