

UTILITIES UNDERGROUNDING PROGRAM

LINCOLN PARK – PROJECT BLOCK 4G

February 2013



WELCOME TO THE UTILITIES UNDERGROUNDING PROGRAM E-NEWS #38

This is the thirty-eighth e-news update to inform you of the progress of the Utilities Undergrounding Program in the Lincoln Park/4G Project Block area. Approximately once a month during construction, or when significant events occur, you will receive an e-mail update.

UTILITIES UNDERGROUNDING PROGRAM DESCRIPTION

The City of San Diego has been undergrounding utility lines since 1970. Approximately 1,200 miles of overhead utility lines remain to be undergrounded. The City, in cooperation with SDG&E, Cox Communications, Time Warner and AT&T, is currently undergrounding the utility lines in your community.

PROJECT BLOCK 4G HIGHLIGHTS

- 3.5 miles of utilities will be undergrounded
- 399 private residences will have their utilities undergrounded
- 48 street lights will be installed
- 63 shade trees will be planted
- 34 curb ramps will be installed
- Streets will be resurfaced or slurry sealed curb-to-curb


PROJECT BLOCK 4G CONSTRUCTION ACTIVITY PHASES

- Construction start: October 2008
- Panel and trench work: Oct. 2008 - January 2012
- Cabling, cut-overs and streetlights: May 2010 - Feb. 2013
- Overhead line removal: Spring 2013
- Street resurfacing: 2014


PROJECT BLOCK 4G CONSTRUCTION ACTIVITIES

- SDG&E is currently conducting cabling, cut-over and overhead line removal activities.
- AT&T is currently conducting overhead line removal activities.

CURRENT CONSTRUCTION AREA MAP: LINCOLN PARK

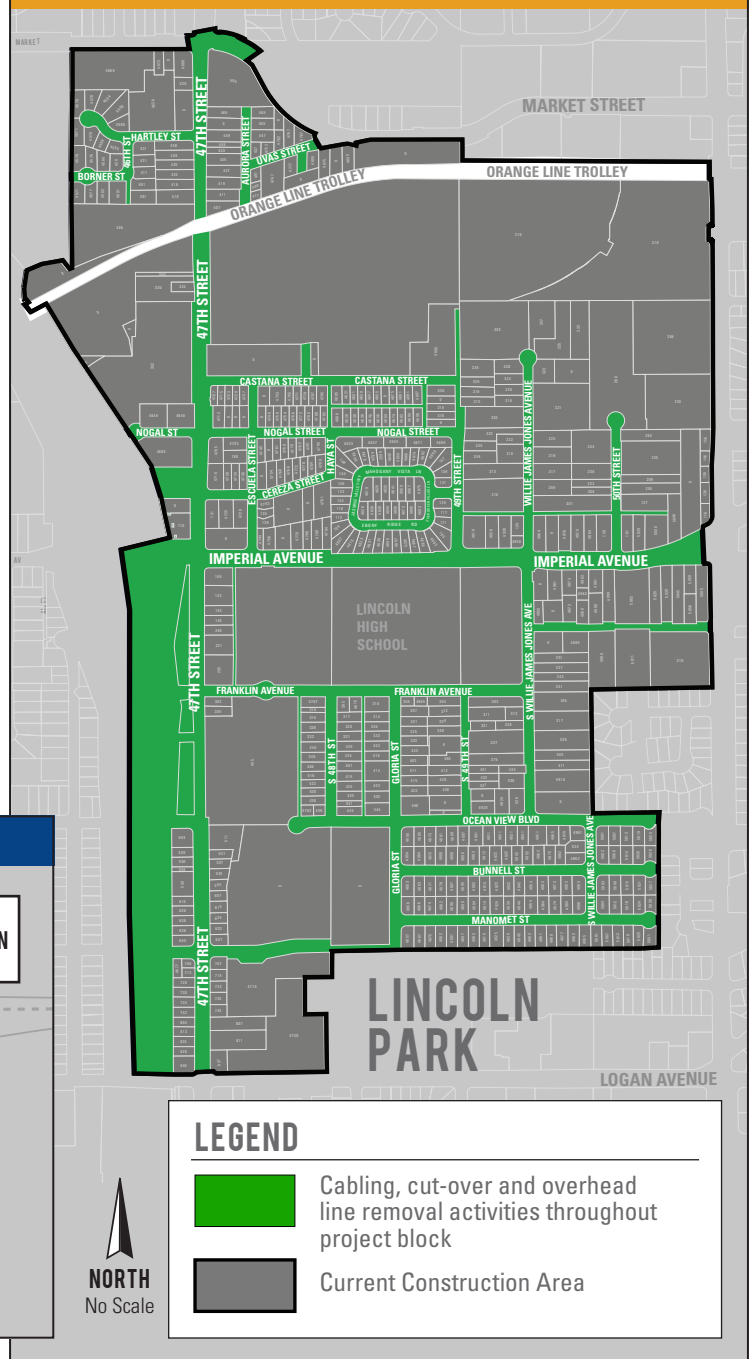

VICINITY MAP: LINCOLN PARK

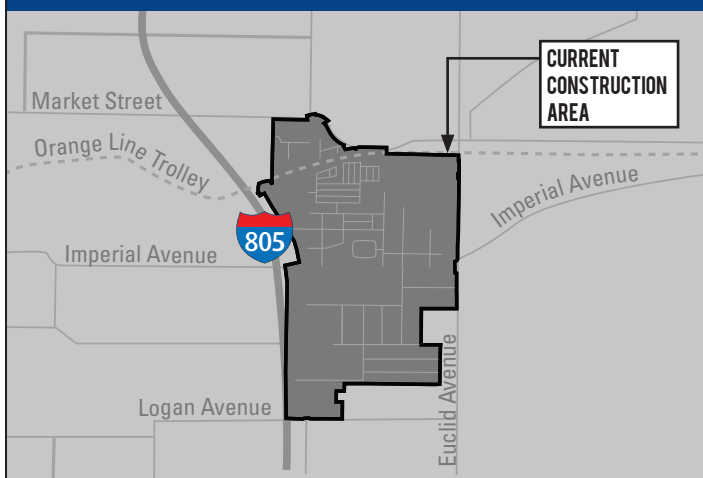

PANEL AND TRENCHING ACTIVITIES

Panel work is when electricians prepare the electrical panel at your home to receive underground service. Trenching activities involves digging a mainline trench in the street and a lateral customer service trench that connects the mainline trench to your utility box. Conduit lines, which house the underground utility cabling, are then installed and buried in the trenches.

- ▶ *Panel and trenching are 100% complete in Project Block 4G.*

CABLING, CUT-OVER AND OVERHEAD LINE REMOVAL

Cabling involves technicians placing new utility lines in the new conduits, so that the new lines can be “energized” and brought into service. Once the new system has been energized, the process to “cut-over” customers from overhead to underground services will begin. Once customers have been cut-over, the overhead lines will be removed. This process is not nearly as disruptive as the trenching work, which is why you may not even see us working. A door hanger will be left prior to the contractor visiting your property. Here is the current status of these activities:

- ▶ *Cox Communications is 100% complete with cabling, cut-over and overhead line removal activities.*
- ▶ *SDG&E is 95% complete with cabling and cut-overs activities. They are 65% complete with overhead line removal activities.*
- ▶ *AT&T is 100% complete with cabling and cut-overs. They are 90% complete with overhead line removal activities.*

STREETLIGHT INSTALLATION

- ▶ *100% of the streetlights have been installed.*



Undergrounding crews work along side the MTS Trolley line to install an underground electrical vault.

CUSTOMER NOTICES

Permission to Enter Forms: Before construction began on this project, property owners were sent a Permission to Enter (PTE) form. By signing this form, you enroll your property in the Utilities Undergrounding Program and grant crews access to the exterior of your property to complete the undergrounding work at no up-front cost. Property owners within this Project Block who have not signed a PTE form or failed to return it by the required deadline date, will be responsible for all costs and permits needed for converting their property to receive underground utility service.

- ▶ *All property owners in Project Block 4G/Lincoln Park have submitted their PTE form.*

Correction Notices: If you need to make a correction to your property in order to pass final inspection, you will receive a door hanger or letter from a City of San Diego inspector. The door hanger and letter have a description of the correction needed. Please do not delay in contacting the inspector whose name and phone number appear on these notices, so that the problem can be resolved.

Most of these corrections are minor and are the responsibility of the property owner. Corrections need to be completed before we can cut customers over to the new underground system. **Customers who are not cut-over to the new underground system risk loss of service when the overhead system is removed.**

- ▶ *All necessary corrections to services or properties have been completed, inspected and approved.*

CUSTOMER RESOURCES

Project Satisfaction: In the event that you are not satisfied or pleased with the work that was done on your property or your street, please let us know. **Please do not attempt to make corrections, adjustments or improvements yourself.** We will not be able to switch your services to the new underground system if any modifications were done to our work.

Safety: All project crew members should be wearing proper identification while on the job site. If you see anyone suspicious on your property, please call the Information Line at (619) 533-3841 or the San Diego Police Department.

Program Info: Visit www.sandiego.gov/undergrounding to access more information on the program, including a video and brochure.

We thank you in advance for your patience and support while we complete the Utilities Undergrounding Program project in your community.
