


Construction Progress

The project scope was developed in Winter 2024, followed by preconstruction, procurement processing and grant administration. Construction began in May 2025 and progressed steadily for approximately one year



Renovation Projected Timeline

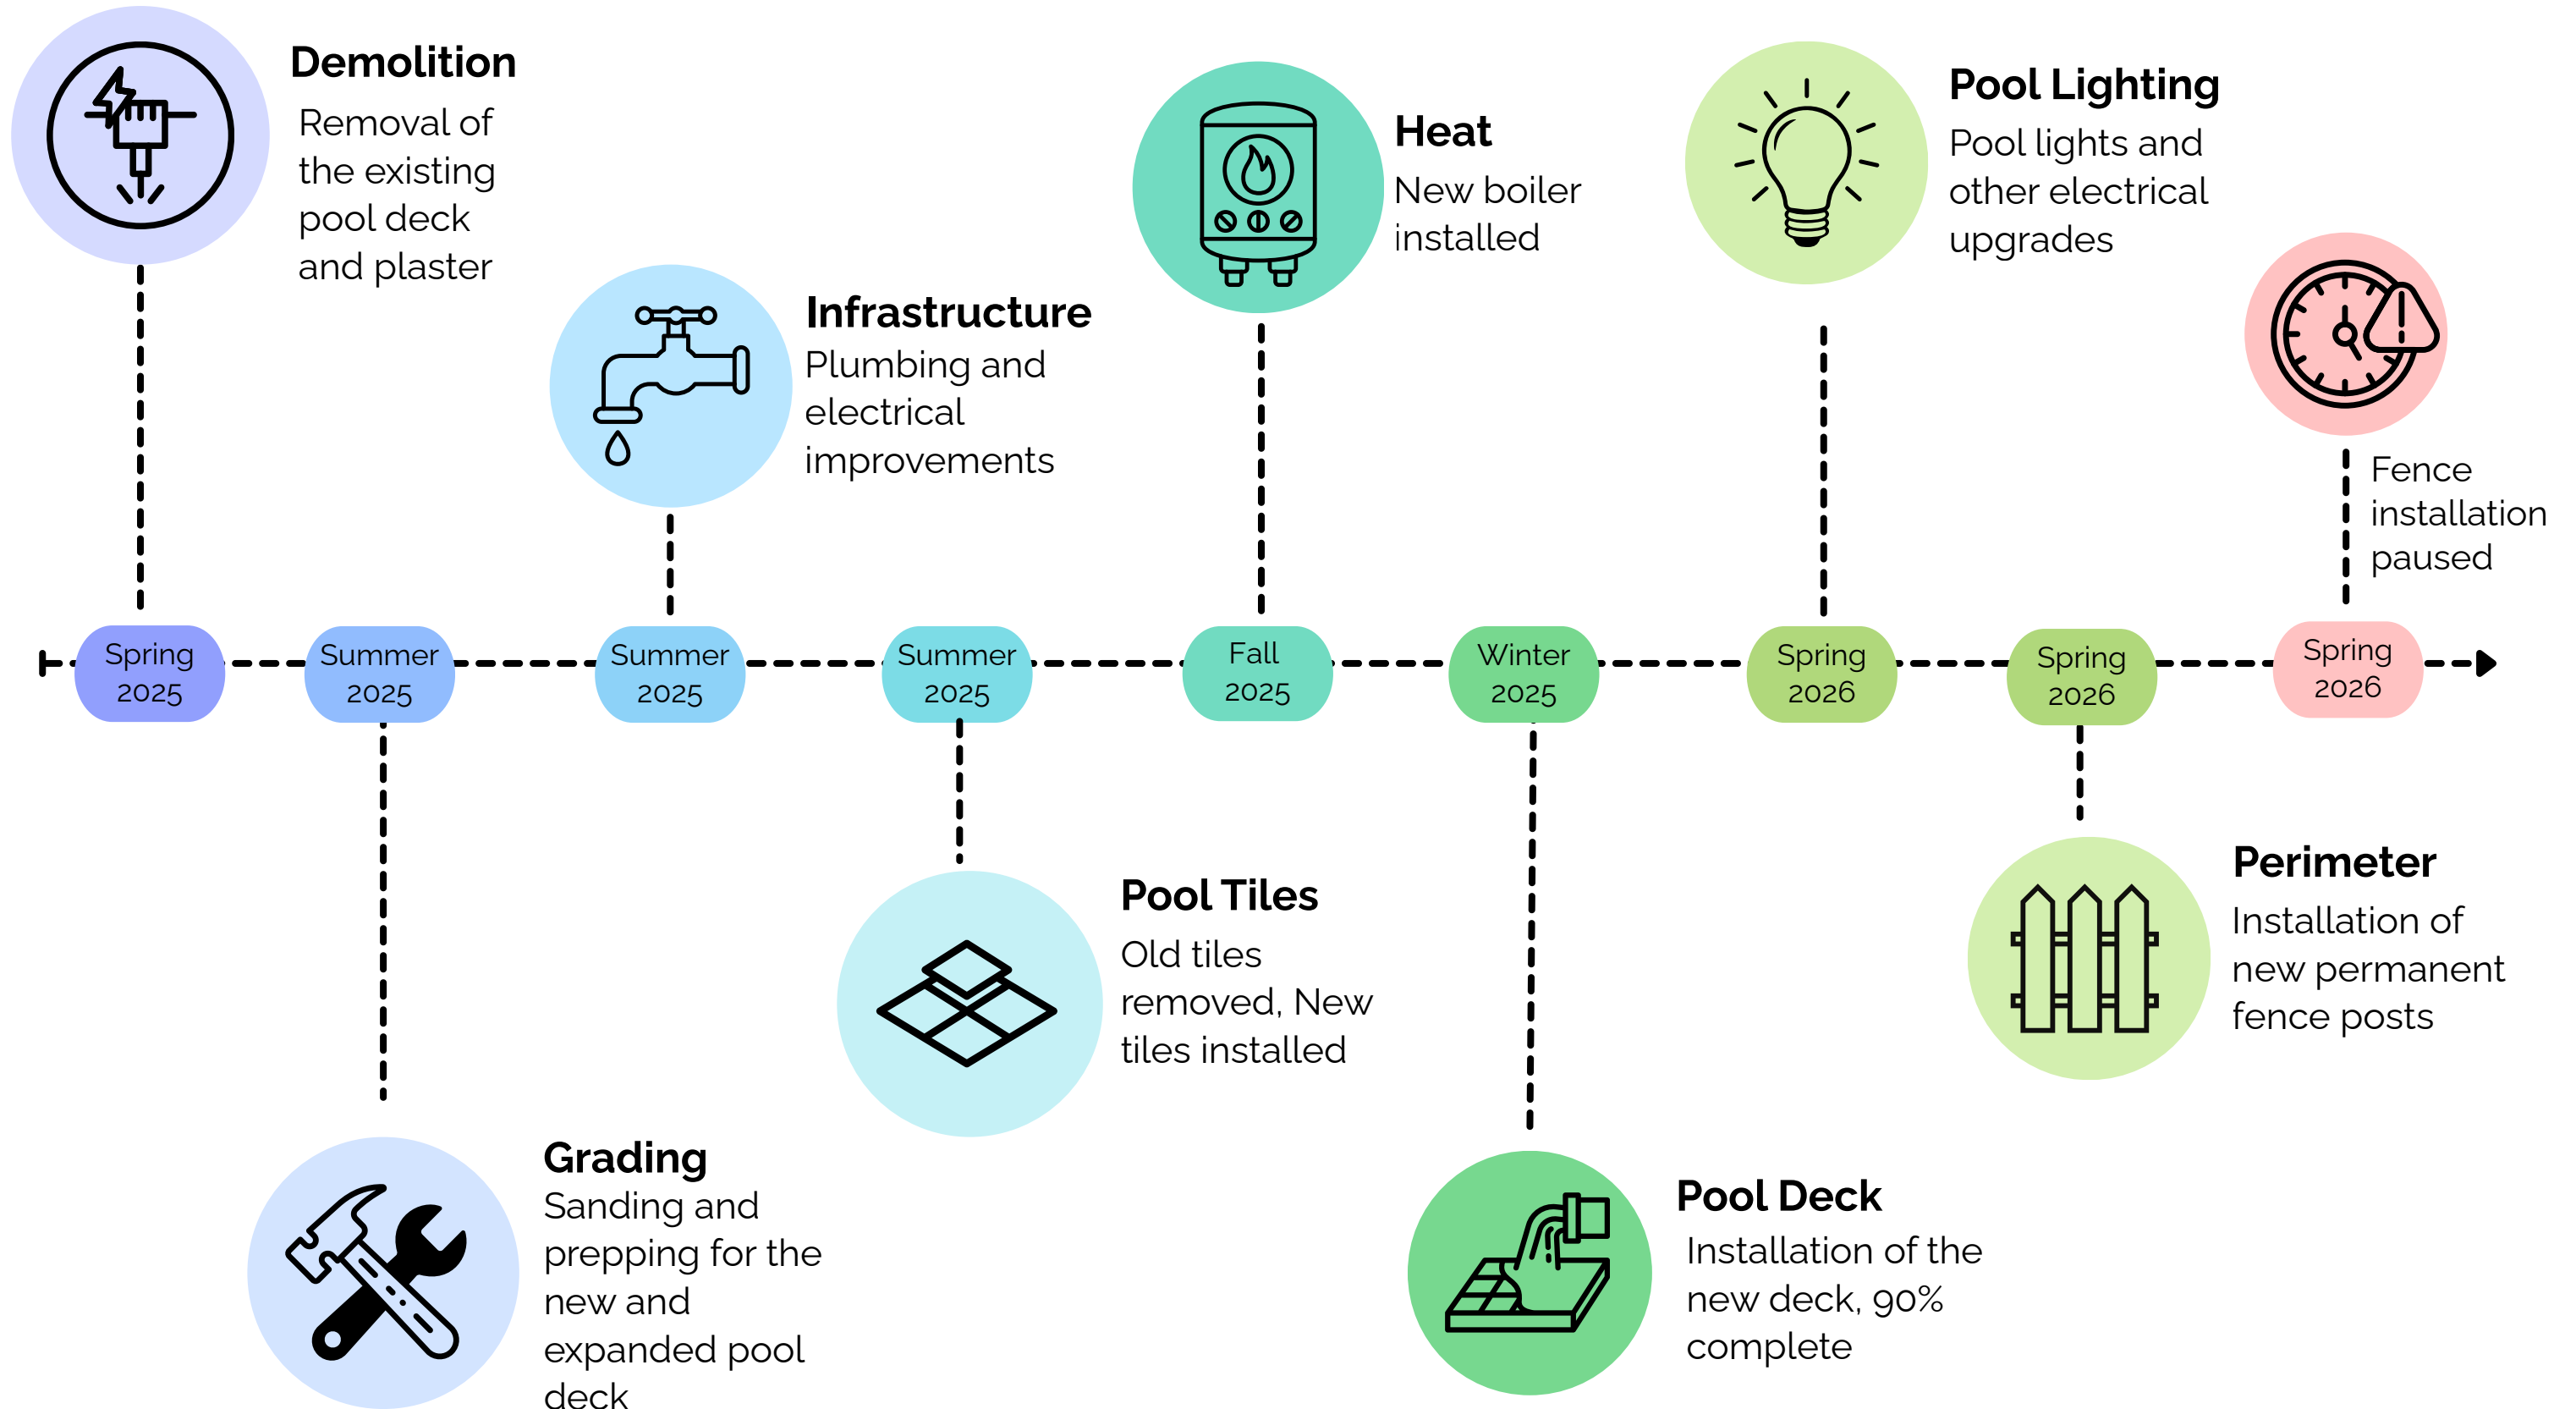

Clairemont Pool is currently anticipated to reopen in Spring 2027. The schedule remains subject to change based on contractor mobilization, equipment lead times, final permitting and inspections, and project closeout. As remaining construction milestones are completed, the City will have greater certainty regarding the reopening schedule. The Parks and Recreation Department remains committed to completing the project and reopening Clairemont Pool as soon as possible and will continue to provide updates to the community as work progresses.

Task	Expected Completion
Pool Filtration System	10/16/2026
Fence Posts and Panels	12/1/2026
Pool Pump and Motor System	12/1/2026
Chemical Controller Upgrade	12/1/2026
Pool Deck, Plaster and Fill	4/1/2027

Current Critical Path

May 2026- Fencing Work Paused

Fencing work was paused due to limited remaining capacity on the City's existing fencing contract. Because the fencing work is sequenced with the remaining pool construction, the work was temporarily paused while a procurement solution was developed.

September to March 2027- Remaining Construction

Work will resume with installation of the permanent fence panels, followed by final pool plaster. The fence and plaster must be completed in sequence. During the plaster work, the new pump and filtration system will be installed.

Spring 2027- Reopening

Once construction, final permitting inspections and project closeout are complete, Clairemont Pool is anticipated to reopen in Spring 2027. The schedule remains subject to change as these final steps progress.
Thank you for your continued support and patience!

September 2026- Procurement & Permitting

The sole source procurement is approved by the Purchasing Department and a purchase order is being established, The County Department of Environmental Health and Quality has approved pool enclosure site plans. Contractors are on track to begin mobilizing.

July 2026- City Council Action

City Council approved an amendment to increase capacity on the Citywide fencing contract. The amendment clarified that the contract, and because the fencing work had already been started, a sole source procurement process was identified to complete the permanent fence.

