Regional Park Improvement Funds Projects Allocation & Expenditure Semi-Annual Update

Presented to the Regional Park Improvement Fund Oversight Committee

April 19, 2018



BACKGROUND

- RPIF is derived from Mission Bay Park lease revenue per City Charter Sec 55.2
- Charter was revised under Measure J passing on November 2016 to include:
 - First \$3.5M or 35%, whichever is greater above the threshold amount of \$20 million from the Mission Bay Leasehold revenues goes into the RPIF beginning in Fiscal Year 2018.
 - RPIF can only be used for capital improvements/deferred capital
- This presentation only covers on-going CIP's funded by the RPIF

PROJECTS COMPLETED TO DATE

- Ocean Beach Comfort Station Replacement
- Museum of Man Roof Reconstruction
- Diamond Street Stairs Reconstruction
- Palisades Park Comfort Station
- Pescadero Street Stairs Reconstruction
- California Tower Electric Room Relocation
- Los Peñasquitos Ranger Station
- Balboa Park Hall of Nations Foundation Reconstruction
- Jas Arnold Trail For All People
- Coastal Beach Access Project
- Chicano Park Comfort Station Replacement

OLD MISSION DAM PRESERVATION S-00611

- Managed by P&R Department
- Scope
 - Completion of the 5 year Mitigation, Monitoring & Reporting Program previously required by the 2008 dredging of the historic dam
- Financial
 - Total Cost \$ 0.918M
 - RPIF Allocation = \$0.315M (FY10)
- Status
 - Extended 5 yr mitigation monitoring due to contractor default
 - Acquiring approvals for permitting longterm dredging
 - Mitigation to Complete in FY18
 - Negotiation is in progress with resource agencies for final sign off





MISSION TRAILS REGIONAL PARK MULTI TRAIL SYSTEM S-10066

- Managed by P&R Department
- Scope
 - Construction of approx. 5,000 LF of new trail & the rehab of approx. 3,500 LF of existing trail
- Financial
 - Total Cost \$0.20M
 - RPIF Allocation: \$0.20M (FY11)
- Status
 - Thru Park Master Plan (MP) & Environmental Assessment
 - Work will be completed after completion of the Natural Resources MP & MP Update (both ready for public review in FY18)
 - Construction to complete in FY 19.



COWLES MOUNTAIN TRAIL – MISSION TRAILS S-10065

- Managed by P&R Department
- Scope
 - Restoration of approximate
 2,000 FT of existing trail
- Financial
 - Total Cost: \$0.40M
 - RPIF Allocation: \$0.40M (FY11)
- Status
 - In Construction
 - Construction to complete in FY18





COASTAL BEACH ACCESS PROJECTS B-14073

Scope


- Repair and re-construction of 3 coastal access stairs:
 - Old Salt Pool in OB
 - Capri by the Sea in PB
 - Orchard Ave in OB

Financial

- Total Cost: \$0.450M
- RPIF Allocation: \$0.435M (FY12)
- Due to 100-202 Coast Blvd. Emergency project, \$377,895 in funding was reallocated from project per Oversight Committee Action in FY17.
- RPIF of \$329,879 was added back to the project in FY17.
- RPIF of \$150,000 is being added in FY18.

- Bid/Award phase started.
- Construction to start in FY18 and complete in FY 18.



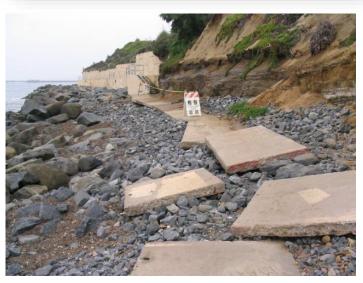

COASTAL BEACH ACCESS PROJECTS B-17029

Scope

 Emergency repairs at the coastal access stairs at 100-202 Coast Boulevard

Financial

Total Cost: \$.72M

RPIF Allocation: \$0.378M (FY17)

Due to 100-202 Coast Blvd.
 Emergency project, \$377,895 in funding was reallocated from project B-14073 Old Salt Pool, Orchard Ave & Capri by the Sea per Oversight Committee Action on July 21, 2016

- Construction started in FY17 and completed in FY 18.
- Working with CDP & SDP agencies for final sign off.





CHOLLAS LAKE PLAYGROUND RENOVATIONS PHASE I S-14002

Scope

 Replacement of existing playgrounds at Chollas Lake Park

Financial

Total Cost: \$1.939M

RPIF Allocation: \$0.974M (FY12)

• \$0.300M (FY18)

• Status:

 Construction is underway and scheduled to complete in FY18





CALIFORNIA TOWER SEISMIC RETROFIT L-12003.2

Scope

 The seismic retrofit of the California Tower to upgrade the structural protection & improve the public safety of the iconic SD landmark


Financial

Total Cost: \$4.061M

RPIF Allocation: \$1.50M (FY13)

RPFI Allocation: \$0.65M (FY18)

- Design phase completed in FY17
- Construction to start in FY19
- Construction to complete in FY19

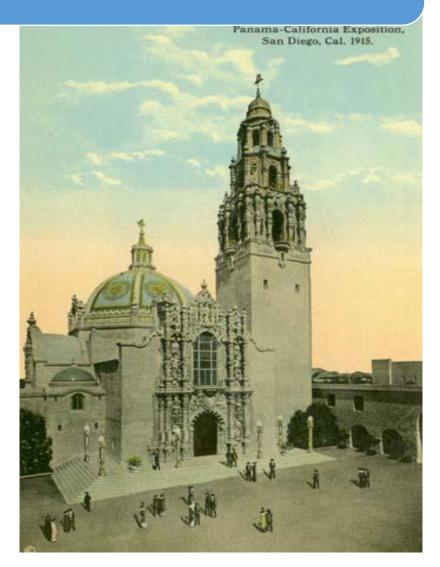

CHICANO PARK COMFORT STATION S-13003

Scope

 Improve/Expand existing aged, undersized and ADA noncompliant comfort station

Financial

Total Cost: \$1.16M

RPIF Allocation: \$0.2M(FY13)

• Status:

- Construction completed in FY18.
- Park opened to public on November 2017.



MOHNIKE ADOBE & HAY BARN RESTORATION S-13008

Scope

- Per Municipal Code, protect historic
 Mohnike Adobe Cultural Landscape on national register of historic places
- Phase 1 of the adobe home rehabilitation was completed in 2005

Financial

- Total Cost: \$2.697M
- RPIF Allocation: \$1M (FY13 & FY15)
- RPIF Funds of \$852,402 were reallocated to fund other projects
- RPFI Funds of \$1M was added back on the project (FY 2017)

- Feasibility Study Completed
- Design & Environmental permitting phase to start in FY 18.
- Construction is scheduled to start in FY 20.





SUNSET CLIFFS NATURAL PARK HILLSIDE IMPROVEMENTS PHASE I (S-10091 / L-16001)

Scope

 Construction of new trails within the entire park including revegetation plan and removal of demolished housing.

Financial

Total Cost: \$1.0M (Phase IA)Total Cost: \$3.2M (Phase 1B)

RPIF Allocation:

- \$1.1M (FY14)
- \$1.0M (FY18)

- Phase 1A (L-16001.1) Construction completed in FY 16
- MMRP PH1A (L-16001.1) completes in 2021
- Phase 1B (L-16001.2) Design completed in FY18;
 Construction started in FY 18 and estimated to complete in FY19
- MMRP PH1B (L-16001.2) completes 2023



SUNSET CLIFFS NATURAL PARK REMOVAL OF LOMALAND DR. AND LADERA ST. STRUCTURES PHASE 2 (L-14005.1)

Scope

- The removal of Lomaland Dr. and Ladera St. structures; regrading and re-vegetating the sites; construction of overlooks and trails.
- Financial
 - Total Cost: \$835K
 - RPIF Allocation \$456K
- Status:
 - In Design
 - Environmental permits to complete FY 19
 - Construction to start FY 20
 - Construction to Complete FY 21



SUNSET CLIFFS NATURAL PARK HILLSIDE DRAINAGE IMPROVEMENTS PHASE 3 (L-14005.2)

Scope

 Design drainage solutions to arrest severe soil & coastal bluff erosion

Financial

- Total Cost: \$4M (Phase I)
- RPIF Allocation (\$4M total):
 - \$1M (FY13)
 - \$1M (FY15)

- In Design
- Construction to start FY 20
- Construction to Complete FY 21



LJ PARKWAY/ MT SOLEDAD EROSION CONTROL B-10089

Scope

 Stabilize the eroding slope on the east side of La Jolla Parkway and reconstruct the failing brow ditches.

Financial

Total Cost: \$2.58M

RPIF Allocations: \$500K (FY15)

- Feasibility Study Phase completed
- Design started & estimated to complete in FY19
- Construction to start in FY19 and to complete in FY20.






JUNIPERO SERRA MUSEUM ADA IMPROVEMENTS S-15034

- Scope
 - Assess & improve Junipero Serra Museum ADA deficiencies
- Financial
 - Total Cost: \$2.27M
 - RPIF Allocations:
 - \$0.5M (FY15)
 - \$0.5M (FY16)
 - \$0.5M (FY18)
- Status:
 - Feasibility Study Phase-Completed
 - Design started in FY 18 to complete in FY 20.
 - Construction to start in FY 20 & complete in FY 21





BALBOA PARK WEST MESA COMFORT STATION REPLACEMENT S-15036

Scope

 Replace two existing comfort stations with new facilities on the West Mesa of Balboa Park.

Financial

Total Cost: \$1.89M

RPIF Allocation: \$1.0M (FY15)

RPIF Allocation: \$300K (FY16)

RPIF Allocation: \$200K (FY17)

- Design completed in FY18
- Construction to start FY18
- Construction to complete FY19





EB SCRIPPS PARK COMFORT STATION REPLACEMENT S-15035

- Scope
 - The replacement of the existing comfort station
- Financial
 - Total Cost: \$2.93M
 - RPIF Allocation:
 - \$0.250M (FY14)
 - \$0.700M (FY17)
- Status:
 - In Design
 - Construction to start FY19
 - Construction to complete FY21



BALBOA PARK BUD KEARNS AQUATIC COMPLEX S-17000

Scope

 Improvement to the pool mechanical systems to allow the recycling of the pool water, ADA path of travel and interior tenant improvement.

Financial

• Total Cost: \$1.544M

RPIF Allocation:

\$0.500M (FY17)

- Design phase started in FY 18
- Construction to start FY20 and complete in FY20





MUSEUM OF ART ELEVATOR MODERNIZATION B-10042

Scope

 The project consists of modernization upgrades to one passenger elevator and two freight elevators.



Financial

- Total Cost: \$1.167M
- RPIF Allocation:
 - \$0.120M (FY17)
- Status:
 - Construction started in FY17 and scheduled to complete in FY 19.

CHOLLAS LAKE IMPROVEMENTS, PHASE 1 – CHOLLAS LAKE ELECTRICAL SERVICE L-18001.1

Scope

 Extend SDG&E service to the park and provide services to the park buildings.



• Total Cost: \$750,000

RPIF Allocation:

• \$143,733 (FY18)

• Status:

 Project is in preliminary design phase.





BERMUDA AVE COASTAL ACCESS & SEAWALL REPAIRS B-17110

Scope

 Replacement of eroded stairs and seawalls.

Financial

- Total Cost: \$1.40M
- RPIF Allocation:
 - \$0.384M (FY17)

• Status:

- Project is in Preliminary Design Phase.
- Design phase to start in FY18.
- Construction phase to start in FY20 and complete in FY21.





SANTA CRUZ AVE ACCESS STAIRS AND WALKWAY B-18027

Scope

 Repair or replacement of stairs, walkways, and stabilization of the fill slope.

Financial


- Total Cost: TBD
- RPIF Allocation:
 - \$0.425M (FY18)
- Status:
 - Project is in Preliminary Design Phase.





NARRAGANSETT AVE ACCESS B-18026

- Scope
 - repair and replacement of the stairs
- Financial
 - Total Cost: TBD
 - RPIF Allocation:
 - \$0.375M (FY18)
- Status:
 - Project is in preliminary design.

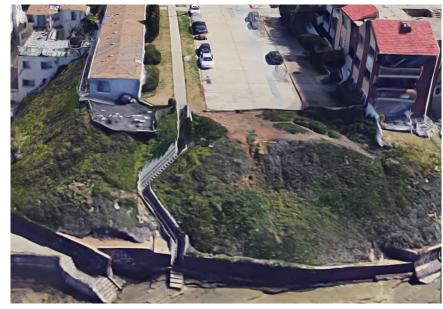



CASA DE BALBOA FIRE ALARM B-17181

Scope

 Replacement of the Fire Alarm Systems

Financial

Total Cost: \$1.588M

RPIF Allocation:

- Allocation of \$804,699 in FY17.
- The amount of \$137,815 was transferred to S-18002 Torrey Pines South Golf Course Improvement Project in FY18.

• Status:

Project is in preliminary design phase.





Regional Park Improvement Fund Allocation and Expenditure Bi Annual Projects Update







Q & A

