# Regional Park Improvement Funds Projects Allocation & Expenditure Semi-Annual Update

Presented to the Regional Park Improvement Fund Oversight Committee

October 18, 2018



### **BACKGROUND**

- RPIF is derived from Mission Bay Park lease revenue per City Charter Sec 55.2
- Charter was revised under Measure J passing on November 2016 to include:
  - First \$3.5M or 35%, whichever is greater above the threshold amount of \$20 million from the Mission Bay Leasehold revenues goes into the RPIF beginning in Fiscal Year 2019.
  - RPIF can only be used for capital improvements/deferred capital
- This presentation only covers on-going CIP's funded by the RPIF

### PROJECTS COMPLETED TO DATE

- Ocean Beach Comfort Station Replacement
- Museum of Man Roof Reconstruction
- Diamond Street Stairs Reconstruction
- Palisades Park Comfort Station
- Pescadero Street Stairs Reconstruction
- California Tower Electric Room Relocation
- Los Peñasquitos Ranger Station
- Balboa Park Hall of Nations Foundation Reconstruction
- Jas Arnold Trail For All People
- Coastal Beach Access Project
- Chicano Park Comfort Station Replacement
- Museum of Art Elevator Modernization

### OLD MISSION DAM PRESERVATION S-00611

- Managed by P&R Department
- Scope
  - Completion of the 5 year Mitigation, Monitoring & Reporting Program previously required by the 2008 dredging of the historic dam
- Financial
  - Total Cost \$ 0.918M
  - RPIF Allocation = \$0.315M (FY10)
- Status
  - Extended 5 yr mitigation monitoring due to contractor default
  - Acquiring approvals for permitting longterm dredging
  - Mitigation to Complete in FY20
  - Negotiation is in progress with resource agencies for final sign off





## MISSION TRAILS REGIONAL PARK MULTI TRAIL SYSTEM S-10066

- Managed by P&R Department
- Scope
  - Construction of approx. 5,000 LF of new trail & the rehab of approx. 3,500 LF of existing trail
- Financial
  - Total Cost \$0.20M
  - RPIF Allocation: \$0.20M (FY11)
- Status
  - Thru Park Master Plan (MP) & Environmental Assessment
  - Work will be completed after completion of the Natural Resources MP & MP Update (both ready for public review in FY18)
  - Construction to complete in FY 20.



### COWLES MOUNTAIN TRAIL – MISSION TRAILS S-10065

- Managed by P&R Department
- Scope
  - Restoration of approximate
     2,000 FT of existing trail
- Financial
  - Total Cost: \$0.40M
  - RPIF Allocation: \$0.40M (FY11)
- Status
  - In Construction
  - Construction to complete in FY19





### COASTAL BEACH ACCESS PROJECTS B-14073

### Scope

- Repair and re-construction of 3 coastal access stairs:
  - Old Salt Pool in OB
  - Capri by the Sea in PB
  - Orchard Ave in OB

### Financial

- Total Cost: \$0.450M
- RPIF Allocation: \$0.435M (FY12)
- Due to 100-202 Coast Blvd. Emergency project, \$377,895 in funding was reallocated from project per Oversight Committee Action in FY17.
- RPIF of \$329,879 was added back to the project in FY17.
- RPIF of \$150,000 is being added in FY18.

#### Status

 Construction started and expected to complete in FY 19.





## CHOLLAS LAKE PLAYGROUND RENOVATIONS PHASE I S-14002

### Scope

 Replacement of existing playgrounds at Chollas Lake Park

### Financial

Total Cost: \$1.939M

RPIF Allocation: \$0.974M (FY12)

• \$0.300M (FY18)

### • Status:

 Construction started in FY18 and scheduled to complete in FY19.





### CALIFORNIA TOWER SEISMIC RETROFIT L-12003.2

### Scope

 The seismic retrofit of the California Tower to upgrade the structural protection & improve the public safety of the iconic SD landmark

### Financial


Total Cost: \$4.061M

RPIF Allocation: \$1.50M (FY13)

RPFI Allocation: \$0.65M (FY18)

### Status

 Construction to start in FY19 and to complete in FY20

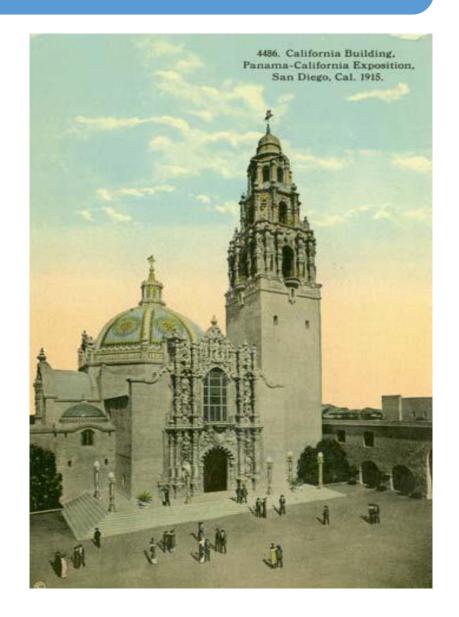

### MOHNIKE ADOBE & HAY BARN RESTORATION S-13008

### Scope

- Per Municipal Code, protect historic Mohnike Adobe Cultural Landscape on national register of historic places
- Phase 1 of the adobe home rehabilitation was completed in 2005

#### Financial

- Total Cost: \$2.697M
- RPIF Allocation: \$1M (FY13 & FY15)
- RPIF Funds of \$852,402 were reallocated to fund other projects
- RPFI Funds of \$1M was added back on the project (FY 2017)
- RPIF Funds of 633,651 were reallocated to fund an emergency project for Ladera Street Beach Stairways (B-19009).

- Design started and expected to complete in FY 20.
- Construction is scheduled to start in FY 20 and to complete in FY21.





## SUNSET CLIFFS NATURAL PARK HILLSIDE IMPROVEMENTS PHASE I (S-10091 / L-16001)

#### Scope

 Construction of new trails within the entire park including revegetation plan and removal of demolished housing.

#### Financial

Total Cost: \$1.0M (Phase IA)Total Cost: \$3.2M (Phase 1B)

#### RPIF Allocation:

- \$1.1M (FY14)
- \$1.0M (FY18)

- Phase 1A (L-16001.1) Construction completed in FY 16
- MMRP PH1A (L-16001.1) completes in 2021
- Phase 1B (L-16001.2) Design completed in FY18;
   Construction started in FY 18 and estimated to complete in FY19
- MMRP PH1B (L-16001.2) completes 2023



## SUNSET CLIFFS NATURAL PARK REMOVAL OF LOMALAND DR. AND LADERA ST. STRUCTURES PHASE 2 (L-14005.1)

### Scope

- The removal of Lomaland Dr. and Ladera St. structures; regrading and re-vegetating the sites; construction of overlooks and trails.
- Financial
  - Total Cost: \$835K
  - RPIF Allocation \$456K
- Status:
  - In Design
  - Environmental permits to complete FY 19
  - Construction to start FY 20
  - Construction to Complete FY 21



## SUNSET CLIFFS NATURAL PARK HILLSIDE DRAINAGE IMPROVEMENTS PHASE 3 (L-14005.2)

### Scope

 Design drainage solutions to arrest severe soil & coastal bluff erosion

### Financial

- Total Cost: \$4M (Phase I)
- RPIF Allocation (\$4M total):
  - \$1M (FY13)
  - \$1M (FY15)
- Status:
  - In Design
  - Construction to start in FY 20 & complete in FY 21



### LJ PARKWAY/ MT SOLEDAD EROSION CONTROL B-10089

### Scope

 Stabilize the eroding slope on the east side of La Jolla Parkway and reconstruct the failing brow ditches.

### Financial

Total Cost: \$2.58M

RPIF Allocations: \$500K (FY15)

- Design started & estimated to complete in FY19
- Construction to start in FY19 and to complete in FY20.





### JUNIPERO SERRA MUSEUM ADA IMPROVEMENTS S-15034

### Scope

- Assess & improve Junipero Serra
   Museum ADA deficiencies
- Financial
  - Total Cost: \$2.27M
  - RPIF Allocations:
    - \$0.5M (FY15)
    - \$0.5M (FY16)
    - \$0.5M (FY18)
- Status:
  - Design started in FY 18 and expected to complete in FY 20.
  - Construction to start in FY 20 & complete in FY 21





### BALBOA PARK WEST MESA COMFORT STATION REPLACEMENT S-15036

### Scope

 Replace two existing comfort stations with new facilities on the West Mesa of Balboa Park.

### Financial

Total Cost: \$1.89M

RPIF Allocation: \$1.0M (FY15)

RPIF Allocation: \$300K (FY16)

RPIF Allocation: \$200K (FY17)

#### Status

 Construction started in FY18 to complete FY19





### EB SCRIPPS PARK COMFORT STATION REPLACEMENT S-15035

- Scope
  - The replacement of the existing comfort station
- Financial
  - Total Cost: \$2.93M
  - RPIF Allocation:
    - \$0.250M (FY14)
    - \$0.700M (FY17)
- Status:
  - Construction to start FY19 and to complete FY21



### BALBOA PARK BUD KEARNS AQUATIC COMPLEX S-17000

### Scope

 Improvement to the pool mechanical systems to allow the recycling of the pool water, ADA path of travel and interior tenant improvement.

#### Financial

• Total Cost: \$1.544M

RPIF Allocation:

\$0.500M (FY17)

- Design phase started and expected to complete in FY19.
- Construction to start FY20 and complete in FY20





### CHOLLAS LAKE IMPROVEMENTS, PHASE 1 – CHOLLAS LAKE ELECTRICAL SERVICE L-18001.1

### Scope

 Extend SDG&E service to the park and provide services to the park buildings.



• Total Cost: \$750,000

RPIF Allocation:

• \$143,733K (FY18)

### • Status:

 Project is in preliminary design phase.





### BERMUDA AVE COASTAL ACCESS & SEAWALL REPAIRS B-17110

### Scope

 Replacement of eroded stairs and seawalls.

### Financial

Total Cost: \$1.40M

RPIF Allocation:

• \$0.384M (FY17)

#### • Status:

- Design phase started in FY18 and expected to complete in FY20.
- Construction phase to start in FY21 and complete in FY21.





### SANTA CRUZ AVE ACCESS STAIRS AND WALKWAY B-18027

### Scope

 Repair or replacement of stairs, walkways, and stabilization of the fill slope.

### Financial

- Total Cost: \$4,032,000
- RPIF Allocation:
  - \$0.425M (FY18)

- Project is in Preliminary Design Phase.
- Feasibility study is complete.





### NARRAGANSETT AVE ACCESS B-18026

- Scope
  - repair and replacement of the stairs
- Financial
  - Total Cost: TBD
  - RPIF Allocation:
    - \$0.375M (FY18)
- Status:
  - Project is in preliminary design.
  - Feasibility study is complete.





### CASA DE BALBOA FIRE ALARM B-17181

### Scope

 Replacement of the Fire Alarm Systems

#### Financial

Total Cost: \$1.588M

RPIF Allocation:

Allocation of \$804,699 in FY17.

 The amount of \$137,815 was transferred to S-18002 Torrey Pines South Golf Course Improvement Project in FY18.

- Design phase started and expected to complete in FY19.
- Construction to start in FY19 and to complete in FY20.



### LADERA ST BEACH ACCESS STAIRWAY B-19009

### Scope

 Emergency stabilization of the bluff that overhang the vertical face.

### Financial

Total Cost: \$1.8M

RPIF Allocation:

 Received a Regional Park Fund allocation of \$1,733,651 in Fiscal Year 2019.

- Project is currently on hold pending concurrence from California Coastal Commission.
- Construction to start in FY19.



### OB DOG BEACH ACCESSIBILITY IMPROVEMENT B-19000

### Scope

 ADA accessibility improvements to meet current ADA standard.

### Financial

• Total Cost: \$669,000

- RPIF Allocation:
  - Received a Regional Park Fund allocation of \$\$443,306 in Fiscal Year 2019.

- Design phase started in FY18 and expected to complete in FY19.
- Construction to start and complete in FY20.



### SEISMIC RETROFIT – MESEUM OF MAN L-12003.3

### Scope

 Retrofit the walls, provide stiffening columns to brace the walls and support the stone ornamentation on the south wall and investigations on the foundations.

### Financial

Total Cost: TBD

RPIF Allocation:

• \$0.40M (FY19)



Project is in preliminary design.



### TP SOUTH GOLF COURSE IMP RENOVATION S-18002

### Scope

 Improvements to irrigation, drainage, bunkers, tees, cart paths, and ADA upgrades of the South Course and the installation and demolition of a temporary turfed driving range on the North Course.

#### Financial

Total Cost: \$17M

RPIF Allocation:

• \$150K (FY18)

- Design Phase started in FY18 to complete in FY19
- Construction Phase expected to start in FY19 and complete in FY21





### Regional Park Improvement Fund Allocation and Expenditure Bi Annual Projects Update







### Q & A

