



THE CITY OF  
SAN DIEGO

► Airports  
► Bikeways  
► Bridges  
► Drainage Control & Flood Control Facilities  
► Libraries  
► Park & Recreation Centers  
► Police, Fire & Lifeguard Stations  
► Street Improvements  
► Street Lights & Traffic Signals  
► Utilities Undergrounding  
► Water & Sewer Facilities  
► Water & Sewer Pipelines



# City of San Diego Engineering & Capital Projects

## Water Main Replacement Group Job 3008: E-Newsletter #8

### E-Newsletter Series for the Harbor Drive Area

This is the 8th e-newsletter for Water Main Replacement Group Job 3008. The newsletter will be distributed weekly to keep the community informed about construction progress.

### Group Job 3008 Project Description

The water main replacement work for Group Job 3008 is well underway. Group Job 3008 consists of two sections - Group Job 532 and 533. Construction crews are now replacing the existing cast-iron mains that are nearly 60-years old and are at the end of their service life.

### The project will:

- replace 17,979 feet of 16" cast iron water mains
- improve service reliability
- minimize future water main breaks caused by aging pipes
- increase the size of existing pipes to better serve the area

**Total project cost is \$5,777,000.**

### Contact Information:

#### Water Department's 24-hour Emergency Services Hotline:


(619) 515-3525

#### Group Job Public Information Line:

(619) 533-4207

#### General FAQs:

[www.sandiego.gov/engineering-cip](http://www.sandiego.gov/engineering-cip)

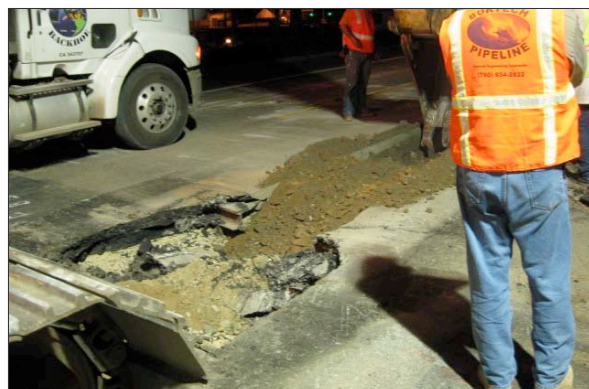

Installing 16" diameter pipe along N. Harbor Drive during night time construction hours.

### Upcoming Construction Activities

Currently, construction crews are working on Group Job 532 (see *Orange dotted line on map below*). The crew is working to minimize impacts to all those who travel in and out of this area.

### During the week of July 20 crews will:

#### Day work:

- Conduct potholing activities at the intersection of Broadway and N. Harbor Drive. (Potholing activities verify the location of existing utilities along the pipeline alignment. This includes excavating, back filling and recompacting excavated material.)

#### Night work:

- Install 16" diameter pipe (approx. 500' of pipe will be laid) along N. Harbor Drive up to Broadway.

#### Traffic Control:

Temporary road closure during night work will occur from 9 p.m. to 6 a.m. on N. Harbor Drive from Seaport Village Parking Lot to Broadway from July 20 -23.

### Construction Area Map: Water Main Replacement/Alignment



*"Working together to engineer a better tomorrow."*
