Act ID	Description	Rem Dur	Early Start	Early Finish
DESIGN PROGRAM				
D-1010	SDs, BUILDING SUBMITTAL (Arch, Struc, Mech,Elec)	5	25JUN07 A	13JUL07
D-1020	DEMOLITION PLANS	26	25JUN07 A	13AUG07
D-1030	DDs, BUILDING SUBMITTAL (Arch, Struc, Mech,Elec)	10	16JUL07	27JUL07
D-1040	CDs, BUILDING SUBMITTAL (Arch, Struc, Mech,Elec)	20	30JUL07	24AUG07
D-1100	PLAN CHECK REVIEW	5	27AUG07	31AUG07
D-1110	ISSUE REQUIRED PERMITTING	0		31AUG07
MILESTONE SUMMARY				
M-0020	BUILDING HEIGHT REDUCED TO 160' ELEVATION	0		16OCT07
M-0890	SUBSTANTIAL COMPLETION	0		17APR08
PROCUREMENT PROGRAM				
MANLIFT				
P-0000	AUTHORIZATION TO PROCEED	0	11JUL07 *	
P-0090	PROCURE MAN HOIST	2	11JUL07	12JUL07
P-0020	SECURE CRANE / MOBILIZATION	5	11JUL07 *	17JUL07
P-0070	STATE ELEV INSPECTION	15	11JUL07	31JUL07
P-0010	ENGINEER MAN HOIST TIE-BACK / RAMPS	5	13JUL07	19JUL07
P-0030	MAN HOIST FOUNDATIONS	5	13JUL07	19JUL07
P-0050	ERECT MAN HOIST	5	15AUG07 *	21AUG07
P-0060	MAN HOIST PRE-TESTING	3	22AUG07	24AUG07
P-0080	MAN HOIST CERTIFICATION	1	27AUG07	27AUG07
SUBCONTRACTOR BUYOUT				
P-5010	AWARD DEMO SUB-CONTRACT	7	14AUG07	22AUG07
P-5000	AWARD SUB-CONTRACTS	10	27AUG07	10SEP07
BUILDING CONSTRUCTION				
STRUCTURE				
0120	SAFE-OFF AND PROTECTION	5	28AUG07	04SEP07
0110	ELEVATOR SHUT DOWN & SALVAGE	10	28AUG07	11SEP07
0900	DEMO EXISTING ARCHITECTUAL FINISHES	10	05SEP07	18SEP07
0100	START STRUCTURAL DEMOLITION	0	19SEP07	
1000	DEMO EXISTING STRUCTURAL STEEL	20	19SEP07	16OCT07
1010	MODIFY EXISTING STRUCTURAL STEEL	20	17OCT07	13NOV07
1020	CONC DECKS & EQUIP PADS	10	14NOV07	29NOV07
EXTERIOR				
ROOF				
4734	ROOF CONSTRUCTION & ROOFING	45	30NOV07	06FEB08
4744	EXTERIOR SKIN GLAZING & SHEET METAL	30	21DEC07	06FEB08
INTERIOR				
11TH FLOOR				
L11-0000	COMPLETE INTERIOR FINISHES	45	07FEB08	10APR08
ELEVATORS				
ELEV-0510	CONSTRUCT ELEVATORS	40	07FEB08	03APR08
TESTING & COMMISSIONING				
TEST-4010	MECHANICAL EQUIP MODIFICATIONS	50	21DEC07	06MAR08
TEST-4020	START UP & CHECK-OUT BLDG SYSTEMS	20	07MAR08	03APR08
TEST-4000	BUILDING FINAL INSPECTIONS	10	04APR08	17APR08

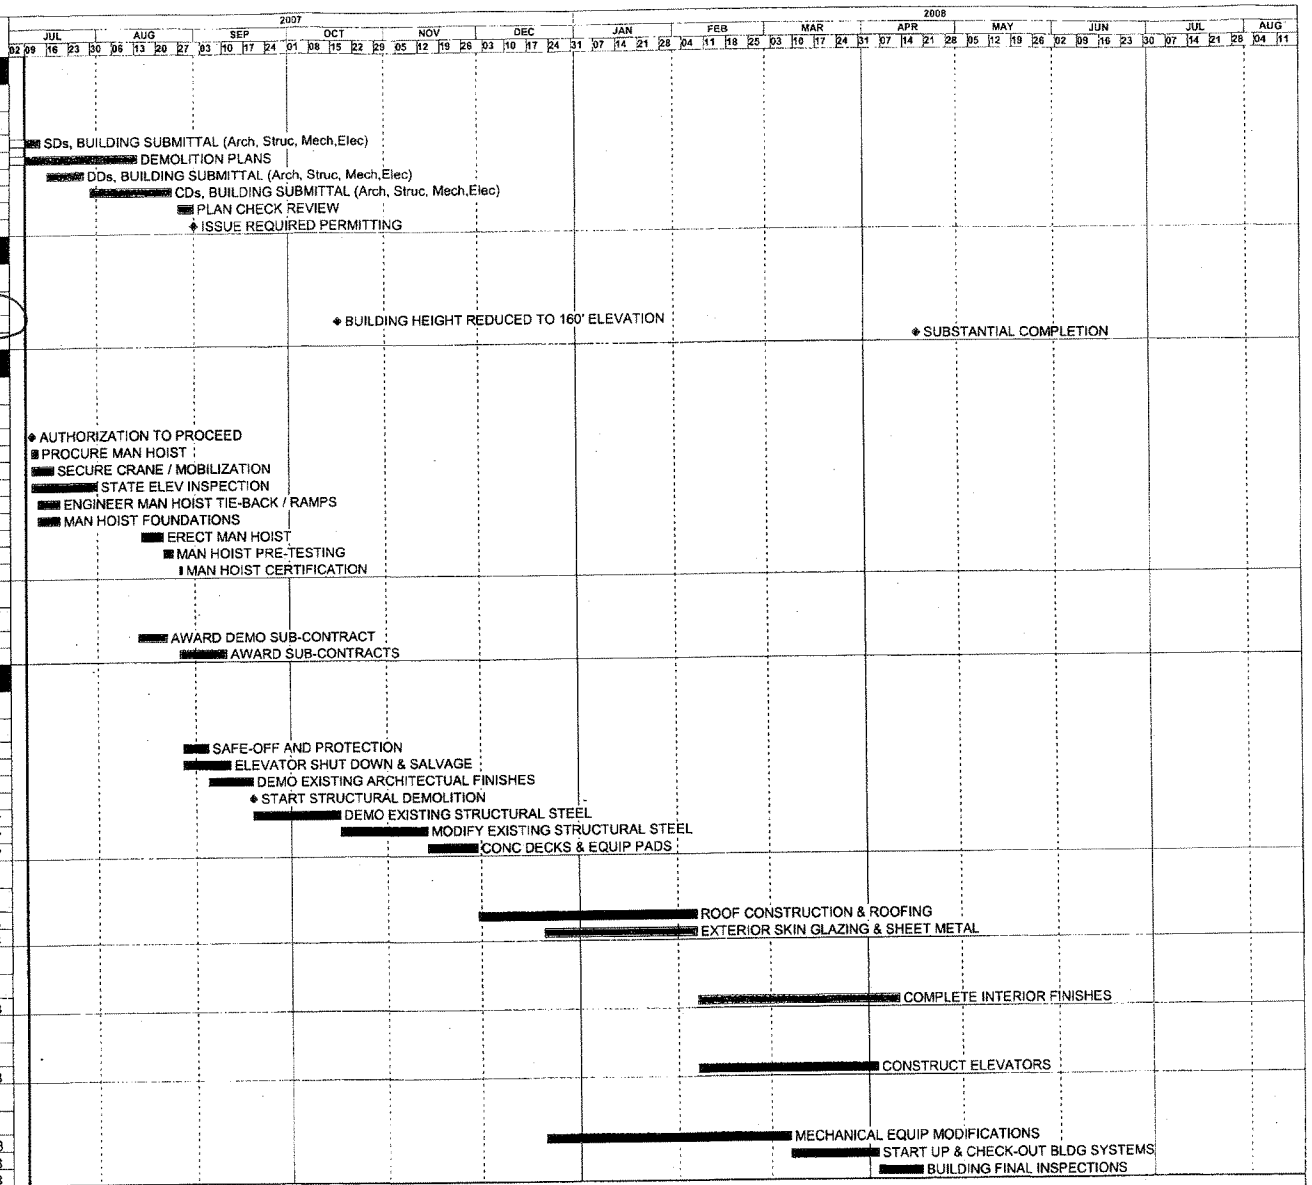

Start date	04MAR05
Finish date	17APR08
Date date	09JUL07
Run date	10JUL07
Page number	1A
Page count	1A

© Primavera Systems, Inc.

Early bar
Progress bar
Critical bar
Summary bar
Start milestone point
Finish milestone point

X20W

CONCEPTUAL SCHEDULE (Lower Bldg Height)
SUNROAD CENTRUM-12 FLR OFFICE BLDG
SWINERTON BUILDERS
