City of San Diego

CONTRACTOR'S NAME: Hazard Construction Company

ADDRESS: 10529 Vine Street, Lakeside, CA 92040

TELEPHONE NO.: 858-587-3600 EMAIL: phutchins@hazardcon.com

CITY CONTACT: Juan E. Espindola, Senior Contract Specialist, Email: JEEspindola@sandiego.gov

Phone No. (619) 533-4491

M. Gonzalez / R. Puertollano / M. L. Wenceslao

CONTRACT DOCUMENTS





FOR

EMERGENCY DESIGN AND CONSTRUCTION SERVICES FOR: 3405 KITE STREET STORM DRAIN EMERGENCY

VOLUME 1 OF 1

RFQ NO.:	K-18-1682-RFQ-3	
BID NO.:	K-22-2052-EMR-3	
SAP NO. (WBS/IO/CC):	B-21153	
CLIENT DEPARTMENT:	2116	
COUNCIL DISTRICT:	3	
PROJECT TYPE:	CA	

ENGINEER OF WORK

The engineering Specifications and Special Provisions contained herein have been prepared by or under the direction of the following Registered Engineer:

4 16h	10-20-21	Seal:	C 73246 EXP. (2/31/22) CIVIL CIVIL CIVIL
For City Engineer	Date		O'CAL.

OROFESSION

TABLE OF CONTENTS

DES	SCRIPTION	PAGE
•	General	4
•	Agreement	14
•	Performance Bond and Labor and Materialmen's Bond	18
•	Exhibit A – Drug-Free Workplace Certification	20
•	Exhibit B – ADA Compliance Certification	22
•	Exhibit C – Contractor Standards - Pledge of Compliance	24
•	Exhibit D – Equal Benefits Ordinance Certification	26
•	Exhibit E – Product Endorsement	28
•	Exhibit F – Affidavit of Disposal	30
•	Exhibit G – Non-Collusion Affidavit	32
•	Exhibit H – Contractor's Certification of Pending Actions	34
•	Exhibit I – Mandatory Disclosure of Business Interest Forms	36
•	Exhibit J – Forms	38
•	Exhibit K – Supplementary Special Provisions (SSP)	50
•	Exhibit L - Notice of Exemption	83
•	Exhibit M – Contractor's Compensation Rate Schedule	86
•	Exhibit N – Location Map	92
•	Exhibit O – Contractor's Notes for Emergency Projects	94
•	Exhibit P – Advanced Metering Infrastructure (AMI) Device Protection	98
•	Exhibit Q - Sample City Invoice	104
•	Exhibit R – Scope of Work	106

CITY OF SAN DIEGO, CALIFORNIA

GENERAL

1. DESCRIPTION OF WORK:

- **1.1.** The Work involves furnishing all labor, materials, equipment, services, and other incidental works and appurtenances for the purpose of designing and constructing this emergency project at the direction of the City Engineer.
- **1.2.** The Work consists of repair and reconstruction that includes but is not limited to a slope repair, sinkhole repair, and replacement of a failing 18-inch (CMP) corrugated metal pipe that is approximately 180-feet in length. The CMP pipe starts from a Type C curb inlet adjacent to 3405 Kite Street and traverses east within the City right-of-way and discharges to a cleanout located in front of 3410 Jackdaw Street.
- **1.3.** This solicitation is for a "Time-and-Materials" contract in accordance with the provisions set forth in 7-3.7, "Agreed Prices" of The WHITEBOOK.
- **1.4.** A time-and-materials contract provides for acquiring labor, material, equipment and services that shall be paid for in accordance with 2-8, "EXTRA WORK" of The GREENBOOK and WHITEBOOK and as modified by the Supplementary Special Provisions.
- **1.5.** The Design-Builder agrees to provide the required services for the terms and conditions noted in this contract and its exhibits. The agreement and other terms and conditions are included in this Design-Build Contract, The GREENBOOK, The WHITEBOOK, and the Supplementary Special Provisions (SSP).
- **1.6.** Any architectural firms, engineering firms, specialty consultants, or individuals retained by the City to assist in drafting the Project's preliminary design may not be eligible to participate in the competition with any Design-Build Entity. It is the responsibility of the Design-Build entity to obtain the required legal advice necessary to resolve such matters.

2. CONTRACTOR REGISTRATION AND ELECTRONIC REPORTING SYSTEM:

- **2.1. Prior** to the Award of the Contract or each Task Order, the Contractor must comply with the following registration requirements:
 - **2.1.1.** This project is subject to compliance monitoring and enforcement by the California Department of Industrial Relations (DIR). **Contractor and Subcontractor Registration Requirements** for compliance with those requirements are outlined in are outlined in paragraph 7.9. of these "General Instructions."
 - **2.1.2.** In addition, prior to award of the Contract or each Task Order, the Contractor and its Subcontractors and Suppliers **must** register with Prism®, the City's web-based contract compliance portal at:

https://pro.prismcompliance.com/default.aspx.

- **2.1.3.** The City may not award the contract until registration of all subcontractors and suppliers is complete. In the event this requirement is not met within the time frame specified in the Notice of Intent to Award letter, the City reserves the right to rescind the Notice of Award / Intent to Award and to make the award to the next responsive and responsible bidder / proposer.
- **3. EQUAL OPPORTUNITY:** For the City's Equal Opportunity Program requirements see Part 0 of the City of San Diego 2018 Whitebook and Exhibit J Forms.
 - **3.1.** The Design-Builders are encouraged to take positive steps to diversify and expand their subcontractor solicitation base and to offer contracting opportunities to all eligible certified Subcontractors in accordance with the City's EOCP requirements included in the Contract Documents.

3.2. Design-Builder's Work Force

- **3.2.1.** The Design-Builders shall submit with its Proposal a Work Force Report (EOC Form BB05) and prior to award of contract, the successful Design-Builder shall submit to the City's EOCP office an updated Work Force Report or an Equal Employment Opportunity (EEO) Plan.
- **3.2.2.** If under representations are noted in the Work Force Report when compared to County Labor Force Availability data, the Design-Builder shall submit an Equal Opportunity Plan. Any Equal Employment Opportunity Plan submitted shall include the elements as outlined in the EOCP Requirements included in The WHITEBOOK.
- **3.2.3.** The specified Equal Opportunity Contracting Program (EOCP) forms are available for download from the City's web site at:

http://www.sandiego.gov/eoc/forms

- 4. CONTRACT TIME: The Work including the Plant Establishment Period shall be completed within 260 Working Days from the date of issuance of the Notice to Proceed. Design shall be completed concurrent with construction and shall be completed within the first 70 Working Days of the contract.
- **5. CONTRACT PRICE**: The Engineer's Estimate of the Contract Price is **\$1,500,000**. The Contractor shall not perform Work that exceeds the Engineer's Estimate excluding Allowances without prior written notice from the City that sufficient additional funding has been secured.
- **6. LICENSE REQUIREMENT:** To be eligible for award of this contract, Prime contractor must possess the following licensing classification: **A**
- **7. PREVAILING WAGE RATES:** Pursuant to San Diego Municipal Code section 22.3019, construction, alteration, demolition, repair and maintenance work performed under this Contract is subject to State prevailing wage laws. For construction work performed under this

Contract cumulatively exceeding \$25,000 and for alteration, demolition, repair and maintenance work performed under this Contract cumulatively exceeding \$15,000, the Contractor and its subcontractors shall comply with State prevailing wage laws including, but not limited to, the requirements listed below.

- 7.1. Compliance with Prevailing Wage Requirements. Pursuant to sections 1720 through 1861 of the California Labor Code, the Contractor and its subcontractors shall ensure that all workers who perform work under this Contract are paid not less than the prevailing rate of per diem wages as determined by the Director of the California Department of Industrial Relations (DIR). This includes work performed during the design and preconstruction phases of construction including, but not limited to, inspection and land surveying work.
 - **7.1.1.** Copies of such prevailing rate of per diem wages are on file at the City and are available for inspection to any interested party on request. Copies of the prevailing rate of per diem wages also may be found at http://www.dir.ca.gov/OPRL/DPreWageDetermination.htm. Contractor and its subcontractors shall post a copy of the prevailing rate of per diem wages determination at each job site and shall make them available to any interested party upon request.
 - **7.1.2.** The wage rates determined by the DIR refer to expiration dates. If the published wage rate does not refer to a predetermined wage rate to be paid after the expiration date, then the published rate of wage shall be in effect for the life of this Contract. If the published wage rate refers to a predetermined wage rate to become effective upon expiration of the published wage rate and the predetermined wage rate is on file with the DIR, such predetermined wage rate shall become effective on the date following the expiration date and shall apply to this Contract in the same manner as if it had been published in said publication. If the predetermined wage rate refers to one or more additional expiration dates with additional predetermined wage rates, which expiration dates occur during the life of this Contract, each successive predetermined wage rate shall apply to this Contract on the date following the expiration date of the previous wage rate. If the last of such predetermined wage rates expires during the life of this Contract, such wage rate shall apply to the balance of the Contract.
- **7.2. Penalties for Violations.** Contractor and its subcontractors shall comply with California Labor Code section 1775 in the event a worker is paid less than the prevailing wage rate for the work or craft in which the worker is employed. This shall be in addition to any other applicable penalties allowed under Labor Code sections 1720 1861.
- **7.3. Payroll Records.** Contractor and its subcontractors shall comply with California Labor Code section 1776, which generally requires keeping accurate payroll records, verifying and certifying payroll records, and making them available for inspection. Contractor shall require its subcontractors to also comply with section 1776. Contractor and its subcontractors shall submit weekly certified payroll records online via

the City's web-based Labor Compliance Program. Contractor is responsible for ensuring its subcontractors submit certified payroll records to the City.

- **7.3.1.** Contractor and their subcontractors shall also furnish records specified in Labor Code section 1776 directly to the Labor Commissioner in the manner required by Labor Code section 1771.4.
- **7.4. Apprentices.** Contractor and its subcontractors shall comply with California Labor Code sections 1777.5, 1777.6 and 1777.7 concerning the employment and wages of apprentices. Contractor is held responsible for the compliance of their subcontractors with sections 1777.5, 1777.6 and 1777.7.
- **7.5. Working Hours.** Contractor and their subcontractors shall comply with California Labor Code sections 1810 through 1815, including but not limited to: (i) restrict working hours on public works contracts to eight hours a day and forty hours a week, unless all hours worked in excess of 8 hours per day are compensated at not less than 1½ times the basic rate of pay; and (ii) specify penalties to be imposed on contractors and subcontractors of \$25 per worker per day for each day the worker works more than 8 hours per day and 40 hours per week in violation of California Labor Code sections1810 through 1815.
- **7.6. Required Provisions for Subcontracts.** Contractor shall include at a minimum a copy of the following provisions in any contract they enter into with a subcontractor: California Labor Code sections 1771, 1771.1, 1775, 1776, 1777.5, 1810, 1813, 1815, 1860 and 1861.
- **7.7. Labor Code Section 1861 Certification.** Contractor in accordance with California Labor Code section 3700 is required to secure the payment of compensation of its employees and by signing this Contract, Contractor certifies that "I am aware of the provisions of Section 3700 of the California Labor Code which require every employer to be insured against liability for workers' compensation or to undertake self-insurance in accordance with the provisions of that code, and I will comply with such provisions before commencing the performance of the work of this Contract."
- **7.8. Labor Compliance Program**. The City has its own Labor Compliance Program authorized in August 2011 by the DIR. The City will withhold contract payments when payroll records are delinquent or deemed inadequate by the City or other governmental entity, or it has been established after an investigation by the City or other governmental entity that underpayment(s) have occurred. For questions or assistance, please contact the City of San Diego's Equal Opportunity Contracting Department at 619-236-6000.
- **7.9. Contractor and Subcontractor Registration Requirements.** This project is subject to compliance monitoring and enforcement by the DIR. A contractor or subcontractor shall not be qualified to bid on, be listed in a bid or proposal, subject to the requirements of section 4104 of the Public Contract Code, or engage in the performance of any contract for public work, unless currently registered and qualified to perform public work pursuant

to Labor Code section 1725.5 It is not a violation of this section for an unregistered contractor to submit a bid that is authorized by Section 7029.1 of the Business and Professions code or by Section 10164 or 20103.5 of the Public Contract Code, provided the contractor is registered to perform public work pursuant to Section 1725.5 at the time the contract is awarded.

- **7.9.1.** A Contractor's inadvertent error in listing a subcontractor who is not registered pursuant to Labor Code section 1725.5 in response to a solicitation shall not be grounds for filing a bid protest or grounds for considering the bid non-responsive provided that any of the following apply: (1) the subcontractor is registered prior to bid opening; (2) within twenty-four hours after the bid opening, the subcontractor is registered and has paid the penalty registration fee specified in Labor Code section 1725.5; or (3) the subcontractor is replaced by another registered subcontractor pursuant to Public Contract Code section 4107.
- **7.9.2.** By submitting a bid or proposal to the City, Contractor is certifying that he or she has verified that all subcontractors used on this public work project are registered with the DIR in compliance with Labor Code sections 1771.1 and 1725.5, and Contractor shall provide proof of registration for themselves and all listed subcontractors to the City at the time of bid or proposal due date or upon request.
- **7.10. Stop Order.** For Contractor or its subcontractors engaging in the performance of any public work contract without having been registered in violation of Labor Code sections 1725.5 or 1771.1, the Labor Commissioner shall issue and serve a stop order prohibiting the use of the unregistered contractors or unregistered subcontractor(s) on ALL public works until the unregistered contractor or unregistered subcontractor(s) is registered. Failure to observe a stop order is a misdemeanor.
- **7.11. List of all Subcontractors.** The Contractor shall provide the list of subcontractors (regardless of tier), along with their DIR registration numbers, utilized on this Contract prior to any work being performed; and the Contractor shall provide a complete list of all subcontractors with each invoice. Additionally, Contractor shall provide the City with a complete list of all subcontractors (regardless of tier) utilized on this contract within ten working days of the completion of the contract, along with their DIR registration numbers. The City shall withhold final payment to Construction Management Professional until at least thirty (30) days after this information is provided to the City.
- **7.12. Exemptions for Small Projects.** There are limited exemptions for installation, alteration, demolition, or repair work done on projects of \$25,000 or less. The Contractor shall still comply with Labor Code sections 1720 et. seq. The only recognized exemptions are listed below:
 - **7.12.1.** Registration. The Contractor will not be required to register with the DIR for small projects. (Labor Code section 1771.1

- **7.12.2.** Certified Payroll Records. The records required in Labor Code section 1776 shall be required to be kept and submitted to the City of San Diego, but will not be required to be submitted online with the DIR directly. The Contractor will need to keep those records for at least three years following the completion of the Contract. (Labor Code section 1771.4).
- **7.12.3.** List of all Subcontractors. The Contractor shall not be required to hire only registered subcontractors and is exempt from submitting the list of all subcontractors that is required in section 7.11. above. (Labor code section 1773.3).
- **8. REFERENCE STANDARDS**: Except as otherwise noted or specified, the Work shall be completed in accordance with the following standards:

Title	Edition	Document Number
Standard Specifications for Public Works Construction ("The GREENBOOK") http://www.greenbookspecs.org/	2018	PWPI010119-01
City of San Diego Standard Specifications for Public Works Construction ("The WHITEBOOK")* https://www.sandiego.gov/ecp/edocref/greenbook	2018	PWPI010119-02
City of San Diego Standard Drawings* https://www.sandiego.gov/ecp/edocref/standarddraw	2018	PWPI010119-03
Citywide Computer Aided Design and Drafting (CADD) Standards https://www.sandiego.gov/ecp/edocref/drawings	2018	PWPI010119-04
California Department of Transportation (CALTRANS) Standard Specifications https://dot.ca.gov/programs/design/ccs-standard-plans-and-standard-specifications	2018	PWPI030119-05
CALTRANS Standard Plans https://dot.ca.gov/programs/design/ccs-standard-plans-and-standard-specifications	2018	PWPI030119-06
California Manual on Uniform Traffic Control Devices Revision 6 (CA MUTCD Rev 6) https://dot.ca.gov/programs/safety-programs/camutcd/camutcd-files	2014	PWPI060121-10

NOTE: *Available online under Engineering Documents and References at:

https://www.sandiego.gov/ecp/edocref/
*Electronic updates to the Standard Drawings may also be found in the link above

9. INSURANCE REQUIREMENTS:

- **9.1.** All certificates of insurance and endorsements required by the contract are to be provided upon issuance of the City's Notice of Intent to Award letter.
- **9.2.** Refer to sections within 5-4, "INSURANCE" of the Supplementary Special Provisions (SSP) for the insurance requirements which must be met.

10. SUBCONTRACTOR INFORMATION:

LISTING OF SUBCONTRACTORS. In accordance with the requirements provided in the "Subletting and Subcontracting Fair Practices Act" of the California Public Contract Code, the Bidder shall provide the **NAME** and **ADDRESS** of each Subcontractor who will perform work, labor, render services or who specially fabricates and installs a portion [type] of the work or improvement, in an amount in excess of 0.5% of the Contractor's total Bid. The Bidder shall also state within the description, whether the subcontractor is a CONSTRUCTOR, CONSULTANT or SUPPLIER. The Bidder shall state the **DIR REGISTRATION NUMBER** for all subcontractors and shall further state within the description, the **PORTION** of the work which will be performed by each subcontractor under this Contract. The Contractor shall list only one Subcontractor for each portion of the Work. The DOLLAR VALUE of the total Bid to be performed shall be stated for all subcontractors listed. Failure to comply with this requirement may result in the Bid being rejected as **non-responsive** and ineligible for award. The Bidder's attention is directed to the Special Provisions - Section 3-2, "SELF-PERFOMANCE", which stipulates the percent of the Work to be performed with the Bidders' own forces. The Bidder shall list all SLBE, ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which Bidders are seeking recognition towards achieving any mandatory, voluntary (or both) subcontracting participation goals.

Additionally, pursuant to California Senate Bill 96 and in accordance with the requirements of Labor Code sections 1771.1 and 1725.5, by submitting a bid or proposal to the City, Contractor is certifying that he or she has verified that all subcontractors used on this public work project are registered with the California Department of Industrial Relations (DIR). The Bidder shall provide the name, address, license number, DIR registration number of any Subcontractor – regardless of tier - who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement pursuant to the contract.

- 10.2. LISTING OF SUPPLIERS. Any Bidder seeking the recognition of Suppliers of equipment, materials, or supplies obtained from third party Suppliers towards achieving any mandatory or voluntary (or both) subcontracting participation goals shall provide, at a minimum, the NAME, LOCATION (CITY), DIR REGISTRATION NUMBER and the DOLLAR VALUE of each supplier. The Bidder will be credited up to 60% of the amount to be paid to the Suppliers for materials and supplies unless vendor manufactures or substantially alters materials and supplies, in which case, 100% will be credited. The Bidder is to indicate within the description whether the listed firm is a supplier or manufacturer. If no indication is provided, the listed firm will be credited at 60% of the listed dollar value for purposes of calculating the Subcontractor Participation Percentage.
- **11. SUBMITTAL OF "OR EQUAL" ITEMS**: See 4-6, "TRADE NAMES" in The WHITEBOOK and as amended in the SSP.

- **SUBCONTRACT LIMITATIONS**: The Bidder's attention is directed to the GREENBOOK and Special Provisions Section 3-2, "SELF-PERFORMANCE" which requires the Contractor to perform not less than the amount therein stipulated with its own forces. Failure to comply with these requirements shall render the Bid non-responsive and ineligible for award.
- 13. PLANS AND SPECIFICATIONS: When provided by the City, questions about the meaning or intent of the Contract Documents relating to the scope of Work and technical nature shall be directed to the City's Project Manager prior to commencement of work. Interpretations or clarifications considered necessary by the City in response to such questions will be issued in writing. Oral and other interpretations or clarifications will be without legal effect. Any questions related to this proposal shall be addressed to the Purchasing & Contracting Department, Public Works Division, 525 B Street, Suite 750, San Diego, CA 92101, Telephone No. (619) 533-3450.
- **14. SAN DIEGO BUSINESS TAX CERTIFICATE:** All Contractors, including Subcontractors, not already having a City of San Diego Business Tax Certificate for the work contemplated shall secure the appropriate certificate from the City Treasurer, Civic Center Plaza, first floor, before the Contract can be executed.
- **15. PROPOSAL FORMS:** The signature of each person signing may be in longhand or in electronic format as specified by the City. The Contractor shall furnish evidence of its corporate existence and evidence that the officer signing the Contract and bond for the corporation is duly authorized to do so.
 - **15.1.** The Bidder, by submitting electronically, agrees to and certifies under penalty of perjury under the laws of the State of California, that the certification, forms and affidavits submitted as part of this contract are true and correct.
- 16. CITY'S RIGHTS RESERVED: The City reserves the right to cancel this request for proposal at any time, and further reserves the right to reject submitted proposals, without giving any reason for such action, at its sole discretion and without liability. Costs incurred by the Contractor as a result of preparing its proposal shall be the sole responsibility of the Contractor.

17. AWARD OF CONTRACT OR REJECTION OF PROPOSALS:

- **17.1.** This contract may be awarded to a contractor selected from the City's as-needed emergency contractors list or may be awarded to another contractor in case the list of available emergency contractors list is exhausted.
- **17.2.** The City reserves the right to reject the proposal from the emergency list-selected contractor and request a proposal from the next contractor on the list when such rejection is in the best interests of the City.
- **18. THE CONTRACT**: The Contractor shall execute a written contract with the City of San Diego and furnish good and approved bonds and insurance documents specified in 1-7.2, "Contract Bonds", and 5-4, "INSURANCE" within **3 Working Days** after receipt by the Contractor of a form of contract for execution unless an extension of time is granted to the Contractor in writing. Bonds shall be in amount of the Contract Price for the Work included in the Bid.

The Contract shall be made in the form adopted by the City, which includes the provision that no claim or suit whatsoever shall be made or brought by Contractor against any officer, agent, or employee of the City for or on account of anything done or omitted to be done in connection with this contract, nor shall any such officer, agent, or employee be liable hereunder. If the Contractor fails to enter into the contract as herein provided, the award may be annulled. An award may be made to the next contractor on the shortlist or in the case the emergency contractor's list is exhausted to any other responsive contractor on a sole-source basis who shall fulfill every stipulation embraced herein as if it were the party to whom the first award was made.

- 19. **EXAMINATION OF PLANS, SPECIFICATIONS, AND SITE OF WORK:** The Contractor shall examine carefully the Project Site, the Plans and Specifications, other materials as described in the Special Provisions, Section 3-9, "TECHNICAL STUDIES AND SUBSURFACE DATA", and the proposal forms. The signing of the Contract shall be conclusive evidence that the Contractor has investigated and is satisfied as to the conditions to be encountered, as to the character, quality, and scope of Work, the quantities of materials to be furnished, and as to the requirements of the Contract Documents.
- **20. CITY STANDARD PROVISIONS.** This contract is subject to the following standard provisions. See The WHITEBOOK for details.
 - **20.1.** The City of San Diego Resolution No. R-277952 adopted on May 20, 1991 for a Drug-Free Workplace.
 - **20.2.** The City of San Diego Resolution No. R-282153 adopted on June 14, 1993 related to the Americans with Disabilities Act.
 - **20.3.** The City of San Diego Municipal Code §22.3004 for Pledge of Compliance.
 - **20.4.** The City of San Diego's Labor Compliance Program and the State of California Labor Code §§1771.5(b) and 1776.
 - **20.5.** Sections 1777.5, 1777.6, and 1777.7 of the State of California Labor Code concerning the employment of apprentices by contractors and subcontractors performing public works contracts.
 - **20.6.** The City's Equal Benefits Ordinance (EBO), Chapter 2, Article 2, Division 43 of The San Diego Municipal Code (SDMC).
 - **20.7.** The City's Information Security Policy (ISP) as defined in the City's Administrative Regulation 90.63.
- 21. **DESIGN SUBMITTALS:** The City's review of the Design-Builder's Design Submittals shall not relieve the Design-Builder from its responsibilities under the Contract, or be deemed to be an acceptance or waiver by City of any deviation from, or of the Design-Builder's failure to comply with, any provision or requirement of the Contract Documents, unless such deviation or failure has been identified as such in writing in the document submitted for acceptance by the Design-Builder and accepted by City. Where approval or acceptance by City is required, it is understood to be general approval only, and does not relieve the Design-Builder of

responsibility for complying with all applicable laws and good professional practices as the Design-Builder shall be the Engineer of Record.

22. WRITTEN AUTHORIZATION: Prior to performing any Professional Services in connection with the Project, the Contractor shall obtain from the City a written authorization to proceed. Further, throughout the term of this Contract, the Contractor shall immediately advise the City in writing of any anticipated change in the scope of services [Section 1 - Description of Work], compensation and rate schedule [Exhibit M], or Time Schedule [Section 4 - Contract Time], and shall obtain the City's written consent to the change prior to making any changes. In no event shall the City's consent be construed to relieve the Contractor from its duty to render all Professional Services in accordance with applicable laws and accepted industry standards.

AGREEMENT FOR EMERGENCY DESIGN AND CONSTRUCTION SERVICES BETWEEN

THE CITY OF SAN DIEGO AND

HAZARD CONSTRUCTION COMPANY

This Emergency Design and Construction Services Agreement (Agreement) is made and entered between THE CITY OF SAN DIEGO, herein called "City" and **Hazard Construction Company** herein called "Contractor", for the purpose of designing (when required) and performing emergency construction services for **3405 Kite Street Storm Drain Emergency**, Bid No. **K-22-2052-EMR-3**, in the amount of **(\$1,500,000)** at the direction of the City Engineer. The City and the Contractor are referred to herein as the "Parties."

RECITALS

- A. The City desires to construct the emergency project identified in Section 1, Description of Work.
- B. The City desires to contract with a single entity for Emergency Construction Services, as set forth in this agreement.
- C. The City had previously issued a Request for Qualifications (RFQ), via **RFQ K-18-1682-RFQ-3**, for on-call emergency construction services.
- D. In accordance with this RFQ, Contractors submitted Statements of Qualifications (SOQ) for these services from which the City established a pre-qualified list of the most highly qualified contractors to perform emergency construction services as directed by the City.
- E. In accordance with said RFQ, the Contractor submitted an SOQ and is prepared to enter into this agreement.
- F. The City has selected the Contractor from the City's list of on-call contractors to perform, either directly or with Subcontracts hereinafter defined, the design, engineering, and construction services set forth in this agreement and the Contract Documents.
- G. The Contractor is ready, willing, and able to perform the emergency design and construction services required as specified in the Scope of Work and Services section of this agreement and in accordance with the terms and conditions of this agreement and under the direction of the Engineer.

In consideration of the above recitals and the mutual covenants and conditions set forth herein, and for good and valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the Parties hereby set forth their mutual covenants and understandings as follows:

AGREEMENT

- A. The above referenced recitals are true and correct and are incorporated into this agreement by this reference.
- B. Exhibits referenced in this agreement are incorporated into the Agreement by this reference.
- C. For such performances, the City shall pay to Contractor the amounts set forth at the times and in the manner and with such additions or deductions as are provided for in this contract, and the Contractor shall accept such payment in full satisfaction of all claims incident to such performances.
- D. No claim or suit whatsoever shall be made or brought by Contractor against any officer, agent, or employee of the City for or on account of anything done or omitted to be done in connection with this contract, nor shall any such officer, agent, or employee be liable hereunder.
- E. This agreement incorporates the Standard Specifications for Public Works Construction (The 2018 GREENBOOK), including those amendments set forth in the City of San Diego Supplement (The 2018 WHITEBOOK). All changes, additions, or both are stated herein and all other provisions remain unchanged.
- F. The Contractor shall comply with City's Equal Opportunity Contracting Program Requirements set forth in the Contract Documents. See The WHITEBOOK Part 0.
- G. The Contractor, including Subcontractors, not already having a City of San Diego Business Tax Certificate for the work contemplated shall secure the appropriate certificate from the City Treasurer, Civic Center Plaza, first floor, before the Agreement can be executed.
- H. The Contractor shall ensure that all Subcontractors complete a Pledge of Compliance attesting under penalty of perjury that they complied with the requirements of this section. The Contractor shall include in each subcontract agreement, language which requires Subcontractors to abide by the provisions of City Municipal Code §22.3004.
- I. The Contractor's attention is directed to the provisions of the State of California Labor Code §1776 (Stats. 1978, Ch. 1249). The Contractor shall be responsible for the compliance with these provisions by Subcontractors.
- J. This contract is effective as of <u>the date the City issued the Contractor a written notice to proceed (NTP)</u>, or the date of the last signatory below, whichever occurred first.
- K. The Contractor shall complete the work to be performed under this agreement and shall achieve Acceptance within the allowed number of Working Days from the NTP as specified in the Notice of Award, unless authorized otherwise by the Engineer. Time is of essence for the completion of the Work and the Project has critical milestones to be met as listed in the Notice of Award.
- L. During the final design process (if any), if the Contractor modifies the Project such that a revision of the environmental document is required, the Contractor shall be responsible for all work required for implementing a revision, including preparation of revised documentation and

coordination with City staff. Work shall not proceed on the project until the environmental requirements are met to the satisfaction of the City. There shall be no additional time allowed in the contract for processing and approval of revised permit documents.

- M. Prior to NTP or as required by the City, the Contractor shall:
 - 1. File surety bonds with the City to be approved by the City in the amounts and for the purposes noted in the Notice Inviting Bids and
 - 2. Obtain the required insurance in accordance with 5-4, "INSURANCE" and any additional insurance as may be specified in the Supplemental Special Provisions.

IN WITNESS WHEREOF, this Agreement is executed by the City of San Diego, acting by and through its Mayor or designee, pursuant to the emergency contract provisions of City Charter §94 authorizing such execution, and by the Contractor.

THE	CITY	OF	SAN	DIEGO
-----	------	----	-----	-------

APPROVED AS TO FORM

0.	Mara W. Elliott, City Attorney
By Styrkes Camain	By Illichell Rynau
Print Name: Stephen Samara Principal Contract Specialist Purchasing & Contracting Department	Print Name: Multer Man Deputy City Attorney
Date: 1/7/2022	Date: 2/1/22
CONTRACTOR	, ,
By	
Print Name: JASON A. MORDHORST, PHESE	DEN7
Title: HAZARD CONSTRUCTION COMPA	NY
Date: 10/29/21	
City of San Diego License No.: 81998000	961

State Contractor's License No.: 750542

Secretary's Certificate Hazard Construction Company

The undersigned, Emmanuel C. Gavino, Secretary of Hazard Construction Company, a California Corporation, (the "Corporation"), does hereby certify that the following are true and complete resolutions which were unanimously adopted at the annual meeting of the Board of Directors of the Corporation on the fifth day of April 2021, and that such resolutions have not been amended or modified and continue to be in full force and effect as of the fifth day of April 2021:

RESOLVED, that the Corporation execute and deliver certain contracts in the form required.

FURTHER RESOLVED, that the President, or the Executive Vice President, or in their absence, the Vice President, or in their absence, the Secretary/Chief Financial Officer, be and hereby is authorized and empowered in the name and on behalf of this Corporation to execute contracts and to deliver the contracts on behalf of the Corporation and to do and perform all acts and things which he deems to be necessary or appropriate to carry out the terms of the contracts, including, but not limited to executing and delivering all agreements and documents contemplated by the contracts.

In witness whereof, I have hereunder set my hand as Secretary of the above Corporation this fifth day of April 2021.

Secretary

PERFORMANCE BOND, LABOR AND MATERIALMEN'S BOND

FAITHFUL PERFORMANCE BOND AND LABOR AND MATERIALMEN'S BOND:

Hazard Construction Company , a corporation, as principal, and Nationwide Mutual Insurance Company , a corporation authorized to do business in the State of California, as Surety, hereby obligate themselves, their successors and assigns, jointly and severally, to The City of San Diego a municipal corporation in the sum of One Million Five Hundred Thousand Dollars and Zero Cents (\$1,500,000.00) for the faithful performance of the annexed contract, and in the sum of One Million Five Hundred Thousand Dollars and Zero Cents (\$1,500,000.00)

Conditions:

If the Principal shall faithfully perform the annexed contract with the City of San Diego, California, then the obligation herein with respect to a faithful performance shall be void; otherwise it shall remain in full force.

for the benefit of laborers and materialmen designated below.

If the Principal shall promptly pay all persons, firms and corporations furnishing materials for or performing labor in the execution of this contract, and shall pay all amounts due under the California Unemployment Insurance Act then the obligation herein with respect to laborers and materialmen shall be void; otherwise it shall remain in full force.

The obligation herein with respect to laborers and materialmen shall inure to the benefit of all persons, firms and corporations entitled to file claims under the provisions of Article 2. Claimants, (iii) public works of improvement commencing with Civil Code Section 9100 of the Civil Code of the State of California.

Changes in the terms of the annexed contract or specifications accompanying same or referred to therein shall not affect the Surety's obligation on this bond, and the Surety hereby waives notice of same.

The Surety shall pay reasonable attorney's fees should suit be brought to enforce the provisions of this bond.

The Surety expressly agrees that the City of San Diego may reject any contractor or subcontractor which may be proposed by Surety in fulfillment of its obligations in the event of default by the Principal.

The Surety shall not utilize the Principal in completing the improvements and work specified in the Agreement in the event the City terminates the Principal for default.

PERFORMANCE BOND, LABOR AND MATERIALMEN'S BOND (continued)

THE CITY OF SAN DIEGO	APPROVED AS TO FORM
By Styrkes Camain	Mara W. Elliott, City Attorney By Michelle Lynan
Print Name: Stephen Samara Principal Contract Specialist Purchasing & Contracting Department	Print Name: Muhelle Lyman Deputy City Attorney
Date:	Date: 1/26/2022
CONTRACTOR Hazard Construction Company By:	SURETY Nationwide Mutual Insurance Company By: Attornéey-In-Fact
Print Name: Jason A. Mordhorst, President	Print Name: Chanel Asfaw, Attorney-in-Fact
Date: 10/29/21	Date: October 27, 2021
	8877 North Gainey Center Drive Scottsdale, AZ 85258 Local Address of Surety
	(480) 365-365-4037
	Local Phone Number of Surety
	\$12,000.00 Subject to adjustment base upon final contract price
	Premium
	7901040793
	Bond Number

CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT Civil Code § 1189 A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document, to which this certificate is attached, and not the truthfulness, accuracy or validity of that document, STATE OF CALIFORNIA County of San Diego OCT 2 7 2021 before me, Rachel A. Mullen Insert Name of Notary exactly as it appears on the official seal , Notary Public, personally appeared who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) RACHEL A. MULLEN acted, executed the instrument. COMM # 2350762 NOTARY PUBLIC-CALIFORNIA I certify under PENALTY OF PERJURY under the laws of SAN DIEGO COUNTY Commission Expires MARCH 10,2025 the State of California that the foregoing paragraph is true and correct. Witness my hand and official seal. Place Notary Seal Above — OPTIONAL -Though the information below is not required by law, it may prove valuable to persons relying on the document and could prevent fraudulent removal and reattachment of the form to another document. **Description of Attached Document** Title or Type of Document: Document Date: _____ Number of Pages: _____ Signer(s) Other Than Named Above: _____ Capacity(ies) Claimed by Signer(s) Signer's Name: Signer's Name: ☐ Individual ☐ Individual ☐ Corporate Officer — Title(s): _____ Corporate Officer — Title(s): ☐ Partner ☐ Limited ☐ General ☐ Partner ☐ Limited ☐ General ☐ Attorney in Fact RIGHT THUMBPRINT ☐ Attorney in Fact RIGHT THUMBPRINT ☐ Trustee ☐ Trustee OF SIGNER OF SIGNER Guardian or Conservator ☐ Guardian or Conservator Top of thumb here Top of thumb here Other: Signer is Representing: Signer is Representing:

Power of Attorney

KNOW ALL MEN BY THESE PRESENTS THAT:

Nationwide Mutual Insurance Company, an Ohio corporation

hereinafter referred to severally as the "Company" and collectively as "the Companies" does hereby make, constitute and appoint:

BILL BODENSTADT; CHANEL ASFAW; HANNAH MCGARVEY; KIM ACEVEDO; KYLE KING; TRAVIS PEARSON;

each in their individual capacity, its true and lawful attorney-in-fact, with full power and authority to sign, seal, and execute on its behalf any and all bonds and undertakings, and other obligatory instruments of similar nature, in penalties not exceeding the sum of

UNLIMITED

and to bind the Company thereby, as fully and to the same extent as if such instruments were signed by the duly authorized officers of the Company; and all acts of said Attorney pursuant to the authority given are hereby ratified and confirmed.

This power of attorney is made and executed pursuant to and by authority of the following resolution duly adopted by the board of directors of the Company:


"RESOLVED, that the president, or any vice president be, and each hereby is, authorized and empowered to appoint attorneys-in-fact of the Company, and to authorize them to execute and deliver on behalf of the Company any and all bonds, forms, applications, memorandums, undertakings, recognizances, transfers, contracts of indemnity, policies, contracts guaranteeing the fidelity of persons holding positions of public or private trust, and other writings obligatory in nature that the business of the Company may require; and to modify or revoke, with or without cause, any such appointment or authority; provided, however, that the authority granted hereby shall in no way limit the authority of other duly authorized agents to sign and countersign any of said documents on behalf of the Company."

"RESOLVED FURTHER, that such attorneys-in-fact shall have full power and authority to execute and deliver any and all such documents and to bind the Company subject to the terms and limitations of the power of attorney issued to them, and to affix the seal of the Company thereto; provided, however, that said seal shall not be necessary for the validity of any such documents."

This power of attorney is signed and sealed under and by the following bylaws duly adopted by the board of directors of the Company.

Execution of Instruments. Any vice president, any assistant secretary or any assistant treasurer shall have the power and authority to sign or attest all approved documents, instruments, contracts, or other papers in connection with the operation of the business of the company in addition to the chairman of the board, the chief executive officer, president, treasurer or secretary; provided, however, the signature of any of them may be printed, engraved, or stamped on any approved document, contract, instrument, or other papers of the Company.

IN WITNESS WHEREOF, the Company has caused this instrument to be sealed and duly attested by the signature of its officer the 20th day of August, 2021.



SEAL BOTTO ACCOUNTS OF

STATE OF NEW YORK COUNTY OF NEW YORK: ss

On this 20th day of August, 2021, before me came the above-named officer for the Company aforesaid, to me personally known to be the officer described in and who executed the preceding instrument, and he acknowledged the execution of the same, and being by me duly sworn, deposes and says, that he is the officer of the Company aforesaid, that the seal affixed hereto is the corporate seal of said Company, and the said corporate seal and his signature were duly affixed and subscribed to said instrument by the authority and direction of said Company.

ACKNOWLEDGMENT

Stephanie Rubino McArthur Notary Public, State of New York No. 02MC6270117 Qualified in New York County Commission Expires October 19, 2024 Scylarie Butuno Matte

My Commission Expires October 19, 2024

CERTIFICATE

I, Laura B. Guy, Assistant Secretary of the Company, do hereby certify that the foregoing is a full, true and correct copy of the original power of attorney issued by the Company; that the resolution included therein is a true and correct transcript from the minutes of the meetings of the boards of directors and the same has not been revoked or amended in any manner; that said Antonio C. Albanese was on the date of the execution of the foregoing power of attorney the duly elected officer of the Company, and the corporate seal and his signature as officer were duly affixed and subscribed to the said instrument by the authority of said board of directors; and the foregoing power of attorney is still in full force and effect.

IN WITNESS WHEREOF, I have hereunto subscribed my name as Assistant Secretary, and affixed the corporate seal of said Company this 27th day of October _______, 2021 .

Assistant Secretary

CALIFORNIA ALL-PURPOSE ACKNOWLEDGMENT

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document, to which this certificate is attached, and not the truthfulness, accuracy or validity of that document.

State of <u>California</u>	
County of San Diego	
On October 29, 2021 before me, _	Apryle Briede, Notary Public
Date	NAME, TITLE OF OFFICER - E.G. AJANE DOE, NOTARY PUBLIC
personally appeared	Jason A. Mordhorst
	NAME(S) OF SIGNER(S)

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies) and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

(SEAL)

APRYLE BRIEDE
Notary Public - California
San Diego County
Commission # 2246886
My Comm. Expires Jul 17, 2022

EXHIBIT A

DRUG-FREE WORKPLACE CERTIFICATION

CONTRACTOR CERTIFICATION

DRUG-FREE WORKPLACE

I hereby certify that I am familiar with the requirements of San Diego City Council Policy No. 100-17 regarding Drug-Free Workplace as outlined in the WHITEBOOK, Section 5-1.3, "Drug-Free Workplace", of the project specifications, and that;

This company_has in place a drug-free workplace program that complies with said policy. I further certify that each subcontract agreement for this project contains language which indicates the subcontractor's agreement to abide by the provisions of subdivisions a) through c) of the policy as outlined.

EXHIBIT B

AMERICANS WITH DISABILITIES ACT (ADA) COMPLIANCE CERTIFICATION

CONTRACTOR CERTIFICATION

AMERICANS WITH DISABILITIES ACT (ADA) COMPLIANCE CERTIFICATION

I hereby certify that I am familiar with the requirements of San Diego City Council Policy No. 100-4 regarding the Americans With Disabilities Act (ADA) outlined in the WHITEBOOK, Section 5-1.2, "California Building Code, California Code of Regulations Title 24 and Americans with Disabilities Act", of the project specifications, and that:

This company has in place workplace program that complies with said policy. I further certify that each subcontract agreement for this project contains language which indicates the subcontractor's agreement to abide by the provisions of the policy as outlined.

EXHIBIT C

CONTRACTOR STANDARDS - PLEDGE OF COMPLIANCE

CONTRACTOR CERTIFICATION

CONTRACTOR STANDARDS - PLEDGE OF COMPLIANCE

I declare under penalty of perjury that I am authorized to make this certification on behalf of the company submitting this bid/proposal, that as Contractor, I am familiar with the requirements of City of San Diego Municipal Code § 22.3004 regarding Contractor Standards as outlined in the WHITEBOOK, Section 5-1.4, ("Contractor Standards and Pledge of Compliance"), of the project specifications, and that Contractor has complied with those requirements.

I further certify that each of the Contractor's subcontractors has completed a Pledge of Compliance attesting under penalty of perjury of having complied with City of San Diego Municipal Code § 22.3004.

EXHIBIT D

EQUAL BENEFITS ORDINANCE CERTIFICATION

CONTRACTOR CERTIFICATION

EQUAL BENEFITS ORDINANCE CERTIFICATION

I declare under penalty of perjury that I am familiar with the requirements of and in compliance with the City of San Diego Municipal Code § 22.4300 regarding Equal Benefits Ordinance.

EXHIBIT E

PRODUCT ENDORSEMENT

CONTRACTOR CERTIFICATION

PRODUCT ENDORSEMENT

I declare under penalty of perjury that I acknowledge and agree to comply with the provisions of City of San Diego Administrative Regulation 95.65, concerning product endorsement. Any advertisement identifying or referring to the City as the user of a product or service requires the prior written approval of the City.

EXHIBIT F

AFFIDAVIT OF DISPOSAL

AFFIDAVIT OF DISPOSAL

(To be submitted upon completion of Construction pursuant to the contracts Certificate of Completion)

WHEREAS, on the	DAY OF	,, the undersigned entered
into and executed a co	ntract with the City of	San Diego, a municipal corporation, for:
		torm Drain Emergency
	(Na	me of Project)
(WBS) B-21153 ; and V affirm that "all brush,	WHEREAS , the speciter trash, debris, and su manner"; and WHERE	and identified as Bid No. K-22-2052-EMR-3 ; SAP No. ication of said contract requires the Contractor to plus materials resulting from this project have been AS , said contract has been completed and all surplus
under the terms of sa	id contract, the under	nal payment by the City of San Diego to said Contractor signed Contractor, does hereby affirm that all surplus een disposed of at the following location(s)
•	•	ng to all applicable laws and regulations.
		·
	Contr	actor
by		
ATTEST:		
State of County of		
and for said County an known	d State, duly commissi to me to be the and whose name is s	, 2, before the undersigned, a Notary Public in oned and sworn, personally appeared Contractor named in ubscribed thereto, and acknowledged to me that said
Notary Public in and fo	r said County and Stat	9

EXHIBIT G

NON-COLLUSION AFFIDAVIT TO BE EXECUTED BY BIDDER AND SUBMITTED WITH BID UNDER 23 UNITED STATES CODE 112 AND PUBLIC CONTRACT CODE 7106

NON-COLLUSION AFFIDAVIT TO BE EXECUTED BY BIDDER AND SUBMITTED WITH BID UNDER 23 UNITED STATES CODE 112 AND PUBLIC CONTRACT CODE 7106

State of California County of San Diego

The bidder, being first duly sworn, deposes and says that he or she is authorized by the party making the foregoing bid that the bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the bid is genuine and not collusive or sham; that the bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or that anyone shall refrain from bidding; that the bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder, or to secure any advantage against the public body awarding the contract of anyone interested in the proposed contract; that all statements contained in the bid are true; and further, that the bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay, any fee to any corporation, partnership, company association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham bid.

EXHIBIT H

CONTRACTOR'S CERTIFICATION OF PENDING ACTIONS

CONTRACTOR'S CERTIFICATION OF PENDING ACTIONS

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of all instances within the past 10 years where a complaint was filed or pending against the Bidder in a legal or administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers, and a description of the status or resolution of that complaint, including any remedial action taken.

	subject of	a complaint or pending a	iction in a leg	al adminis	e Bidder has NOT been the strative proceeding alleging ctors, vendors or suppliers
	of a comp Bidder dis description	plaint or pending action i criminated against its em	n a legal adr nployees, sub on of that con	ninistrativ contracto	Bidder has been the subjecte proceeding alleging that rs, vendors or suppliers. A cluding any remedial action
DATE OF CLAIM	LOCATION	DESCRIPTION OF CLAIM	LITIGATION (Y/N)	STATUS	RESOLUTION/REMEDIAL ACTION TAKEN
Contractor	Name:		•		
Certified By	/			Title	
		Name			
		Cignatura		Date	
		Signature			

USE ADDITIONAL FORMS AS NECESSARY

CHECK ONE BOX ONLY.

EXHIBIT I

MANDATORY DISCLOSURE OF BUSINESS INTERESTS FORM

Mandatory Disclosure of Business Interests Form

BIDDER/PROPOSER INFORMATION

Le	gal Name		DBA		
Street Address	City	State	Zip		
Contact Person, Title		Phone	Fax		

Provide the name, identity, and precise nature of the interest* of all persons who are directly or indirectly involved** in this proposed transaction (SDMC § 21.0103).

- * The precise nature of the interest includes:
- the percentage ownership interest in a party to the transaction,
- the percentage ownership interest in any firm, corporation, or partnership that will receive funds from the
- transaction, the value of any financial interest in the transaction,
- any contingent interest in the transaction and the value of such interest should the contingency be satisfied, and any
- philanthropic, scientific, artistic, or property interest in the transaction.
- ** Directly or indirectly involved means pursuing the transaction by:
- communicating or negotiating with City officers or employees,
- submitting or preparing applications, bids, proposals or other documents for purposes of contracting with the City,
- or directing or supervising the actions of persons engaged in the above activity.

Name	Title/Position
City and State of Residence	Employer (if different than Bidder/Proposer)
Interest in the transaction	

Name	Title/Position
City and State of Residence	Employer (if different than Bidder/Proposer)
Interest in the transaction	

* Use Additional Pages if Necessary *

Under penalty of perjury under the laws of the State of California, I certify that I am responsible for the completeness and accuracy of the responses contained herein, and that all information provided is true, full and complete to the best of my knowledge and belief. I agree to provide written notice to the Mayor or Designee within five (5) business days if, at any time, I learn that any portion of this Mandatory Disclosure of Business Interests Form requires an updated response. Failure to timely provide the Mayor or Designee with written notice is grounds for Contract termination.

Print Name, Title	Signature	Date

Failure to sign and submit this form with the bid/proposal shall make the bid/proposal non-responsive. In the case of an informal solicitation, the contract will not be awarded unless a signed and completed Mandatory Disclosure of Business Interests Form is submitted.

EXHIBIT J

FORMS

CONTRACTOR'S CERTIFICATION OF PENDING ACTIONS

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of all instances within the past 10 years where a complaint was filed or pending against the Bidder in a legal or administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers, and a description of the status or resolution of that complaint, including any remedial action taken.

The undersigned certifies that within the past 10 years the Bidder has NOT been the subject of a complaint or pending action in a legal administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers. V The undersigned certifies that within the past 10 years the Bidder has been the subject of a complaint or pending action in a legal administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers. A description of the status or resolution of that complaint, including any remedial action taken and the applicable dates is as follows: RESOLUTION/REMEDIAL DATE OF LOCATION **DESCRIPTION OF CLAIM** LITIGATION **STATUS ACTION TAKEN** (Y/N) CLAIM HAZARD CONSTRUCTION COMPANY Contractor Name:

USE ADDITIONAL FORMS AS NECESSARY

Name

Signature

RESIDENT

Certified By

CHECK ONE BOX ONLY.

HAZARD CONSTRUCTION COMPANY CONTRACTORS CERTIFICATION OF PENDING ACTIONS

In March 2013, a lawsuit was filed against Hazard Construction Company by a former employee, Kenneth McDonald, in the Superior Court of California, County of San Diego. McDonald was laid off by Hazard as part of a company-wide labor force reduction in December 2011. The lawsuit stated various allegations of discrimination, harassment, and retaliation against McDonald by Hazard and/or its employees. Hazard's management believed the lawsuit was without merit and vigorously defended against the allegations. This matter was mediated and settled in January 2014 without any admission of wrongdoing or fault by Hazard.

In May 2016, a lawsuit was filed against Hazard Construction Company by a former employee, Trinidad Davalos, in the Superior Court of California, County of San Diego. Davalos was terminated earlier in 2016. The lawsuit stated a claim for wrongful termination due to disability discrimination against Davalos. Hazard's management believes the lawsuit is without merit and has vigorously defended against the allegation. This matter was settled in January 2017 without any admission of wrongdoing or fault by Hazard.

EXHIBIT I

MANDATORY DISCLOSURE OF BUSINESS INTERESTS FORM

Mandatory Disclosure of Business Interests Form

BIDDER/PROPOSER INFORMATION

Legal	Name		DBA	
Hazard Construction Company				
Street Address City		State	Zip	
0529 Vine Street	Lakeside	California	92040	
Contact Person, Title		Phone	Fax	
Jason A. Mordhorst		858-587-3600	858-453-6034	

Provide the name, identity, and precise nature of the interest* of all persons who are directly or indirectly involved** in this proposed transaction (SDMC § 21.0103).

- * The precise nature of the interest includes:
- the percentage ownership interest in a party to the transaction,
- the percentage ownership interest in any firm, corporation, or partnership that will receive funds from the
- transaction, the value of any financial interest in the transaction,
- any contingent interest in the transaction and the value of such interest should the contingency be satisfied, and any
- philanthropic, scientific, artistic, or property interest in the transaction.
- ** Directly or indirectly involved means pursuing the transaction by:
- communicating or negotiating with City officers or employees,
- · submitting or preparing applications, bids, proposals or other documents for purposes of contracting with the City,
- or directing or supervising the actions of persons engaged in the above activity.

Name	Title/Position
Jason A. Mordhorst	President
City and State of Residence	Employer (if different than Bidder/Proposer)
San Diego, CA	
Interest in the transaction	
63.16%	

Name	Title/Position			
Emmanuel Gavino	Chief Financial Officer / Secretary			
City and State of Residence	Employer (if different than Bidder/Proposer)			
Chula Vista, CA				
Interest in the transaction				
31.58%				

* Use Additional Pages if Necessary *

Under penalty of perjury under the laws of the State of California, I certify that I am responsible for the completeness and accuracy of the responses contained herein, and that all information provided is true, full and complete to the best of my knowledge and belief. I agree to provide written notice to the Mayor or Designee within five (5) business days if, at any time, I learn that any portion of this Mandatory Disclosure of Business Interests Form requires an updated response. Failure to timely provide the Mayor or Designee with written notice is grounds for Contract termination.

Jason A. Mordhorst, President

Print Name, Title

Signature

Date

Failure to sign and submit this form with the bid/proposal shall make the bid/proposal non-responsive. In the case of an informal solicitation, the contract will not be awarded unless a signed and completed Mandatory Disclosure of Business Interests Form is submitted.

EXHIBIT J

FORMS

HAZARD CONSTRUCTION COMPANY

LIST OF SUBCONTRACTORS

In accordance with the requirements of the "Subletting and Subcontracting Fair Practices Act", Section 4100, of the California Public Contract Code (PCC), the Bidder is to list below the name, address and license number of each Subcontractor who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement, in an amount of or in excess of 0.5% of the Contractor's total Bid. Failure to comply with this requirement may result in the Bid being rejected as non-responsive. The Contractor is to list only one Subcontractor for each portion of the Work. The Bidder's attention is directed to the GREENBOOK and Special Provisions Section 3-2, "SELF-PERFORMANCE", which stipulates the percentage of the Work to be performed with the Bidder's own forces. The Bidder is to also list all SLBE, ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which the Bidders are seeking recognition towards achieving any mandatory, voluntary, or both subcontracting participation percentages.

NAME, ADDRESS AND TELEPHONE NUMBER OF SUBCONTRACTOR	CONSTRUCTOR OR DESIGNER	DIR REGISTRATION NUMBER	SUBCONTRACTOR LICENSE NUMBER	TYPE OF WORK	DOLLAR VALUE OF SUBCONTRACT	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSBØ	WHERE CERTIFIED Ø	CHECK IF JOINT VENTURE PARTNERSHIP
Name	4	114			=			
Name:								

 As appropriate, Bidder shall identify Subcontractor as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE): Certified Minority Business Enterprise Certified Woman Business Enterprise MBE WBE Certified Disadvantaged Business Enterprise DBE Certified Disabled Veteran Business Enterprise DVBE Other Business Enterprise OBE Certified Emerging Local Business Enterprise ELBE Certified Small Local Business Enterprise SLBE Small Disadvantaged Business SDB Woman-Owned Small Business WoSB **HUBZone Business HUBZone** Service-Disabled Veteran Owned Small Business 5DVOSB ② As appropriate, Bidder shall indicate if Subcontractor is certified by: City of San Diego CITY State of California Department of Transportation **CALTRANS** California Public Utilities Commission CPUC State of California's Department of General Services CADoGS City of Los Angeles LA State of California CA U.S. Small Business Administration SBA

The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.

HAZARD CONSTRUCTION COMPANY

NAMED EQUIPMENT/MATERIAL SUPPLIER LIST

NAME, AI	ODRESS AND TELEPHONE NUMBER OF VENDOR/SUPPLIER	MATERIALS OR SUPPLIES	DOLLAR VALUE OF MATERIAL OR SUPPLIES (MUST BE FILLED OUT)	SUPPLIER (Yes/No)	MANUFACTURER (Yes/No)	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB®	WHERE CERTIFIED@
Name:							
City:	State:		. 112				
Zip:	Phone:						
			X V				
Name:							
Citv:	State:						
	Phone:						
0	As appropriate, Bidder shall identify Ven	dor/Supplier as one of	the following and shall incli	ude a valid pr	oof of certification (ex	cept for OBE, SLBE and	j ELBE):
	Certified Minority Business Enterprise		MBE		oman Business Enterp		WBE
	Certified Disadvantaged Business Enterp	orise	DBE		sabled Veteran Busine	•	DVBE
	Other Business Enterprise		OBE		nerging Local Busines	s Enterprise	ELBE
	Certified Small Local Business Enterprise	2	SLBE		dvantaged Business		SDB
	Woman-Owned Small Business Service-Disabled Veteran Owned Small E	Queinoss	WoSB SDVOSB	HUBZone B	susiness		HUBZone
	Service-Disabled veterall Owned Small b	pusitiess	304036				
Ø	As appropriate, Bidder shall indicate if V	endor/Supplier is certi	fied by:				
	City of San Diego		CITY	State of Cal	lifornia Department of	f Transportation	CALTRANS
	California Public Utilities Commission		CPUC				
	State of California's Department of Gene	eral Services	CADoGS	City of Los	0	_	LA
	State of California		CA	u.s. small E	Business Administratio	on	SBA

The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.

DEBARMENT AND SUSPENSION CERTIFICATION

EFFECT OF DEBARMENT OR SUSPENSION

To promote integrity in the City's contracting processes and to protect the public interest, the City shall only enter into contracts with responsible bidders and contractors. In accordance with San Diego Municipal Code §22.0814 (a): Bidders and contractors who have been debarred or suspended are excluded from submitting bids, submitting responses to requests for proposal or qualifications, receiving contract awards, executing contracts, participating as a subcontractor, employee, agent or representative of another person contracting with the City.

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of Names of the Principal Individual owner(s)

The names of all persons interested in the foregoing proposal as Principals are as follows:

NAME	TITLE
Silling	
Methaculd Princip	als

IMPORTANT NOTICE: If Bidder or other interested person is a corporation, state secretary, treasurer, and manager thereof; if a co-partnership, state true name of firm, also names of all individual co-partners composing firm; if Bidder or other interested person is an individual, state first and last names in full.

The Bidder, under penalty of perjury, certifies that, except as noted below, he/she or any person associated therewith in the capacity of owner, partner, director, officer, manager:

- Is not currently under suspension, debarment, voluntary exclusion, or determination of ineligibility by any Federal, State or local agency;
- has not been suspended, debarred, voluntarily excluded or determined ineligible by any Federal, State or local agency within the past 3 years;
- does not have a proposed debarment pending; and
- has not been indicted, convicted, or had a civil judgment rendered against it by a court of competent jurisdiction in any matter involving fraud or official misconduct within the past 3 years.

If there are any exceptions to this certification, insert the exceptions in the following space.

NA	
•	considered in determining bidder responsibility. For any exception noted above, indicate below to itiating agency, and dates of action.
Contractor Name:_	HAZARD CONSTRUCTION COMPANY
Certified By	
	Name 10/29/21
	Signature
NOTE:	Providing false information may result in criminal prosecution or administrative sanctions.



10529 Vine Street Lakeside, CA 92040 Phone (858) 587-3600 Fax (858) 453-6034 License No. 750542 A/C31 DIR No. 1000022121 hazardconstruction.com

Principals

Jason A. Mordhorst W.S. Rogers Mark Thunder Bryan Seeger Emmanuel Gavino President Exec. V.P. / Asst. Secretary Vice President of Operations Vice President of Estimating Treasurer / Secretary

Names of the Principal individual owner(s)

FOR SUBCONTRACTORS/SUPPLIERS/MANUFACTURERS

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of Names of the Principal Individual owner(s) for their subcontractor/supplier/manufacturers.

Please	indicate if prin	cipal owner is servi	ng in the capac	ity of subcontract	or, supplier, and/or	manufacturer:
	SUBCONTR	ACTOR		SUPPLIER		MANUFACTURER
	V'	NAME			TITLE	Activities of the state of the
-						
	SUBCONTR	ACTOR		SUPPLIER		MANUFACTURER
	PRODUCT NO.	NAME			TITLE	
-						
	SUBCONTR	ACTOR		SUPPLIER		MANUFACTURER
		NAME			TITLE	
-				_		
	SUBCONTR	ACTOR		SUPPLIER		MANUFACTURER
		NAME	<u> </u>	R	TITLE	
-						
Contra	ctor Name:	HAZARD CO	NSTRUCT	ON COMPAN	IV .	
		JAZON A. I	MODDIOD	ST, PRESIDEN	'n	
Certifie	ed By	SAPONA.	Name	24 THEOREM	Title	
		L	Marie	,		11-
	-	112	Ciarra		Date	129/21
		1	Signature			

USE ADDITIONAL FORMS AS NECESSARY



EOC Work Force Report (rev. 08/2018)

EQUAL OPPORTUNITY CONTRACTING (EOC)

1200 Third Avenue, Suite 200 · San Diego, CA 92101 Phone: (619) 236-6000 · Fax: (619) 236-5904

WORK FORCE REPORT

The objective of the Equal Employment Opportunity Outreach Program, San Diego Municipal Code Sections 22.3501 through 22.3517, is to ensure that contractors doing business with the City, or receiving funds from the City, do not engage in unlawful discriminatory employment practices prohibited by State and Federal law. Such employment practices include, but are not limited to unlawful discrimination in the following: employment, promotion or upgrading, demotion or transfer, recruitment or recruitment advertising, layoff or termination, rate of pay or other forms of compensation, and selection for training, including apprenticeship. Contractors are required to provide a completed Work Force Report (WFR).

NO OTHER FORMS WILL BE ACCEPTED

		CONTRACTOR ID	ENTIFICATION	l	
Type of Contractor:	□ Consultant	☐ Grant Recipient	☐ Financial Ir ☐ Insurance (nstitution □ I Company □ C	Lessee/Lessor Other
Name of Company: Haz	ard Construction I	ENGR LLC			
ADA/DBA:					
Address (Corporate Head	quarters, where appli	icable): 10529 Vine Sti	reet		
City: Lakeside		County: San Diego			Zip: <u>92040</u>
Telephone Number: 858	-587-3600		Fax Number: 85	8-200-3619	
Name of Company CEO:	Jason A. Mordhor	rst, President			
Address(es), phone and f		pany facilities located in	San Diego County	(if different from abov	e):
City:		County:		State:	Zip:
Telephone Number:		_ Fax Number:		Email:	
Type of Business: Heav	⁄y Highway		Type of License:	Contractor	
The Company has appoin	ited: Emmanuel Ga	vino and Mark Thund	ler		
As its Equal Employment				to establish, dissemin	ate and enforce equal
employment and affirma	tive action policies of	f this company. The EEO	O may be contacte	d at:	
Address: 10529 Vine S	treet, Lakeside, CA	92040			
Telephone Number: 858	-587-3600	Fax Number: 858-20	0-3619	_ _{Email:} _ngavino@h	azardcon.com
		One San Diego Cou	nty (or Most L	ocal County) Work	Force – Mandatory
		Branch Work Force			
		l Managing Office W			
	_	i Managing Office W	OIR POICE		
		Check the box above tha			
*Submit a separa	ate Work Force Repor	t for all participating bro	anches. Combine V	VFRs if more than one	branch per county.
I, the undersigned repres	sentative of Hazard (Construction Compan	у		
i, the underorghed repres			rm Name)		 :
San Diego		, <u>CA</u>		hereby certify that inf	ormation provided
(County herein is true and correct	y)	(State)		of January	20.22
9	Int			Lety Dhe	
(Authori	zed Signature)		-	uthorized Signature Nam	

1 of 7

Form Number: BB05

WORK FORCE REPORT - Page 2 NAME OF FIRM: Hazard Cons	structio	n ENG	SR LLC							Di	ATE: <u>1</u>	/28/20	022	
OFFICE(S) or BRANCH(ES): N/									COUNT		an Die			
INSTRUCTIONS: For each occup provided. Sum of all totals should time basis. The following groups	l be eau	al to vo	ur total	. work f	orce. I	nclude	all thos	se empl	loyed b	ery ethi y your (nic grou compan	up. Tot ıy on ei	al colu ther a t	mns in ro full or par
 Black or African-American Hispanic or Latino Asian American Indian or Alaska Definitions of the race and ethnical	a Nativo		can be _s	found o	n Page	(6) (7)	Native White Other						other g	roups
ADMINISTRATION OCCUPATIONAL CATEGORY	(1) Black or African American		(2) Hispanic or Latino		(3) Asian		(4) American Indian/ Nat. Alaskan		(5) Pacific Islander		(6) White		Other	7) r Race/ nicity
	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)
Management & Financial			3								7			
Professional														
A&E, Science, Computer														
Technical														
Sales														
Administrative Support														
Services				2000										
Crafts														
Operative Workers														
Transportation	6		2		1						4			
Laborers*				(((
*Construction laborers and other field	d employ	ees are 1	not to be	include	d on this	s page								
Totals Each Column	6	0	5	0	1	0	0	0	0	0	11	0	0	0
Grand Total All Employees		23												
Indicate by Gender and Ethnicity	the Nu	mber o	f Above	Employ	yees W	ho Are	Disable	d:	1	1				
Disabled								İ						İ
Non-Profit Organizations Only:														
Board of Directors										į				
Volunteers														
Artists														
			1117								1			

FFICE(S) or BRANCH(ES): N/A NSTRUCTIONS: For each occupational	catego	ory, inc	licate 1	numbe	r of m	ales ar	nd fem	— ales in	UNTY: every	ethnic	Diego group	. Tota	l colun	nns in
rovided. Sum of all totals should be eq me basis. The following groups are to	ual to y be incl	your to uded in	tal wor ethnic	k force catego	e. Inclu ories lis	ide all sted in	those e columi	mploy ns belo	ed by y w:	our co	mpany	on eit	her a fi	ıll or p
.) Black or African-American 2) Hispanic or Latino 3) Asian 4) American Indian or Alaska Nati efinitions of the race and ethnicity ca		s can b	e foun	d on Pe	(7	6) Wh							ther gr	oups
TRADE OCCUPATIONAL CATEGORY	(1) Black or African American		(2) Hispanic or Latino		(3) Asian		(4) American Indian/ Nat. Alaskan		(5) Pacific Islander		(6) White		(7) Other Race/ Ethnicity	
	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)	(M)	(F)
Brick, Block or Stone Masons														
Carpenters			6								4			
Carpet, Floor & Tile Installers Finishers														
Cement Masons, Concrete Finishers														
Construction Laborers	1		18								5			
Drywall Installers, Ceiling Tile Inst														
Electricians														
Elevator Installers														
First-Line Supervisors/Managers														
Glaziers														
Helpers; Construction Trade														
Millwrights														
Misc. Const. Equipment Operators	2		17								10			
Painters, Const. & Maintenance														
Pipelayers, Plumbers, Pipe & Steam Fitters														
Plasterers & Stucco Masons														
Roofers														
Security Guards & Surveillance Officers														
Sheet Metal Workers														
Structural Metal Fabricators &														
Fitters Welding, Soldering & Brazing Workers														
Workers, Extractive Crafts, Miners														
Totals Each Column	3	0	41	0	0	0	0	0	0	0	19	0	0	0
Grand Total All Employees		86											1	
ndicate By Gender and Ethnicity the N														



Work Force Report

HISTORY

The Work Force Report (WFR) is the document that allows the City of San Diego to analyze the work forces of all firms wishing to do business with the City. We are able to compare the firm's work force data to County Labor Force Availability (CLFA) data derived from the United States Census. CLFA data is a compilation of lists of occupations and includes the percentage of each ethnicity we track (American Indian or Alaska Native, Asian, Black or African-American, Native Hawaiian or Pacific Islander, White, and Other) for each occupation. Currently, our CLFA data is taken from the 2010 Census. In order to compare one firm to another, it is important that the data we receive from the consultant firm is accurate and organized in the manner that allows for this fair comparison.

WORK FORCE & BRANCH WORK FORCE REPORTS

When submitting a WFR, especially if the WFR is for a specific project or activity, we would like to have information about the firm's work force that is actually participating in the project or activity. That is, if the project is in San Diego and the work force is from San Diego, we want a San Diego County Work Force Report¹. By the same token, if the project is in San Diego, but the work force is from another county, such as Orange or Riverside County, we want a Work Force Report from that county2. If participation in a San Diego project is by work forces from San Diego County and, for example, from Los Angeles County and from Sacramento County, we ask for separate Work Force Reports representing your firm from each of the three counties.

MANAGING OFFICE WORK FORCE

Equal Opportunity Contracting may occasionally ask for a Managing Office Work Force (MOWF) Report. This may occur in an instance where the firm involved is a large national or international firm but the San Diego or other local work force is very small. In this case, we may ask for both a local and a MOWF Report^{1, 3}. In another case, when work is done only by the Managing Office, only the MOWF Report may be necessary.³

TYPES OF WORK FORCE REPORTS:

Please note, throughout the preceding text of this page, the superscript numbers one ¹, two ² & three ³. These numbers coincide with the types of work force report required in the example. See below:

- ¹ One San Diego County (or Most Local County)
 Work Force Mandatory in most cases
- ² Branch Work Force *
- ³ Managing Office Work Force
- *Submit a separate Work Force Report for all participating branches. Combine WFRs if more than one branch per county.

RACE/ETHNICY CATEGORIES

American Indian or Alaska Native – A person having origins in any of the peoples of North and South America (including Central America) and who maintains tribal affiliation or community attachment.

Asian – A person having origins in any of the peoples of the Far East, Southeast Asia, or the Indian subcontinent including, for example, Cambodia, China, India, Japan, Korea, Malaysia, Pakistan, the Philippine Islands, Thailand, and Vietnam.

Black or African American – A person having origins in any of the Black racial groups of Africa.

Native Hawaiian or Pacific Islander – A person having origins in any of the peoples of Hawaii, Guam, Samoa, or other Pacific Islands.

White – A person having origins in any of the peoples of Europe, the Middle East, or North Africa.

Hispanic or Latino – A person of Cuban, Mexican, Puerto Rican, South or Central American, or other Spanish culture or origin.

Exhibit A: Work Force Report Job Categories – Administration

Refer to this table when completing your firm's Work Force Report form(s).

Management & Financial

Advertising, Marketing, Promotions, Public Relations, and Sales Managers **Business Operations Specialists** Financial Specialists **Operations Specialties Managers** Other Management Occupations **Top Executives**

Professional

Art and Design Workers Counselors, Social Workers, and Other Community and Social Service Specialists Entertainers and Performers, Sports and Related Workers Health Diagnosing and Treating Practitioners Lawyers, Judges, and Related Workers Librarians, Curators, and Archivists Life Scientists Media and Communication Workers Other Teachers and Instructors **Postsecondary Teachers** Primary, Secondary, and Special Education School Teachers **Religious Workers** Social Scientists and Related Workers

Architecture & Engineering, Science, Computer

Architects, Surveyors, and Cartographers **Computer Specialists Engineers Mathematical Science Occupations** Physical Scientists

Technical

Drafters, Engineering, and Mapping Technicians Health Technologists and Technicians Life, Physical, and Social Science Technicians Media and Communication Equipment Workers

Sales

Other Sales and Related Workers **Retail Sales Workers** Sales Representatives, Services Sales Representatives, Wholesale and Manufacturing Supervisors, Sales Workers

Administrative Support

Financial Clerks Information and Record Clerks **Legal Support Workers**

Material Recording, Scheduling, Dispatching, and Distributing Workers Other Education, Training, and Library Occupations Other Office and Administrative Support Workers

Secretaries and Administrative Assistants Supervisors, Office and Administrative Support Workers

Services

Building Cleaning and Pest Control Workers Cooks and Food Preparation Workers **Entertainment Attendants and Related** Workers

Fire Fighting and Prevention Workers First-Line Supervisors/Managers, Protective Service Workers

Food and Beverage Serving Workers **Funeral Service Workers** Law Enforcement Workers

Nursing, Psychiatric, and Home Health Aides Occupational and Physical Therapist Assistants and Aides

Other Food Preparation and Serving Related Workers

Other Healthcare Support Occupations Other Personal Care and Service Workers Other Protective Service Workers Personal Appearance Workers Supervisors, Food Preparation and Serving Workers Supervisors, Personal Care and Service

Transportation, Tourism, and Lodging Attendants

Crafts

Page 5 of 7

Construction Trades Workers Electrical and Electronic Equipment Mechanics, Installers, and Repairers **Extraction Workers Material Moving Workers** Other Construction and Related Workers Other Installation, Maintenance, and Repair Occupations Plant and System Operators Supervisors of Installation, Maintenance, and Repair Workers Supervisors, Construction and Extraction Workers Vehicle and Mobile Equipment Mechanics,

Form Number: BBo5

Installers, and Repairers Woodworkers

Operative Workers

Assemblers and Fabricators **Communications Equipment Operators Food Processing Workers** Metal Workers and Plastic Workers **Motor Vehicle Operators** Other Production Occupations **Printing Workers** Supervisors, Production Workers Textile, Apparel, and Furnishings Workers

Transportation

Air Transportation Workers Other Transportation Workers **Rail Transportation Workers** Supervisors, Transportation and Material **Moving Workers** Water Transportation Workers

Laborers

Agricultural Workers Animal Care and Service Workers Fishing and Hunting Workers Forest, Conservation, and Logging Workers **Grounds Maintenance Workers** Helpers, Construction Trades Supervisors, Building and Grounds Cleaning and Maintenance Workers Supervisors, Farming, Fishing, and Forestry Workers

Exhibit B: Work Force Report Job Categories-Trade

Brick, Block or Stone Masons Brickmasons and Blockmasons

Stonemasons

Carpenters

Carpet, floor and Tile Installers and Finishers

Carpet Installers

Floor Layers, except Carpet, Wood and Hard

Tiles

Floor Sanders and Finishers Tile and Marble Setters

Cement Masons, Concrete Finishers

Cement Masons and Concrete Finishers Terrazzo Workers and Finishers

Construction Laborers

Drywall Installers, Ceiling Tile Inst Drywall and Ceiling Tile Installers **Tapers**

Electricians

Elevator Installers and Repairers

First-Line Supervisors/Managers

First-line Supervisors/Managers of Construction Trades and Extraction Workers

Glaziers

Helpers, Construction Trade

Brickmasons, Blockmasons, and Tile and Marble Setters Carpenters Electricians Painters, Paperhangers, Plasterers and Stucco Pipelayers, Plumbers, Pipefitters and

Steamfitters Roofers

All other Construction Trades

Millwrights

Heating, Air Conditioning and Refrigeration Mechanics and Installers Mechanical Door Repairers Control and Valve Installers and Repairers Other Installation, Maintenance and Repair Occupations

Misc. Const. Equipment Operators

Paving, Surfacing and Tamping Equipment Operators Pile-Driver Operators Operating Engineers and Other Construction Equipment Operators

Painters, Const. Maintenance

Painters, Construction and Maintenance Paperhangers

Pipelayers and Plumbers

Pipelayers Plumbers, Pipefitters and Steamfitters

Plasterers and Stucco Masons

Roofers

Security Guards & Surveillance Officers

Sheet Metal Workers

Structural Iron and Steel Workers

Welding, Soldering and Brazing Workers

Welders, Cutter, Solderers and Brazers Welding, Soldering and Brazing Machine Setter, Operators and Tenders

Workers, Extractive Crafts, Miners

EXHIBIT K

SUPPLEMENTARY SPECIAL PROVISIONS

SUPPLEMENTARY SPECIAL PROVISIONS

The following Supplementary Special Provisions (SSP) modifies the following documents:

- 1. The **2018 Edition** of the Standard Specifications for Public Works Construction (The "GREENBOOK").
- 2. The **2018 Edition** of the City of San Diego Standard Specifications for Public Works Construction (The "WHITEBOOK"), including the following:
 - a) General Provisions (A) for all Construction Contracts.
 - b) General Provisions (B) for Design-Build and Multiple Award Construction Contracts.

PART 0 - EQUAL OPPORTUNITY CONTRACTING PROGRAM (EOCP)

SECTION A - GENERAL REQUIREMENTS

- **0-12 CONTRACT RECORDS AND REPORTS.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. You shall maintain records of all subcontracts and invoices from your Subcontractors and Suppliers for work on this project. Records shall show name, telephone number including area code, and business address of each Subcontractor, Supplier, and joint venture partner, and the total amount actually paid to each firm. Project relevant records, regardless of tier, may be periodically reviewed by the City.
 - 2. You shall retain all records, books, papers, and documents pertinent to the Contract for a period of not less than 5 years after Notice of Completion and allow access to said records by the City's authorized representatives.
 - 3. You shall submit the following reports using the City's web-based contract compliance (Prism® portal):
 - a) **Monthly Payment.** You shall submit Monthly Payment Reporting by the 10th day of the subsequent month. Incomplete and/or delinquent reporting may cause payment delays, non-payment of invoices, or both.
 - 4. The records maintained under item 1, described above, shall be consolidated into a Final Summary Report, certified as correct by an authorized representative of the Contractor. The Final Summary Report shall include all subcontracting activities and be sent to the EOCP Program Manager prior to Acceptance. Failure to comply may result in assessment of liquidated damages or withholding of retention. The City will review and verify 100% of subcontract participation reported in the Final Summary Report prior to approval and release of final retention to you. In the event your Subcontractors are owed money for completed Work, the City may authorize payment to subcontractor via a joint check from the withheld retention.

SECTION 1 – GENERAL, TERMS, DEFINITIONS, ABBREVIATIONS, UNITS OF MEASURE, AND SYMBOLS

- **1-2 TERMS AND DEFINITIONS.** To the "WHITEBOOK", items 56, 69, and 102, DELETE in their entirety and SUBSTITUTE with the following:
 - 56. **Notice of Completion (NOC)** A document recorded with the County of San Diego to signify that the Contract Work has been completed and accepted by the City.
 - 69. **Punchlist** A list of items of Work or corrections generated after a Walk-through that is conducted when you consider that the Work and Services are complete, and as verified by the Owner. The Punchlist may be completed in phases if defined in the Contract.
 - 102. **Walk-through** An inspection the City uses to verify the completion of the Project or phase of the Project and to generate a Punchlist prior to Acceptance.

To the "WHITEBOOK", item 54, "Normal Working Hours", ADD the following:

The Normal Working Hours are 8:00 AM to 4:00 PM.

To the "WHITEBOOK", ADD the following:

- 108. Acceptance When all of the Contract Work, including all Punchlist items, is deemed officially complete by the City Asset Owning Department or Deputy City Engineer.
- 109. **Occupancy** When the Owner deems a building is ready for use, the Owner will issue a certificate of Occupancy in writing.
- 110. **Substantial Completion** When all Contract Work is deemed complete by the Contractor in writing, and as verified by the Owner. Substantial Completion may be completed in phases if defined in the Contract.
- **1-7.1.3 Requests for Information (RFI).** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - Should You discover a conflict, omission, errors in the Contract Documents, differences with existing field conditions, or have any questions concerning interpretation or clarification of Contract Documents, or when you propose deviations to the standards or design, you shall submit a Request for Information (RFI) to the City regarding your question or clarification within 1 Working Day.
 - 2. Your RFI shall meet the following requirements:
 - a) All RFIs, whether by You or your Subcontractor or supplier at any tier, shall be submitted by You to the City.
 - b) RFIs shall be numbered sequentially.

- c) You shall clearly and concisely set forth the single issue for which interpretation or clarification is sought, indicate Specification Section numbers, Contract Drawing numbers, and details, or other items involved, and state why a response is required from the City.
- d) RFIs shall be submitted within **1 Working Day** in order that they may be adequately researched and answered before the response affects any critical activity of the Work.
- e) Should You believe that a response to an RFI causes a change to the requirements of the Contract, You shall, before proceeding, give written notice to the City, indicating that You believe that City response to the RFI to be a Change Order. Failure to give such written notice within **5 Working Days** of receipt of the City's response to the RFI shall waive Your right to seek additional time or cost.
- 3. The City will respond to RFIs within **5 Working Days** unless the City notifies You in writing that a response will take longer. The **5 Working Days** shall begin when the RFI is received and dated by the City. Responses from the City will not change any requirement of the Contract unless so noted by the City in the response to the RFI. The City will not issue a Change Order for Extra Work or additional time when the issue raised in the RFI was due to your fault, neglect, or any unauthorized deviations from the project design or specifications.
- 4. If You proceed in resolving a conflict, omission, or any error in the Contract Documents without sending the City an RFI in accordance with the requirements stated above, the City may require You to remove such work at Your cost or back charge You the cost to remove this work.
- **1-7.2 Contract Bonds.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Before execution of the Contract, file payment and performance bonds with the City to be approved by the Board in the amounts and for the purposes noted. Bonds shall be executed by a responsible surety as follows:
 - a) If the Work is being funded with state or local money, consistent with California Code of Civil Procedure §995.670, the Surety shall be an "admitted surety" authorized by the State of California Department of Insurance to transact surety insurance in the State.
 - b) If the Work is being funded with federal money, the Surety shall be listed in the U.S. Treasury Department Circular 570 and shall be in conformance with the specified Underwriting Limitations.

To the "WHITEBOOK", item 2, subsection "a", subsection "i", DELETE in its entirety and SUBSTITUTE with the following:

i. A "Payment Bond" (Materials and Labor Bond) is optional. If no bond is submitted, no payment shall be made until 35 Calendar Days after Acceptance

and any lien requirements have been fulfilled. If a bond is submitted, progress payments shall be made in accordance with these Specifications.

To the "WHITEBOOK", item 2, subsection "d", DELETE in its entirety and SUBSTITUTE with the following:

- d) For Contracts over \$100,000:
 - i. A "Payment Bond" (Materials and Labor Bond) for 100% of the Contract Price to satisfy claims of material Suppliers and of mechanics and laborers employed on the Work. You shall maintain the bond in full force and effect until Acceptance and until all claims for materials and labor are paid and shall otherwise comply with the Government Code.
 - ii. A "Faithful Performance Bond" for 100% of the Contract Price to guarantee faithful performance of Work, within the time prescribed and in a manner satisfactory to the City, that materials and workmanship shall be free from original or developed defects.

To the "WHITEBOOK", item 7, DELETE in its entirety and SUBSTITUTE with the following:

7. You shall require the Surety to mail its standard "Bond Status" form to the Engineer at the following address:

Deputy Director Construction Management and Field Engineering Division 9573 Chesapeake Drive San Diego, CA 92123

SECTION 2 - SCOPE OF THE WORK

- **2-8 EXTRA WORK.** To the "WHITEBOOK", ADD the following:
 - 2. Compensation for "Time-and-Material" emergency Contracts.
 - a) You will be compensated for staff charges directly associated with the project.
 - b) Any invoiced off site work shall include a summary of work.
 - c) Mark up for off site work shall be the same as on site work.

SECTION 3 - CONTROL OF THE WORK

- **3-3 SUBCONTRACTORS.** To the "WHITEBOOK", ADD the following:
 - 10. When a Subcontractor fails to prosecute a portion of the Work in a manner satisfactory to the City, you shall remove such Subcontractor immediately upon written request of the City, and shall request approval of a replacement

Subcontractor to perform the Work in accordance with California Public Contract Code (PCC), Subletting and Subcontracting, Section 4107, at no added cost to the City.

SURVEYING. To the "GREENBOOK" and "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

3-10 SURVEYING (DESIGN-BUILD).

3-10.1 **General.**

- 1. You shall provide all required site layout not specified in this section.
- 2. Unless surveying services are provided by the City, only the Design Firm, not the Contractor, shall be allowed to hire a Licensed Land Surveyor or a Registered Civil Engineer authorized to practice land surveying within the State of California to provide all surveying services needed for the design, and if requested by the City, also for the construction activities required for the completion of the Project. Surveying services include, but are not limited to: land, aerial, topographic and construction.
- 3. If requested by the City, the Design Firm shall submit a letter to the City's Project Manager identifying the Licensed Land Surveyor or the Registered Civil Engineer authorized to practice land surveying within the State of California that will be performing the design and/or construction phase survey services for the Project.
- 4. Where applicable, notify the City in writing at least 2 Working Days prior to requesting survey services to be provided by the City.
- 5. The Design Firm is responsible for performing and meeting the accuracy of surveying standards adequate for design and construction through the Design Firm's Licensed Land Surveyor or Registered Civil Engineer authorized to practice land surveying within the State of California.
- 6. All Survey Services deliverables shall be submitted per the City's CADD Standards and pertinent Public Works Department Engineering Deliverable specifications.

https://www.sandiego.gov/ecp/edocref/drawings

- 7. All Survey Services and deliverables which reveal non-compliance with the requirements of the Construction Documents and standards shall be corrected as deemed necessary by the City at the Design-Builder's expense.
- 8. Where Survey Services are provided by the City, all construction survey stakes, control points, and other survey related marks shall be preserved for the duration of the Project. If any construction survey stakes, control points, or

- other survey related marks are lost or disturbed and need to be replaced, such replacement shall be performed at the Design-Builder's expense.
- 9. The City's Land Survey Section (LSS) shall be notified a minimum of 2 Working Days (large projects may require more) before any ground is to be disturbed within the City of San Diego (concrete, asphalt, or dirt). The LSS may need to inspect the site and provide monumentation information.

3-10.2 Monument Perpetuation.

- Monument Perpetuation, including mark-outs, will be performed by the City Public Works Engineering Support & Technical Services Division's (ES&TS), Land Survey Section (LSS), unless otherwise noted. You are responsible for requesting the coordination of these services.
- 2. If at any time a monument will be destroyed or covered, such monument shall be perpetuated in accordance with state law. Inform the LSS, via project Resident Engineer, if any monument will be destroyed or covered during any construction activity.

3-10.3 Line and Grade.

- 1. The Work shall conform to the lines, elevations, and grades shown on the Plans. Three consecutive points set on the same slope shall be used together so that any variation from a straight grade can be detected. Any such variation shall be reported to the City's PM. In the absence of such report, the Surveyor shall be responsible for any error in the grade of the Work.
- 2. Grades for underground conduits will be set at the surface of the ground. The Design-Builder shall transfer them to the bottom of the trench.

3-10.4 Topographic and Monument Survey - Preliminary Design.

- Topographic field survey shall include all existing ground surface topography, fencing, hardscape, utilities, roadway surface, and curb returns within the delineated mapping limit. Monument survey shall include the sufficient collection of existing record survey monuments to perform right-of-way (ROW) analysis along within subject mapping limits.
- 2. Unless otherwise specified, the Land Surveyor shall adhere to Section 3 of the Minimum Standard Detail Requirements for ALTA/NSPS Land Title Surveys (Effective February 23, 2016).

https://www.nsps.us.com/page/ALTANSPSStandards

- 3. Horizontal Control shall be based on the CCS83 Zone 6, 1991.35 epoch, U.S. Survey Feet per Record of Survey Map No. 14492 (ROS 14492). It is required to tie into a first order monument per ROS 14492 unless a first order monument no longer exists within a three mile radius. Horizontal control measurements shall be collected in conformance with the local standard of practice.
- 4. Vertical Control shall be based on NGVD29 per benchmarks in the City of San Diego Bench Book. Non 1970 adjusted and 1970 adjusted benchmarks listed

- with an asterisk (*) in the City Benchmark book are not to be used together for Vertical Control common adjustment sets are to be used.
- 5. All topographic field survey data shall be collected using conventional survey methods utilizing total station instrumentation.
- 6. Deliverables.
 - a) Horizontal and Vertical Control.
 - i. Completed Calibration sheet as provided indicating the monuments used to establish the Basis of Bearings and Vertical Benchmark held to control this survey.
 - b) Field Data.
 - i. Data collected as points and break lines to define a proper DTM if requested outside of aerial mapping.
 - ii. Includes utilities collected on surface as required.
 - iii. Includes Horizontal control points from ROS 14492 used to define the Basis of Bearings and Vertical control Benchmark(s) to establish elevation.
 - iv. Includes record monument points.
 - v. Data collector project files.
 - vi. Raw (unedited) data file.
 - vii. Project file.
 - viii. Point comma delimited text file formatted.
 - c) Topography.
 - i. Create and deliver a complete ASCII coordinate list (.txt/.doc etc.) of all field collected survey points.
 - The contours produced from the surface digital terrain model (dtm) shall meet or exceed ASPRS 90 standards where 68% (1σ) of the contours tested fall within 1/3 contour interval. Any point tested that is more than 3σ out shall be regarded as a blunder. These standards closely parallel the familiar National Map Accuracy Standards.
 - d) Records Research.
 - All public or private records acquired to determine the City's ROW in the project area delivered in digital or hardcopy format with any markups and City Records as acquired.
 - City records may include but are not limited to GIS scope plots, sewer and water sheets, loose leaf survey notes, Tie Point sheets, dedication or vacation

- drawings, easement drawings, benchmark list, and etc.
- After initial search of City records by the Surveyor, they may request City assistance to search for hard to find records.
- e) Survey Monument Measurements.
 - i. All found monuments located within, or near, the survey limits shall be searched and measured. Sufficient additional monuments to control all boundaries extending from the survey limits shall be tied (i.e. block corners, Points of Curve etc.) to the next available survey monument past the survey limits.
 - All Monuments found shall be described with details as to what was found along with identifying number.

3-10.5 Monument Search, Field Boundary Survey and Boundary Analysis – Right-of-Way (ROW) Mapping.

- 1. The monument survey, for each designated site, shall be of sufficient coverage and quality for a Right-of-Way boundary analysis performed and provided in conformance with City CADD standards.
- 2. Surveyor shall deliver to the City all requested survey information and CADD data, as specified below, upon completion of the Monument Survey and Boundary Analysis.
- 3. Unless otherwise specified, the Land Surveyor shall adhere to Section 3 of the Minimum Standard Detail Requirements for ALTA/NSPS Land Title Surveys (Effective February 23, 2016).

https://www.nsps.us.com/page/ALTANSPSStandards

- 4. Field monument survey to be performed and provided in conformance with City CADD standards.
- 5. Field Measurements shall be collected in conformance the local standard of practice.
- 6. Horizontal Control shall be based on the CCS83 Zone 6, 1991.35 epoch, U.S. Survey Feet units, per City of San Diego Record of Survey Map No. 14492 (ROS 14492). All Project survey control shall be based upon field-tied measurements to a Horizontal First Order monument as shown on ROS 14492. Where existing First Order monument cannot be recovered or located within a 3-mile radial distance from the project site a Horizontal Second-Order Monument may be used as Project survey basis. The Project vertical control datum shall be based on NGVD29 per benchmarks identified in the City of San Diego Vertical Control

Bench Book (Bench Book). All Project benchmarks shall be selected from a common Bench Book source group:

- a) Benchmarks with elevations updated per U.S.C.G.S adjustment of 1970, identified with an asterisk (*).
- b) Benchmarks not adjusted per the 1970 adjusted values (non-asterisked identifiers).

7. Deliverables.

- a) Horizontal and Vertical Control.
 - Completed Calibration sheet indicating the monuments used to establish the Basis of Bearings and Vertical Benchmark held to control this survey.
- b) Field Data.
 - i. Complete, Correct CADD file in conformance with City CADD Standards and industry standards.
 - Includes Horizontal control points from ROS 14492 used to define the Basis of Bearings and Vertical control Benchmark(s) to establish elevation.
 - Includes Monument points covering the area of work.
 - ii. Data collector project files.
 - Raw (unedited) data file.
 - Project file.
 - Point comma delimited text file.
- c) Records Research.
 - If requested, all public or private records acquired to determine the City's ROW in the project area delivered in digital or hardcopy format with any markups and City Records as acquired.
 - ii. City records may include but are not limited to GIS scope plots, sewer and water sheets, loose leaf survey notes, Tie Point sheets, dedication or vacation drawings, easement drawings, benchmark list, and etc.

d) Boundary Ties

- All monuments within the survey limits shall be searched and tied if found. Sufficient additional monuments to control all boundaries extending from the survey limits shall be tied (i.e. Block Corners, Points of Curve etc.) to the next available survey monument past the survey limits.
 - All Monuments found shall be described details as to what was found along with identifying number.

3-10.6 Field Monument Survey and Topographic Utility Survey.

- 1. The right-of-way monumentation survey data shall be provided to the City.
- 2. Surveyor shall perform a right-of-way monument survey and existing utility survey (locating feature centers). Surveyor shall also collect ground surface topography over any aerial obscured areas.
- 3. Unless otherwise specified, the Land Surveyor shall adhere to Section 3 of the Minimum Standard Detail Requirements for ALTA/NSPS Land Title Surveys (Effective February 23, 2016).

https://www.nsps.us.com/page/ALTANSPSStandards

- 4. Field Measurements shall be collected in conformance with the local standard of practice.
- 5. Project Horizontal and Vertical Control.
 - a) The Horizontal and Vertical Control for this project shall be based on the same datum, basis of bearing, calibration and benchmark as used for the Aerial Survey.
 - b) Horizontal Control Shall be based on the CCS83 Zone 6, 1991.35 epoch, U.S. Survey Feet per ROS 14492. It is required to tie into a first order monument per ROS 14492 unless a first order monument no longer exists within a three mile radius.
 - c) Vertical Control shall be based on NGVD29 per benchmarks in the City of San Diego Bench Book. Non 1970 adjusted and 1970 adjusted benchmarks listed with an asterisk (*) in the City Benchmark book are not to be used together for Vertical Control common adjustment sets are to be used.
 - d) If adjacent City projects have been found and are included in the research packages, measurements to a minimum of 3 common control or ROW points shall be made for evaluation and consistency between projects. These projects can be used for establishing common horizontal or vertical control, joining or adding to existing data, and/or as an inventory of survey monuments for search purposes.

6. Deliverables.

- a) Horizontal and Vertical Control.
 - Completed Calibration sheet indicating the monuments used to establish the Basis of Bearings and Vertical Benchmark held to control this survey. The horizontal and vertical control shall be set by the Surveyor that's issued the first Notice to Proceed.
- b) Field Data.

- Data collected as points and break lines to define a proper
 DTM beyond the identified mapping limits if requested.
- ii. Include utilities collected on surface as required.
- iii. Include horizontal control points from ROS 14492 to define the Basis of Bearings and Vertical control Benchmark(s) to establish elevation.
- iv. Include Monument points covering the area of work.
- v. Data collector project files.
 - Raw (unedited) data file.
 - Project file.
 - Point data text file in "comma delimited format".

vi. CADD File.

- A digital design file displaying all field work, existing right-of-way monuments, and utility feature data per City CADD standards. The design file shall be complete, correct, and free of duplicate elements.
- The following data shall be included in the electronic mapping file: Name of Design/Engineering Firm and/or Surveyor doing the project, Company Logo (if available), Name of project, Work order number, Date & Scale.
- Include right-of-way monument elements.
- Use appropriate levels and attributes for all elements to meet City of San Diego CADD Standards.

c) Topography

- i. Create and deliver a complete ASCII coordinate list (.txt/.doc etc.) as a result of the geometry report of the final .ALG file.
- ii. Use appropriate levels and attributes for all elements to meet City of San Diego CADD Standards.

d) Records Research.

- i. If requested, all public or private records acquired to assist with right-of-way monument collection.
- ii. City records may include but are not limited to GIS scope plots, sewer and water sheets, loose leaf survey notes, Tie Point sheets, dedication or vacation drawings, easement drawings, benchmark list, and etc.
- iii. After initial search of City records by the Surveyor, they may request City assistance to search for hard to find records.
- e) Right-of-Way Monument Survey Locations

- All monuments within the survey limits shall be searched and located if found. Sufficient additional monuments to control all boundaries extending from the survey limits shall be located to facilitate LSS ROW Mapping (i.e. block corners, points of curve, and etc.).
 - All found survey monuments shall describe the character and identifying reference marks.
 - City survey notes and City drawings can be provided, as applicable.
- f) The appropriate City of San Diego cell library (V8 City existing.cel), font resource file (V8 City font.rsc), color table (V8 City color.tbl), line style (V8 City Line style.rsc), level scheme, and seed file parameters are to be used for placement of all elements in the design files, with strict adherence to "Working Units" and seed file "Global Origin". Base map level schemes are attached. A CD containing the most current version of the above seed files, cell libraries and font resource files will be provided, if needed, upon request.

3-10.7 Construction Survey/Staking.

- 1. Construction staking surveying shall be performed with the standards customarily adhered to by an experienced and competent land surveying firm using the degree of care and skill ordinarily exercised by reputable professionals practicing in the same field of service in the State of California. Where approval by the City is required, it is understood to be general approval only and shall not relieve the Design Firm of their responsibility to comply with all applicable laws, codes, and good consulting practices.
- 2. Field Measurements shall comply with the local standards of practice. All construction staking with a gradient of less than 1.5% shall be performed by a total station survey instrument. Gradients less than 0.2% shall require a level run prior to construction, and all said services shall be performed by the Surveyor.
- 3. The following are minimum requirement guidelines for various types of staking:
 - a) Limits of work 50-foot maximum interval.
 - b) Limits of Demolition 50-foot maximum interval.
 - c) Rough grade stakes 50-foot maximum interval.
 - d) Finish grade stakes 50-foot maximum interval.
 - e) Slope staking at 50-foot maximum interval.
 - f) Contour staking @ 50-foot maximum interval.
 - g) Curb stakes with offset to face of curb, and grade to top of curb with 50-foot maximum interval.
 - h) Storm drain at 50-foot maximum interval where grade exceeds 1%.

- i) Sewer lines at 50-foot maximum interval where grade exceeds 1%.
- j) Water lines at 50-foot' maximum interval offset to near curb face (no grades minimum cover).
- k) Dry utilities at 50-foot maximum interval where grade exceeds 1%.
- Construction staking involving horizontal and vertical curves shall be staked at 25-foot maximum intervals, and further densification for deltas on applicable curb returns and pipe joints.
- m) Storm Drain inlet stakes shall be on face of curb produced, and on string line grade.
- n) Walls staked at footing breaks, with station interval of 25-foot maximum intervals.
- o) Buildings offsets to outside face of wall.
- p) Bridge abutments and bents on opposing sides.
- **3-13.1 Completion.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. You shall submit a written assertion that the Work has been completed and is ready for Owner Acceptance. If, in the Engineer's judgment, the Work has been completed in accordance with the Contract Documents, the Engineer will set forth in writing the date the Work was completed. This will be the date that you are relieved from responsibility to protect and maintain the Work and to which liquidated damages will be computed.
- **3-13.1.1 Requirements Before Requesting a Walk-through.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

3-13.1.1 Requirements Before Requesting Substantial Completion.

- 1. The following items are required prior to requesting a Substantial Completion:
 - a) Remove temporary facilities from the Site.
 - b) Thoroughly cleaning the Site and removing all mark outs and construction staking.
 - c) Provide completed and signed Red-lines in accordance with 3-7.3 "Redlines and Record Documents".
 - d) Provide all material and equipment maintenance and operation instructions and/or manuals.
 - e) Provide all tools which are permanent parts of the equipment installed in the Project.
 - f) Provide and properly identify all keys for construction and all keys for permanent Work.

- g) Provide all final Special Inspection reports required by the applicable building Code.
- h) Provide all items specified to be supplied as extra stock. Wrap, seal, or place in a container all items as necessary to allow for storage by the City for future use. Verify the specified quantities.
- i) Ensure that all specified EOCP and certified wage rate documentations covering the Contract Time have been submitted.
- j) If the Work includes installing an irrigation system, provide the spare parts for the proposed irrigation system as specified in the Special Provisions.
- k) If the Work includes sewer and storm drain installations, the inspection shall include televising in accordance with 306-18, "VIDEO INSPECTION".
- I) If the Work includes a Plant Establishment Period, Work in accordance with 801-6, "MAINTENANCE AND PLANT ESTABLISHMENT" shall be completed prior to requesting Substantial Completion, unless approved otherwise by the Owner.
- m) Notify the Engineer to arrange a final inspection of permanent BMPs installed.

3-13.1.2 Walk-through and Punchlist Procedure. To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

- 1. You shall notify the Engineer 15 Working Days in advance of date of anticipated Substantial Completion to allow time for Engineer to schedule a Walk-through.
- 2. After you complete the requirements in 3-13.1.1, "Requirements Before Requesting Substantial Completion" and when you consider that the Work is Substantially Complete, you will notify the Engineer in writing that the Project is Substantially Complete and request a Walk-through. The Engineer will review your request and determine if the Project is ready for a Walk-through, by verifying whether you have completed all items as required by 3-13.1.1, "Requirements Before Requesting Substantial Completion". Within 7 Working Days, the City will either reject your request for a Walk-through in writing or schedule and conduct a Walk-through inspection. The Engineer shall facilitate the Walk-through.
- 3. The following documents shall be provided at the time of your Walk-through request: As-Built markup, Plans, specifications, technical data such as submittals and equipment manuals, draft final payment, warranties, material certifications, bonds, guarantees, maintenance service agreements, and maintenance and operating manuals.
- 4. Written warranties, except manufacturer's standard printed warranties, shall be on a letterhead addressed to you. Warranties shall be submitted in the format described in this section, modified as approved by the City, to suit the

- conditions pertaining to the warranty. Lack of submitting these items will delay start of Walk-through.
- 5. The Engineer will provide you with the Punchlist within 15 Working Days after the date of the Walk-through. The City shall not provide a preliminary Punchlist.
- 6. If the Engineer finds that the Project is not Substantially Complete as defined herein, the Engineer will terminate the Walk-through and notify you in writing.
- 7. If, at any time during the Engineer's evaluation of the corrective Work required by the Punchlist, the Engineer discovers that additional corrective Work is required, the Engineer may include that corrective Work in the Punchlist.
- 8. You shall remain solely responsible for the Project Site until the Project is completely operational, all Punchlist items have been corrected, all operation and maintenance manuals have been approved, all necessary warranty letters have been received, and the work is formally accepted by the City.
- 9. The Engineer shall meet with you within 5 Working Days of notification that all Punchlist items are corrected. You shall complete the Punchlist within 30 Working Days, and Working Days will continue to be counted until Acceptance of the Project.
- **Acceptance.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. You shall provide the completed, signed, and stamped DS-563 to the Engineer prior to Acceptance.
 - 2. You shall deliver the final As-builts and final billing prior to Acceptance.
 - 3. You shall assemble and deliver to the Engineer a Final Summary Report and Affidavit of Disposal prior to Acceptance.
 - 4. Acceptance shall occur after all of the requirements contained in the Contract Documents have been fulfilled. If, in the Engineer's judgment, you have fully performed the Contract, the Engineer will recommend to the City Engineer that your performance of the Contract be accepted. You shall receive notification of Acceptance in writing from the Owner and counting of working days shall cease and Warranty begins.
 - 5. Retention can be released 35 Calendar Days after NOC. Submit your request for retention to the Resident Engineer and they will mail to you a "Release of Claims" form which shall be completed and returned before the retention will be released.
- **3-13.3 Warranty.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. You shall warranty and repair all defective materials and workmanship for a period of 1 year. This call back warranty period shall start on the date the Work

- was accepted by the City unless the City has Beneficial Use or takes Occupancy of the project earlier (excluding water, sewer, and storm drain projects).
- 2. You shall warranty the Work free from all latent defects for 10 years and patent defects for a period of 4 years.
- 3. The warranty period for specific items covered under manufacturers' or suppliers' warranties shall commence on the date they are placed into service at the direction of the Engineer in writing.
- 4. All express warranties from Subcontractors, manufacturers', or Suppliers', of any tier, for the materials furnished and Work performed shall be assigned, in writing, to the City, and shall be delivered to the Engineer prior to the Acceptance of your performance of the Contract.
- 5. Replace or repair defective materials and workmanship in a manner satisfactory to the Engineer after notice to do so from the Engineer and within the time specified in the notice. If you fail to make such replacements or repairs within the time specified in the notice, the City may perform the replacement or repairs at your expense. If you fail to reimburse the City for the actual costs, your Surety shall be liable for the cost
- 6. Items that shall be warrantied free from defective workmanship and materials for a period longer than 1 year are as follows:

Specified Item	Minimum Warranty Period
Detectable Warning Tile Construction	3 Years of Manufacturer's Warranty
All Work Under SECTION 500 – PIPELINE REHABILITATION	3 Years
Fiber Optic Interconnect Cables	2 Years
Luminaires*	10 Years of Manufacturer's Warranty
LED Signal Modules	3 Years of Manufacturer's Warranty
Field Devices Associated with 700-6.3, "Adaptive Control Note"	See 700-6.3.9, "Warranty"

- * Provide documentation verifying that the induction luminaire models being offered for the Project are covered by the 10 year warranty.
- 7. If installed, you shall provide the City and property owner a copy of the manufacturer's warranty for private sewer pumps, including the alarm panel and all other accessories.
 - a) You shall involve the manufacturer in the installation and startup as needed to secure any extended warranty required.

- b) Nothing in here is intended to limit any manufacturer's warranty which provides the City with greater warranty rights than set forth in this section or the Contract Documents.
- c) The warranty shall include all components. The form of the warranty shall be approved by the Engineer in accordance with 3-13.3.2, "Warranty Format Requirements".
- 8. If, during the warranty period, any item of the Work is found to be Defective Work, you shall correct it promptly after receipt of written notice from the City to do so. The warranty period shall be extended with respect to portions of the Work corrected as part of the warranty requirements.

SECTION 4 - CONTROL OF MATERIALS

ADD:

- **4-3.6 Preapproved Materials.** To the "WHITEBOOK", ADD the following:
 - 3. You shall submit in writing a list of all products to be incorporated in the Work that are on the AML.

SECTION 5 - LEGAL RELATIONS AND RESPONSIBILITIES

5-4 INSURANCE. To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:

5-4 INSURANCE.

1. The insurance provisions herein shall not be construed to limit your indemnity obligations contained in the Contract.

5-4.1 Policies and Procedures.

- 1. You shall procure the insurance described below, at its sole cost and expense, to provide coverage against claims for loss including injuries to persons or damage to property, which may arise out of or in connection with the performance of the Work by you, your agents, representatives, officers, employees or Subcontractors.
- 2. Insurance coverage for property damage resulting from your operations is on a replacement cost valuation. The market value will not be accepted.
- 3. You shall maintain this insurance for the duration of this Contract and at all times thereafter when you are correcting, removing, or replacing Work in accordance with this Contract. Your liabilities under the Contract, e.g., your indemnity obligations, is not deemed limited to the insurance coverage required by this Contract.
- 4. The payment for insurance shall be included in the Contract Price as bid by you. Except as specifically agreed to by the City in writing, you are not entitled

- to any additional payment. Do not begin any Work under this Contract until you have provided and the City has approved all required insurance.
- 5. Policies of insurance shall provide that the City is entitled to 30 Days (10 Days for cancellation due to non-payment of premium) prior written notice of cancellation or non-renewal of the policy. Maintenance of specified insurance coverage is a material element of the Contract. Your failure to maintain or renew coverage or to provide evidence of renewal during the term of the Contract may be treated by the City as a material breach of the Contract.

5-4.2 Types of Insurance.

5-4.2.1 Commercial General Liability Insurance.

- 1. Commercial General Liability Insurance shall be written on the current version of the ISO Occurrence form CG 00 01 07 98 or an equivalent form providing coverage at least as broad.
- 2. The policy shall cover liability arising from premises and operations, XCU (explosions, underground, and collapse), independent contractors, products/completed operations, personal injury and advertising injury, bodily injury, property damage, and liability assumed under an insured's contract (including the tort liability of another assumed in a business contract).
- 3. There shall be no endorsement or modification limiting the scope of coverage for either "insured vs. insured" claims or contractual liability. You shall maintain the same or equivalent insurance for at least 10 years following completion of the Work.
- 4. All costs of defense shall be outside the policy limits. Policy coverage shall be in liability limits of not less than the following:

General Annual Aggregate Limit	Limits of Liability
Other than Products/Completed Operations	\$2,000,000
Products/Completed Operations Aggregate Limit	\$2,000,000
Personal Injury Limit	\$1,000,000
Each Occurrence	\$1,000,000

5-4.2.2 Commercial Automobile Liability Insurance.

- 1. You shall provide a policy or policies of Commercial Automobile Liability Insurance written on the current version of the ISO form CA 00 01 12 90 or later version or equivalent form providing coverage at least as broad in the amount of \$1,000,000 combined single limit per accident, covering bodily injury and property damage for owned, non-owned, and hired automobiles ("Any Auto").
- 2. All costs of defense shall be outside the limits of the policy.

- **Fating Requirements.** Except for the State Compensation Insurance Fund, all insurance required by this Contract as described herein shall be carried only by responsible insurance companies with a rating of, or equivalent to, at least "A-, VI" by A.M. Best Company, that are authorized by the California Insurance Commissioner to do business in the State, and that have been approved by the City.
- **5-4.3.1 Non-Admitted Carriers.** The City will accept insurance provided by non-admitted, "surplus lines" carriers only if the carrier is authorized to do business in the State and is included on the List of Approved Surplus Lines Insurers (LASLI list).

All policies of insurance carried by non-admitted carriers shall be subject to all of the requirements for policies of insurance provided by admitted carriers described herein.

Evidence of Insurance. Furnish to the City documents e.g., certificates of insurance and endorsements evidencing the insurance required herein, and furnish renewal documentation prior to expiration of this insurance. Each required document shall be signed by the insurer or a person authorized by the insurer to bind coverage on its behalf. We reserve the right to require complete, certified copies of all insurance policies required herein.

5-4.5 Policy Endorsements.

5-4.5.1 Commercial General Liability Insurance.

5-4.5.1.1 Additional Insured.

- 1. You shall provide at your expense policy endorsement written on the current version of the ISO Occurrence form CG 20 10 11 85 or an equivalent form providing coverage at least as broad.
- 2. To the fullest extent allowed by law e.g., California Insurance Code §11580.04, the policy shall be endorsed to include the City and its respective elected officials, officers, employees, agents, and representatives as additional insured.
- 3. The additional insured coverage for projects for which the Engineer's Estimate is \$1,000,000 or more shall include liability arising out of:
 - a) Ongoing operations performed by you or on your behalf,
 - b) your products,
 - c) your Work, e.g., your completed operations performed by you or on your behalf, or
 - d) premises owned, leased, controlled, or used by you.
- 4. The additional insured coverage for projects for which the Engineer's Estimate is less than \$1,000,000 shall include liability arising out of:
 - a) Ongoing operations performed by you or on your behalf,
 - b) your products, or
 - c) premises owned, leased, controlled, or used by you.

- **5-4.5.1.2 Primary and Non-Contributory Coverage.** The policy shall be endorsed to provide that the coverage with respect to operations, including the completed operations, if appropriate, of the Named Insured is primary to any insurance or self-insurance of the City and its elected officials, officers, employees, agents and representatives. Further, it shall provide that any insurance maintained by the City and its elected officials, officers, employees, agents and representatives shall be in excess of your insurance and shall not contribute to it.
- **5-4.5.1.3 Project General Aggregate Limit.** The policy or policies shall be endorsed to provide a Designated Construction Project General Aggregate Limit that will apply only to the Work. Only claims payments which arise from the Work shall reduce the Designated Construction Project General Aggregate Limit. The Designated Construction Project General Aggregate Limit shall be in addition to the aggregate limit provided for the products-completed operations hazard.
- 5-4.5.2 Commercial Automobile Liability Insurance.
- **5-4.5.2.1 Additional Insured.** Unless the policy or policies of Commercial Auto Liability Insurance are written on an ISO form CA 00 01 12 90 or a later version of this form or equivalent form providing coverage at least as broad, the policy shall be endorsed to include the City and its respective elected officials, officers, employees, agents, and representatives as additional insured, with respect to liability arising out of automobiles owned, leased, hired or borrowed by you or on your behalf. This endorsement is limited to the obligations permitted by California Insurance Code §11580.04.
- **5-4.6 Deductibles and Self-Insured Retentions.** You shall pay for all deductibles and self-insured retentions. You shall disclose deductibles and self-insured retentions to the City at the time the evidence of insurance is provided.
- **S-4.7 Reservation of Rights.** The City reserves the right, from time to time, to review your insurance coverage, limits, deductibles and self-insured retentions to determine if they are acceptable to the City. The City will reimburse you, without overhead, profit, or any other markup, for the cost of additional premium for any coverage requested by the Engineer but not required by this Contract.
- **Notice of Changes to Insurance.** You shall notify the City 30 Days prior to any material change to the policies of insurance provided under this Contract.
- **5-4.9 Excess Insurance.** Policies providing excess coverage shall follow the form of the primary policy or policies e.g., all endorsements.
- 5-4.10 Architects and Engineers Professional Insurance (Errors and Omissions Insurance).
 - 1. For Contracts with required engineering services (e.g., <u>Design-Build</u>, preparation of engineered Traffic Control Plans (TCP), and etc) by you, you shall keep or require all of your employees or Subcontractors, who provide professional engineering services under this contract, Professional Liability

coverage with a limit of \$1,000,000 per claim and \$2,000,000 annual aggregate in full force and effect.

- 2. You shall ensure the following:
 - a) The policy retroactive date is on or before the date of commencement of the Project.
 - b) The policy will be maintained in force for a period of 3 years after completion of the Project or termination of this Contract, whichever occurs last. You agree that for the time period specified above, there will be no changes or endorsements to the policy that affect the specified coverage.
- 3. If professional engineering services are to be provided solely by the Subcontractor, you shall:
 - a) Certify this to the City in writing and
 - b) Agree in writing to require the Subcontractor to procure Professional Liability coverage in accordance with the requirements set forth above.

5-4.11 Workers' Compensation Insurance and Employers Liability Insurance.

- 1. In accordance with the provisions of §3700 of the California Labor Code, you shall provide at your expense Workers' Compensation Insurance and Employers Liability Insurance to protect you against all claims under applicable state workers compensation laws. The City, its elected officials, and employees will not be responsible for any claims in law or equity occasioned by your failure to comply with the requirements of this section.
- 2. Limits for this insurance shall be not less than the following:

Workers' Compensation	Statutory Employers Liability
Bodily Injury by Accident	\$1,000,000 each accident
Bodily Injury by Disease	\$1,000,000 each employee
Bodily Injury by Disease	\$1,000,000 policy limit

- 3. By signing and returning the Contract you certify that you are aware of the provisions of §3700 of the Labor Code which requires every employer to be insured against liability for worker's compensation or to undertake self-insurance in accordance with the provisions of that code and you shall comply with such provisions before commencing the Work as required by §1861 of the California Labor Code.
- **5-4.11.1 Waiver of Subrogation.** The policy or policies shall be endorsed to provide that the insurer will waive all rights of subrogation against the City and its respective elected officials, officers, employees, agents, and representatives for losses paid under the terms of the policy or policies and which arise from Work performed by the Named Insured for the City.

- **5-10.2.1 Public Notice by Contractor.** To the "WHITEBOOK", items 2 and 3, DELETE in its entirety and SUBSTITUTE with the following:
 - 2. No less than 5 Working Days in advance of Project construction activities and utility service interruptions, you shall notify all critical facilities, businesses, institutions, property owners, residents, or any other impacted stakeholders within a minimum 300-foot (90 m) radius of the Project. Verbal and written notifications shall be sent to critical facilities (including but not limited to police stations, fire stations, hospitals, and schools). A copy of written notifications sent to any critical facility shall also be sent to the Resident Engineer. You shall keep records of the people contacted, along with the dates of notification, and shall provide the record to the Engineer upon request. You shall identify all other critical facilities that need to be notified.
 - 3. Furnish and distribute public notices in the form of door hangers using the City's format to all occupants and/or property owners along streets:
 - a) Where Work is to be performed at least Working 5 Working Days before starting construction or survey activities or impacting the community as approved by the Resident Engineer.
 - b) Within 5 Working Days of the completion of your construction activities where Work was performed, you shall distribute public notices in the form of door hangers, which outlines the anticipated dates of Asphalt Resurfacing or Slurry Seal.
 - c) 72 hours in advance of the scheduled resurfacing.
- **5-13 ELECTRONIC COMMUNICATION.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Virtual Project Manager shall be used on this Contract.
 - 2. You shall post all communications addressed to the Engineer concerning construction including RFIs, submittals, daily logs including the Weekly Statement of Working Days (WSWD), Storm Water, and transmittals to the Virtual Project Manager (VPM) website established for the Projects. This shall not supersede any Federal requirements.
 - 3. Maintain a list of scheduled activities including planned and actual execution dates for all major construction activities and milestones defined in the approved Schedule.
 - 4. Review and act on all communications addressed to you in the VPM project website.
 - 5. A user's guide to the VPM system is available on the City's website and shall be provided to you at the Pre-construction Meeting. Refer to the VPM training videos and forms at the location below:
 - https://www.sandiego.gov/ecp/edocref/

- 6. Submit the Sensitive Information Authorization Acknowledgement Form and VPM User Agreement located in the VPM user's guide at the Pre-construction Meeting.
- **Special Project Conditions.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:
 - 1. When removal of sediments and debris from channels and storm drains are required, you shall make a preliminary estimate of the materials that can be diverted to beneficial use. Receipts from disposal, re-use, and recycling options shall indicate that 65% of materials are diverted.
- **5-15.1 General.** To the "WHITEBOOK", item 10, DELETE in its entirety and SUBSTITUTE with the following:
 - 10. You shall ensure that construction staff have the required Hazardous Waste Operations and Emergency Response (HAZWOPER) certification for construction activities that have encountered flammable liquids or other hazardous substances. Construction staff shall include: City Engineers, City Laboratory Technicians, and City staff that perform onsite inspections.
 - a) If your Work encounters flammable liquids or other hazardous substances, you shall be responsible for scheduling training for all construction staff to attend and for submitting verification to the Engineer that construction staff have the required HAZWOPER certification prior to continuing that Work in that area. You shall maintain the HAZWOPER certifications annually until the construction activities triggering the requirement is complete, as approved by the Resident Engineer.

SECTION 6 - PROSECUTION AND PROGRESS OF THE WORK

6-1.1 Construction Schedule. To the "GREENBOOK", paragraph (1), sentence (1), DELETE in its entirety and SUBSTITUTE with the following:

After notification of award of the Contract and prior to the start of any Work, you shall submit your proposed Cost Loaded Construction Schedule to the Engineer at the pre-construction meeting.

To the "WHITEBOOK", item 1, subsection "e", "h", and "s", DELETE in their entirety and SUBSTITUTE with the following:

- e) Monthly progress payments are contingent upon the submittal of an updated Schedule to the Engineer. The Engineer may refuse to process the whole or part of any monthly payment if you refuse or fail to provide an acceptable schedule.
- h) Your Schedule shall include 7 Working Days for the Engineer to schedule and conduct a Walk-through inspection and 15 Working Days for the generation of the Punchlist. You shall Work diligently to complete all Punchlist items within 30 Working Days after the Engineer provides the Punchlist.

s) Refer to the Sample City Invoice materials in **Exhibit Q - Sample City Invoice** and use the format shown.

To the "WHITEBOOK", ADD the following:

- 3. The **120 Calendar Day** Plant Establishment Period is included in the stipulated Contract Time and shall begin with the acceptance of installation of the vegetation plan in accordance with Section 801-6, "MAINTENANCE AND PLANT ESTABLISHMENT".
- **6-1.1.2 Contracts More Than \$500,000 In Value.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Provide the Schedule to the Engineer in accordance with 6-1.1, "Construction Schedule" and 6-1.2, "Commencement of the Work".

To the "WHITEBOOK", item 2, DELETE in its entirety.

- **6-1.2 Commencement of the Work.** To the "WHITEBOOK", ADD the following:
 - 5. You shall submit a Cost Loaded Construction Schedule in accordance with 6-1.1, "Construction Schedule" at the scheduled pre-construction meeting.
 - 6. If a Cost Loaded Construction Schedule is not provided, the pre-construction meeting will still be held. The Contract Time shall commence at issuance of the NTP, but you shall be limited to the following activities until the Cost Loaded Construction Schedule has been submitted to the Resident Engineer with no exceptions taken:
 - a) Mobilization of your trailers, associated utility setup, and grading for trailer area
 - b) Permit Procurement
 - c) Fencing and temporary utilities for your storage areas
 - d) Submittal of anticipated critical path submittals
- **6-1.5.2 Excusable Non-Compensable Delays.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
- 6-1.5.2 Excusable Non-Compensable and Concurrent Delays.
 - The City shall only issue an extension of time for Excusable Delays that meet the requirements of 6-4.2, "Extensions of Time" for the following circumstances:
 - a) Delays resulting from Force Majeure.
 - b) Delays caused by weather.
 - c) Delays caused by changes to County, State, or Federal law.

- 2. When a non-excusable delay is concurrent with an Excusable Delay, you shall not be entitled to an extension of Contract Time for the period the non-excusable delay is concurrent with the Excusable Delay.
- 3. When an Excusable Non-Compensable Delay is concurrent with an Excusable Compensable Delay, you shall be entitled to an extension of Contract Time, but shall not be entitled to compensation for the period the Excusable Non-Compensable Delay is concurrent with the Excusable Compensable Delay.
- **6-4.2 Extensions of Time.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. The Contract Time shall not be modified except by Change Order.
 - 2. You shall notify the City in writing within **1 Working Day** after the occurrence and discovery of an event that impacts the Project Schedule.
 - a) If you believe this event requires a Change Order, you shall submit a written Change Order request with a report to the City that explains the request for Change Order within **5 Working Days**. The Change Order request must include supporting data, a general description of the discovery, the basis for extension, and the estimated length of extension. The City may grant an extension of time, in writing, for the Change Order request if you require more time to gather and analyze data.
 - 3. The Engineer shall not grant an extension of Contract Time in accordance with 6-1.5, "Excusable Delays" unless you demonstrate, through an analysis of the critical path, the following:
 - a) The event causing the delay impacted the activities along the Project's critical path.
 - b) The increases in the time to perform all or part of the Project beyond the Contract Time arose from unforeseeable causes beyond your control and without your fault or negligence and that all project float has been used.
 - 4. Any modifications to the Contract Time will be incorporated into the weekly document that the Engineer issues that stipulates the Contract Time. If you do not agree with this document, submit to the Engineer for review a written protest supporting your objections to the document within **30 Calendar Days** after receipt of the statement. Your failure to file a timely protest shall constitute your acceptance of the Engineer's weekly document.
 - a) Your protest will be considered a claim for time extension and shall be subject to 2-10.1, "Claims".

- **6-4.4 Written Notice and Report.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Your failure to notify the Resident Engineer within **1 Working Day** OR provide a Change Order request within **5 Working Days** after the event, in accordance with 6-4.2, "Extensions of Time", will be considered grounds for refusal by the City to consider such request if your failure to notify prejudices the City in responding to the event.

ADD:

6-6.1.1 Environmental Document.

- The City of San Diego has prepared a Notice of Exemption for 3405 Kite Street Storm Drain Emergency, WBS No. B-21153, as referenced in the Contract Exhibit. You shall comply with all requirements of the Notice of Exemption as set forth in Exhibit L.
- 2. Compliance with the City's environmental document shall be included in the Contract Price.

SECTION 7 - MEASUREMENT AND PAYMENT

7-3.1 General. To the "GREENBOOK" and "WHITEBOOK", paragraph (8), DELETE in its entirety and SUBSTITUTE with the following:

If, within the time fixed by law, a properly executed notice to stop payment is filed with the City, due to your failure to pay for labor or materials used in the Work, all money due for such labor or materials will be withheld from payment in accordance with applicable laws.

To the "WHITEBOOK", ADD the following:

- 1. Unless specified otherwise, the Contract Price includes use, consumer, and other taxes mandated by applicable legal requirements.
- 2. As provided in §7105 of the California Public Contract Code, if the Contract is not financed by revenue bonds, you are not responsible for the cost of repairing or restoring damage to the Project when damage was proximately caused by an act of God, in excess of 5% of the Contract Price, if the following occur:
 - a) The Project damaged was built in accordance with the Contract requirements.
 - b) There are no insurance requirements in the Contract for the damages.
- 3. COST OVERRUN NOTIFICATION: You shall promptly notify the City in writing of any potential cost overruns. Cost overruns shall include, but are not limited to the following:
 - a) Where the total cost for the performance of the scope of services defined in Section 1 Description of Work appears that it may be greater than the maximum compensation for this Contract.

- **7-3.2 Partial and Final Payment.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:
 - 1. The Final Payment, which is the release of Retention, shall be paid to you after you have successfully submitted the following required documents:
 - a) An affidavit that payrolls and bills for materials, equipment, and other indebtedness connected with the Work for which the City or the City's property might be responsible for or encumbered by.
 - b) A certificate evidencing that insurances required by the Contract Documents shall remain in force after Final Payment is currently in effect and shall not be canceled or allowed to expire until at least a 30 Calendar Days prior written notice has been given to the Engineer.
 - c) Consent of Surety to Final Payment.
 - d) If required by the Engineer, other data establishing payment or satisfaction of obligations such as receipts, releases and waivers of liens, claims, and security interests or encumbrances arising out of the Contract Documents. If a Subcontractor refuses to furnish a release or waiver required by the City, you may furnish a bond satisfactory to the Engineer to indemnify the City against such lien.
 - e) If required in the Contract Documents, the successful completion and submittal of the required reports such as construction demolition, waste recycling, and hydrostatic discharge reports.
 - f) Required EOCP Final Summary Report in accordance with Section 0-12, "Contract Records and Reports", record drawings, operations manuals, test reports, warranty documentation, and UL labels shall be submitted before requesting the release of retention.
 - g) Acceptance of the completed Project by the asset owning Department.

To the "WHITEBOOK", ADD the following:

- 2. Submit an invoice for payment after you successfully complete the required documents and the City will pay the invoice within 30 Calendar Days. The City will pay 6% annually for late retention payments.
- **7-3.2.1 Application for Progress Payment.** To the "WHITEBOOK", item 3, DELETE in its entirety and SUBSTITUTE with the following:
 - 3. The City shall not pay progress or partial payments until you submit to the Engineer an acceptable updated Schedule. It is solely your responsibility to prepare and submit the Schedule updates.
- **7-3.2.2 Amount of Progress Payments.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. The City will pay 6% annually for late progress payments.

- 2. Progress payments will be considered "late" if the following occur:
 - a) The City does not pay the contractor within 30 Calendar Days from receipt of an undisputed and properly submitted invoice. A properly submitted payment invoice means that the City has approved for payment the entire invoice amount or if the Resident Engineer has not disputed any portion of the application within 7 Calendar Days of the date of submission.
 - b) The application for payment does not require signing of a Contract Change Order.
- 3. The Engineer may withhold payment for any of the following reasons:
 - a) Defective or incomplete Work.
 - b) Not providing an updated and accurate Cost Loaded Construction Schedule in accordance with 6-1.1, "Construction Schedule".
 - c) Stop notices, wage orders, or other withholdings required by Applicable Law. Your failure to comply with 5-3.3, "Payroll Records" and the Contractor Registration and Electronic Reporting System requirements of the Contract Documents.
- 4. The Engineer may back charge the contract for any of the following reasons:
 - a) Defective or incorrect Work not remedied.
 - b) Damage to City property or a third party's property that was caused by you.
 - c) Liquidated Damages.
- **7-3.2.3 Waiver of Claims at Final Payment.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Your acceptance of Final Payment constitutes a waiver of affirmative Claims by you, except those previously made in writing and identified as unsettled at the time of Final Payment.
- **7-3.2.4 Withholding of Payment and Back Charge.** To the "WHITEBOOK", DELETE in its entirety.
- **7-3.5.1 General.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Unit Bid prices shall not be subject to adjustment regardless of quantity used, or if none is used, for the following Bid items:
 - a) imported backfill
 - b) shoring
 - c) water services
 - d) house connection sewers
 - e) water pollution control items

- 2. Upon discovery and prior to the Work, you shall notify the Resident Engineer if there is a change in Bid item quantity that increases the total Contract Price by 5% or \$100,000 or more, whichever is less.
- **7-3.11** Compensation Adjustments for Price Index Fluctuations. To the "WHITEBOOK" ADD the following:
 - 5. This Contract is not subject to the provisions of The "WHITEBOOK" for Compensation Adjustments for Price Index Fluctuations for paving asphalt.
- **7-4.3 Markup.** To the "WHITEBOOK", item 4, DELETE in its entirety and SUBSTITUTE with the following:
 - 4. When a Subcontractor is performing Extra Work, the allowance for overhead and profit shall be applied to the labor, materials, and equipment costs of the Subcontractor as follows:
 - a) Regardless of the number of a Subcontractor's tasks for Extra Work, you may only apply 10% for the first \$50,000 of the Subcontractor's portion of accumulated total cost then 5% for any remaining costs. You shall not apply 10% to any costs after the first \$50,000 of accumulated total costs from performing Extra Work.
 - b) If the accumulated costs of single or subsequent tasks exceed the \$50,000 threshold, you shall instead only apply 5% to any amounts in excess of the \$50,000.
 - c) Regardless of the number of hierarchical tiers of Subcontractors, you may only markup a Subcontractor's Work once.

SECTION 203 - BITUMINOUS MATERIALS

- **203-6.3.1 General.** To the "WHITEBOOK", ADD the following:
 - 3. Asphalt concrete for Job Mix Formula (JMF) and Mix Designs shall be Type III and shall not exceed 15% RAP.

SECTION 301 – SUBGRADE PREPARATION, TREATED MATERIALS, AND PLACEMENT OF BASE MATERIALS

- **301-1.6 Preparatory Repair Work.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:
 - 1. Prior to the placement of any asphalt concrete or application of slurry, you shall complete all necessary preparation and repair Work and shall obtain approval by the Resident Engineer.

ADD the following:

13. Asphalt concrete shall be Type III and shall not exceed 15% RAP in accordance with 203-6.3.1, "General".

SECTION 302 - ROADWAY SURFACING

- **302-4.5 Scheduling, Public Convenience and Traffic Control.** To the "GREENBOOK", paragraphs (1) and (2), DELETE in their entirety and SUBSTITUTE with the following:
 - In addition to the requirements of Part 6, you shall comply with the following:
 - a) At least 5 Working Days prior to commencing the Work, you shall submit your proposed Schedule to the Engineer for approval.
 - b) Based upon the approved schedule, you shall notify residents and businesses of the Work and post temporary "No Parking" signs 72 hours in advance.
 - c) Requests for changes in the approved Schedule shall be submitted to the Engineer for approval at least 3 Working Days before the street is scheduled to be sealed.

SECTION 303 - CONCRETE AND MASONRY CONSTRUCTION

303-5.1.1 General. To the "WHITEBOOK", ADD the following:

7. For the purposes of this section, the terms "walk" and "access ramp" shall be synonymous with "sidewalk" and "curb ramp and pedestrian ramp", respectively.

SECTION 402 - UTILITIES

- **402-7.2 Pipe Separations.** To the "WHITEBOOK", item 1, subsection "a", DELETE in its entirety and SUBSTITUTE with the following:
 - a) You shall notify the Engineer immediately if:
 - i. 1 foot (0.3 m) vertical separation as measured from the outside of pipe wall to the outside of pipe wall between sewer and water mains cannot be maintained.
 - ii. 10 feet (3.0 m) horizontal separation as measured from the outside of pipe wall to the outside of pipe wall between sewer and water mains cannot be maintained.
 - iii. 6 inches (152.4 mm) vertical separation as measured from the outside of pipe wall to the outside of pipe wall between utilities other than sewer and water mains cannot be maintained.
 - iv. 3 feet (0.9 m) or more of cover over the top of the water main cannot be maintained.
 - v. 5 feet (1.5 m) or more of cover over the top of the recycled water main cannot be maintained.

SECTION 600 - ACCESS

- **GENERAL.** To the "WHITEBOOK", item 5, DELETE in its entirety and SUBSTITUTE with the following:
 - 5. You shall notify Environmental Services Department via email (trash@sandiego.gov) of street closures affecting the regular scheduled solid waste collection at least 3 Working Days prior to the street closure. Include your business name and phone number, days of closure, time of scheduled closure, and date of anticipated street reopening in the notification.
 - a) You shall verify waste collection schedules via the Environmental Services website at:

http://www.sandiego.gov/environmental-services/collection/index.shtml

- b) You shall comply with the following requirements for trash, recycling, and yard waste collection:
 - i. Provide advance written notice to every property affected by blocked public right of way.
 - ii. Coordinate the relocation of trash, recycling, and yard waste containers to an accessible public street for the City's waste collection crews on collection day.
 - iii. When necessary, relocate the containers from the blocked streets to the accessible public right of way before the City's collection vehicles arrive to assist with collection on existing schedules. Return the containers to their point of origin to ensure the accuracy of inventory assignment by address.
- c) If the City's crews are unable to provide the citizens with the mandated services due to your failure to comply with these specifications, you shall collect trash, recyclables, and yard waste on the City's schedule and deliver to the City's designated locations. If you fail to perform this Work, you shall incur additional costs for the City to reschedule pick up of an area.

SECTION 601 - TEMPORARY TRAFFIC CONTROL FOR CONSTRUCTION AND MAINTENANCE WORK ZONES

- **General.** To the "WHITEBOOK", item 3, DELETE in its entirety and SUBSTITUTE with the following:
 - 3. Temporary "No Parking" and "No Stopping" signs shall be installed 72 hours before enforcement. Temporary "No Parking" and "No Stopping" signs shall be installed and removed as specified in the Special Provisions. Signs shall indicate specific days, dates, and times of restrictions. If violations occur, call Police Dispatch 619-531-2000 to enforce the Tow-Away notice.

Channelizing Devices. To the "WHITEBOOK", item 4, Barricades, ADD the following:

h) You shall place "OPEN TRENCH" signs (C27(CA)) on Type 3 Barricade within the construction Work zone, ahead of any Work areas with open trenches that are greater than 3 inches in depth, in accordance with California MUTCD SECTION 6F.103 (CA). The barricades shall be placed in a continuous manner and shall prevent pedestrian, vehicular, and biker access to the open trench area.

SECTION 1001 - CONSTRUCTION BEST MANAGEMENT PRACTICES (BMPs)

1001-1 GENERAL. To the "WHITEBOOK", ADD the following:

7. Based on a preliminary assessment by the City, this Contract is subject to **WPCP**.

END OF SUPPLEMENTARY SPECIAL PROVISIONS (SSP)

EXHIBIT L

NOTICE OF EXEMPTION

NOTICE OF EXEMPTION

		0	
(Check one or both TO: X		FROM:	City of San Diego Engineering & Capital Projects Department 525 B Street, Suite 750, MS 908A San Diego, CA 92101
Project Name	e: Kite Street Emergency Storm Drain	Repair	WBS No.: B-21153.02.06
Project Location-Specific: The project is located at 3405 Kite Street, San Diego, CA 92103 within the Uptown Community (Council District 3).			
Project Locat	cion-City/County: San Diego/San Dieg	0	
Description of nature and purpose of the Project: A recent inspection of an 18-inch diameter corrugated metal pipe (CMP) storm drain segment has revealed severe deterioration of over 50 feet of pipe length. The deterioration of the CMP has occurred underground, where storm water is conveyed east down a steep hillslope from a Type C curb inlet at 3405 Kite Street and discharges at a cleanout located at the base of the slope at 3410 Jackdaw Street. The deteriorated condition of the CMP within the hillslope has resulted in subsurface soil erosion from leaking stormwater, which has created a sinkhole in the center of the slope (17 feet long, 8 feet wide, and 16 feet deep), 15 feet of subgrade cylindrical void surrounding the eroded CMP uphill from the sinkhole, and 22 feet of void downhill from the sinkhole. The soil erosion has the potential to cause a sudden failure to the hillslope, which would send debris and/or stormwater toward the downstream residences. The chance of slope failure will continue to increase with future storm events. Therefore, the CMP requires immediate repair in order to halt further slope failure and prevent impacts to life, health, and property in the immediate area. The emergency scope of work includes the replacement of approximately 180 linear feet of existing deteriorated 18-inch diameter CMP storm drain pipe with new 18-inch diameter fusible HDPE (High-Density Polyethylene Pipe) with 24-inch casing, utilizing trenchless installation methods. Following completion of work, all areas impacted by the emergency will be restored to their pre-impact condition.			
Name of Public Agency Approving Project: City of San Diego			
Name of Pers	son or Agency Carrying Out Project:	Engineer Contact: Email: <u>Jla</u>	an Diego Fing & Capital Projects Department Jerry Jakubauskas; Iskubauskas@sandiego.gov / Phone: (619) 533-3755 Feet, Suite 750 (MS 908A), San Diego, CA 92101
() Minist () Declar (X) Emerg	s: (CHECK ONE) Perial (Sec. 21080(b)(1); 15268); Ped Emergency (Sec. 21080(b)(3); 15269 Rency Project: <u>CEQA Statute Sections 27</u> Rency Projects) Rency Projects) Rency Exemption:	∂(a));	and (4) and CEQA Guidelines Sections 15269(b)

() Statutory Exemption:

Reasons why project is exempt: The City of San Diego conducted an environmental review that determined the project meets the definition of an "Emergency" as defined in CEQA Guidelines Section 15359 (Emergency) as the project involves a sudden, unexpected occurrence, involving a clear and imminent danger, demanding immediate action to prevent or mitigate loss of, or damage to, life, health, property, or essential public services. This emergency repair is required in order to protect public health, safety and property, and is supported by the expert opinion of the City Engineer. Thus, this emergency activity is statutorily exempt from CEQA pursuant to CEQA Statute Section 21080(b)(2) and CEQA Guidelines Section 15269(b) (Emergency Projects) which exempts emergency repairs to publicly or privately owned service facilities necessary to maintain service essential to public health, safety or welfare. This activity is also statutorily exempt from CEQA pursuant to CEQA Statute Section 21080(b)(4) and CEQA Guidelines Section 15269(c) (Emergency Projects) which exempts specific actions necessary to prevent or mitigate an emergency.

medassary to provent or malgate an emergency.		
Lead Agency Contact Person : Jerry Jakubauskas	Telephone : (619) 533-3755	
If filed by applicant:1. Attach certified document of exemption finding.2. Has a notice of exemption been filed by the publ	ic agency approving the project? ()Yes ()No	
It is hereby certified that the City of San Diego has determined the above activity to be exempt from CEQA		
Carris Purcell	9/10/21	
Carrie Purcell, Interim Assistant Deputy Director	Date	
Check One: (X) Signed By Lead Agency () Signed by Applicant	Date Received for Filing with County Clerk or OPR:	

EXHIBIT M

CONTRACTOR'S COMPENSATION RATE SCHEDULE

EXHIBIT M

CONTRACTOR'S COMPENSATION RATE SCHEDULE

The following Compensation Rate Schedule shall constitute the maximum rates (e.g., labor, direct costs, etc.) for Extra Work, if any, provided by the Contractor during the term of this agreement.

These rates are being specified as the Contractor's standard established rates for calculating labor costs without allowance for overhead and profits. For markup provisions and allowable charges refer to 7-3.7, "Agreed Prices"

CONSTRUCTION * MANAGEMENT * SITE DEVELOPMENT Labor & Equipment Cost Rates October 1, 2021 to August 31, 2022

	Straight Time	Labor Only Overtime
Labor Rates Per Hour *		
Operating Engineer Foreman	139.00	46.00
Laborer	97.00	29.00
Teamster	106.00	34.00
Operating Engineer	128.00	40.00
Carpenter Foreman	120.00	40.00
Carpenter	107.00	34.00

* Additional daily labor charges for work performed outside San Diego County:

- \$75.00 daily subsistence per employee in North Riverside County (north of Ramona Expressway), Orange County, Imperial Valley, and Borrego Springs
- \$175.00 daily subsistence and hotel costs per employee in Coachella Valley, San Bernardino County, and Los Angeles County

Bare Vehicle and Equipment Rates Per Hour

Truck Cost Rates	
Paving Truck with Tools	52.00
Pickup Truck	28.00
Carpenter Truck with Generator/Tools	33.00
Broom Sweeper - High Dump	117.00
Broom Sweeper - Vacuum	155.00
10 Wheel, Demo Truck	65.00
Attenuator Truck with Arrow Board	70.00
Attenuator Attachment	10.00
Flatbed Truck	60.00
Water 2000-2500 Gal Truck	40.00
Semi Truck	78.00
Oil Distributor Truck	92.00
Sand Truck	75.00
Fuel Truck	65.00
Mechanic/Lube Truck with Tools	50.00
Traffic Control Truck with Arrow Board/Cones	55.00
Trailer Cost Rates	
Utility Trailer	15.00
Low Bed Trailer	25.00
40 Ft Flat Trailer	25.00

CONSTRUCTION * MANAGEMENT * SITE DEVELOPMENT Labor & Equipment Cost Rates October 1, 2021 to August 31, 2022

Dump Trailer	20.00
Tilt/Roller Trailer	20.00
Tack AC Trailer	25.00
Construction Equipment Cost Rates	
Blade Cat 16G	175.00
Blade Cat 140G	145.00
Blade Cat 140G with GPS	180.00
Skid Steer Loader 4'	37.00
Skid Steer Loader 6'	47.00
Bobcat Breaker Attachment	35.00
Bobcat Broom Attachment	20.00
Bobcat Grinder Attachment - 18"	50.00
Bobcat With Tracks	41.00
Dozer Cat D4H Track	85.00
Dozer Cat D5H Track	95.00
Dozer Cat D6H Track	185.00
Dozer Cat D8N Track	200.00
Dozer Attachment GPS	25.00
Excavator Mini	50.00
Excavator 20,000 Lb (Compact)	60.00
Excavator 40,000 Lb (Cat 312 Class)	62.00
Excavator 46,000 Lb (Cat 320 Class)	117.00
Excavator 77,000 Lb (Cat 330 Class)	127.00
Excavator 100,000 Lb (Cat 345 Class)	200.00
Rubber Tire Excavator 50,000 Lb	120.00
Excavator Attachment Breaker	90.00
Excavator Attachment Wheel/Compactor	30.00
Backhoe - Cat 446 Rt	70.00
Backhoe Attachment Breaker	40.00
Backhoe Attachment Wheel/Compactor	15.00
Forklift 6,000 Lb	35.00
Forklift 12,000 Lb	50.00
Forklift 22,500 Lb	60.00
Forklift 30,000 Lb	80.00
Inertial Profiler	175.00
Wheel Loader 19,000 lb (Cat 920 Class)	52.00
Wheel Loader 27,000 lb (Cat 936 Class)	67.00
Wheel Loader 42,000 lb (Cat 950 Class)	97.00
Wheel Loader 51,000 Lb (Cat 966 Class)	145.00

CONSTRUCTION * MANAGEMENT * SITE DEVELOPMENT Labor & Equipment Cost Rates October 1, 2021 to August 31, 2022

\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\	045.00
Wheel Loader 66,000 Lb (Cat 980 Class)	215.00
Track Loader 44,000 Lb (Cat 963 Class)	135.00
Skiploader	37.00
Material Transfer Vehicle	400.00
Asphalt Paver	300.00
Roller 84" Vibratory Drum	52.00
Roller 84" Vibratory Sheepsfoot Drum	57.00
AC Rubber Tire Roller 15 Ton	57.00
AC Rubber Tire Roller 25 Ton	77.00
Roller Dual Drum 48" 3-5 Ton	30.00
AC Roller Vibratory Dual Drum 6-8 Ton	70.00
AC Roller Vibratory Dual Drum 8-10 Ton	80.00
AC Roller Vibratory Dual Drum 10-12 Ton	105.00
Scraper (Cat 613 Class)	150.00
Scraper (Cat 623 Class)	185.00
Farm Tractor	125.00
Cost Rates of Construction Equipment and Hand Tools	
Absorption Crash Cushion	4.00
AC Pick-Up Machine	115.00
Backup AC Pick-up Machine	115.00
Compressor Package 180 CFM	25.00
Berm Builder	75.00
Backpack Blower	8.00
Manhole Blower	10.00
Arrow Solar Board	15.00
Speed Radar Sign	15.00
Changeable Message Board	25.00
Cement Mixer	10.00
Compactor - Ram X	65.00
Compactor - Wacker, Hand Held	12.00
Compactor 4 X 4 Sheepsfoot Tow	15.00
Compactor 5 X 5 Sheepsfoot Tow	18.00
Concrete Saw, Walk Behind	25.00
Concrete Screed	75.00
Cutoff Saw/Chainsaw	12.00
Concrete Sawcutter - 30Hp with Trailer	100.00
Disc, Offset, Rome	15.00
Generator - 1 To 75 Kw	5.00
GPS Rover	25.00
<u> </u>	23.00

CONSTRUCTION * MANAGEMENT * SITE DEVELOPMENT Labor & Equipment Cost Rates October 1, 2021 to August 31, 2022

Jobsite Shed / Storage Box	2.00
K-Rail per LF - Monthly	4.00
K-Rail Lifter	5.00
Laser Level	15.00
Lite Tower, Towable 30'	20.00
Paint/Cure Sprayer	7.00
Pavement Breaker	12.00
Pumps - Water	21.00
Sandblast Pot - 1 Sk	10.00
Stripping Winch	20.00
Vibra Plate	10.00
Water Buffalo - Tow Tank	17.00

EXHIBIT N

LOCATION MAP






Kite Street Storm Drain Emergency

SENIOR ENGINEER Jong Choi 619-533-5493 PROJECT MANAGER Manuel Gonzalez 619-533-3471 FOR QUESTIONS ABOUT THIS PROJECT

Call: 619-533-4207

Email: engineering@sandiego.gov

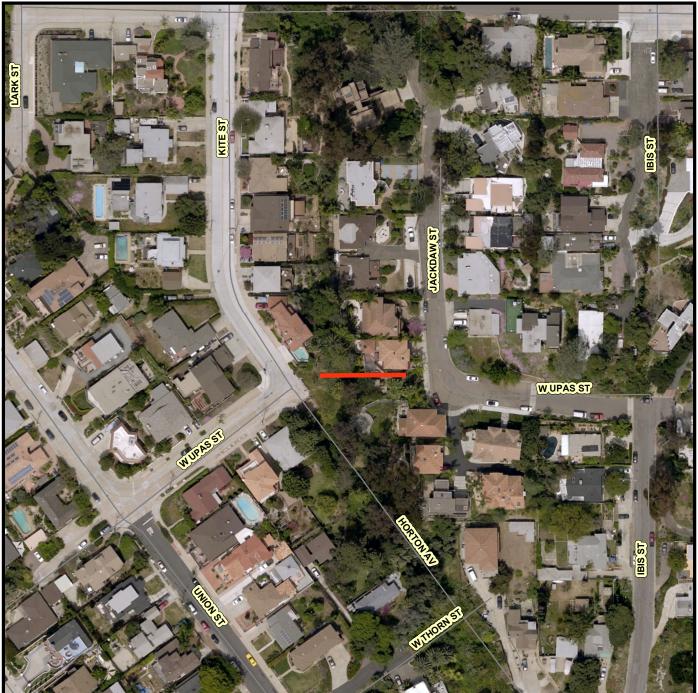

Legend

Area of Work

W E

COMMUNITY NAME: Mid-Town

Date: 8/19/2021

3405 Kite Street Storm Drain Emergency

COUNCIL DISTRICT: 3

SanGIS

WBS NO: B21153

EXHIBIT O

CONTRACTOR'S NOTES FOR EMERGENCY PROJECTS

CONTRACTOR'S NOTES

- 1. THE CONTRACTOR SHALL BE RESPONSIBLE FOR SURVEY MONUMENTS AND/OR VERTICAL CONTROL BENCHMARKS WHICH ARE DISTURBED OR DESTROYED BY CONSTRUCTION. A LICENSED LAND SURVEYOR OR LICENSED CIVIL ENGINEER AUTHORIZED TO PRACTICE LAND SURVEYING IN THE STATE OF CALIFORNIA SHALL FIELD LOCATE, REFERENCE, AND/OR PRESERVE ALL HISTORICAL OR CONTROLLING MONUMENTS PRIOR ANY EARTHWORK, DEMOLITION OR SURFACE IMPROVEMENTS. IF DESTROYED, A LICENSED LAND SURVEYOR SHALL REPLACE SUCH MONUMENT(S) WITH APPROPRIATE MONUMENTS. WHEN SETTING SURVEY MONUMENTS USED FOR RE-ESTABLISHMENT OF THE DISTURBED CONTROLLING SURVEY MONUMENTS AS REQUIRED BY SECTIONS 6730.2 AND 8771 OF THE BUSINESS AND PROFESSIONS CODE OF THE STATE OF CALIFORNIA. A CORNER RECORD OR RECORD OF SURVEY, AS APPROPRIATE, SHALL BE FILLED WITH THE COUNTY SURVEYOR. IF ANY VERTICAL CONTROL IS TO BE DISTURBED OR DESTROYED, THE CITY OF SAN DIEGO FIELD SURVEY SECTION SHALL BE NOTIFIED IN WRITING AT LEAST 7 DAYS PRIOR TO CONSTRUCTION. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE COST OF REPLACING AND VERTICAL CONTROL BENCHMARKS DESTROYED BY THE CONSTRUCTION.
- CONSTRUCTION STORM WATER PROTECTION NOTES
 - a. TOTAL SITE DISTURBANCE AREA: 0.5 ACRES)
 - b. HYDROLOGIC UNIT/WATERSHED: PUEBLO SAN DIEGO/SAN DIEGO BAY WMA
 - c. HYDROLOGIC SUBAREA NAME & NO: LINDBERGH / 908.21
 - d. THE CONTRACTOR SHALL COMPLY WITH THE REQUIREMENTS OF THE
 - MWPCP

 x WPCP

 THE PROJECT IS SUBJECT TO MUNICIPAL STORM WATER PERMIT NO.

 PD 2012 0001 AS AMENDED BY PD 2015 0001 AND PD 2015 0100
 - R9-2013-0001 AS AMENDED BY R9-2015-0001 AND R9-2015-0100

 WPPP
 - THE PROJECT IS SUBJECT TO MUNICIPAL STORM WATER PERMIT NO. R9-2013- 0001 AS AMENDED BY R9-2015-0001 AND R9-2015-0100 AND CONSTRUCTION GENERAL PERMIT ORDER 2009-0009-DWQ AS AMENDED BY ORDER 2010-0014-DWQ AND 2012-0006-DWQ

TRADITIONAL: RISK LEVEL 1□ 2□ 3□

LUP: RISK TYPE 1□ 2□ 3□

e.

CONSTUCTION SITE PRIORITY

☐ ASBS ☐ HIGH ☐ MEDIUM ☒ LOW

- 3. ALL ADVANCE METERING INFRASTRUCTURE (AMI) DEVICES ATTACHED TO THE WATER METER OR LOCATED IN OR NEAR WATER METER BOXES, COFFINS, OR VAULTS SHALL BE PROTECTED AT ALL TIMES IN ACCORDANCE WITH THE CONTRACT DOCUMENTS.
- 4. CONTRACTOR TO EXCAVATE AROUND WATER METER BOX (CITY PROPERTY SIDE) TO DETERMINE IN ADVANCE, THE EXACT SIZE OF EACH SERVICE BEFORE TAPPING MAIN.
- 5. CITY FORCES, WHERE CALLED OUT SHALL MAKE PERMANENT CUTS & PLUGS, CONNECTIONS, ETC. EXISTING MAINS SHALL BE KEPT IN SERVICE IN LIEU OF HIGH-LINING.
- 6. STORM DRAIN INLETS ARE TO REMAIN FUNCTIONAL/OPERATIONAL AT ALL TIMES DURING CONSTRUCTION.
- 7. CONTRACTOR SHALL NOTIFY THE RESIDENT ENGINEER IMMEDIATELY IF A ONE FOOT VERTICAL SEPARATION (FROM OUTSIDE PIPE WALL TO OUTSIDE PIPE WALL) BETWEEN SEWER AND WATER MAINS CANNOT BE MAINTAINED.
- 8. CONTRACTOR SHALL NOTIFY THE RESIDENT ENGINEER IMMEDIATELY IF A 6-INCH VERTICAL SEPARATION (FROM OUTSIDE PIPE WALL TO OUTSIDE PIPE WALL) BETWEEN UTILITIES OTHER THAN SEWER AND WATER MAINS CANNOT BE MAINTAINED.
- 9. CONTRACTOR TO MAINTAIN A MINIMUM 3' OF COVER OVER TOP OF WATER MAIN.
- 10. CONTRACTOR SHALL RESTORE ALL TRENCHES ON THE PAVEMENT WORKED BY CITY FORCES AFTER FINAL CONNECTION.
- 11. CONTRACTOR SHALL PROVIDE A 1-FOOT SAND CUSHION OR A MINIMUM 6-INCH SAND CUSHION WITH 1-INCH NEOPRENE PAD FOR ALL CROSSINGS WHERE VERTICAL CLEARANCE BETWEEN CROSSINGS IS 1-FOOT OR LESS.
- 12. POTHOLE ALL UTILITIES THAT CROSS PROPOSED WATER MAIN BEFORE TRENCHING
- 13. WHEN APPLICABLE, EXISTING UTILITY CROSSING AS SHOWN ON THE PLANS ARE APPROXIMATE AND ARE NOT EXACT.
- 14. FOR COORDINATION OF THE SHUTDOWN OF TRANSMISSION MAINS (16 INCHES OR LARGER), CONTACT THE CITY'S SENIOR WATER DISTRIBUTION OPERATIONS SUPERVISOR AT (616) 524-7438. FOR COORDINATION OF THE SHUTDOWN OF DISTRIBUTION MAINS (LESS THAN 16 INCHES), CONTACT THE CITY'S WATER OPERATIONS DISTRICT MANAGER AT (619) 527-3945.

EXHIBIT P

ADVANCED METERING INFRASTRUCTURE (AMI) DEVICE PROTECTION

Protecting AMI Devices in Meter Boxes and on Street Lights

The Public Utilities Department (PUD) has begun the installation of the Advanced Metering Infrastructure (AMI) technology as a new tool to enhance water meter reading accuracy and efficiency, customer service and billing, and to be used by individual accounts to better manage the efficient use of water. All AMI devices shall be protected per Section 402-2, "Protection", of the 2018 Whitebook.

AMI technology allows water meters to be read electronically rather than through direct visual inspection by PUD field staff. This will assist PUD staff and customers in managing unusual consumption patterns which could indicate leaks or meter tampering on a customer's property.

Three of the main components of an AMI system are the:

A. Endpoints, see Photo 1:

Photo 1




B. AMI Antenna attached to Endpoint (antenna not always required), see Photo 2:



Network Devices, see Photo 3:

Photo 3

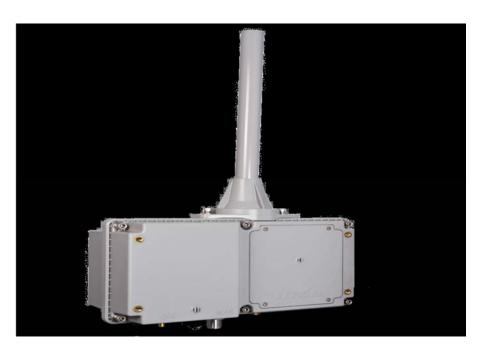

AMI endpoints transmit meter information to the AMI system and will soon be on the vast majority of meters in San Diego. These AMI devices provide interval consumption data to the PUD's Customer Support Division. If these devices are damaged or communication is interrupted, this Division will be alerted of the situation. The endpoints are installed in water meter boxes, coffins, and vaults adjacent to the meter. A separate flat round antenna may also be installed through the meter box lid. This antenna is connected to the endpoint via cable. The following proper installation shall be implemented when removing the lid to avoid damaging the antenna, cable, and/or endpoint. Photo 4 below demonstrates a diagram of the connection:

Photo 4



The AMI device ERT/Endpoint/Transmitter shall be positioned and installed as discussed in this Appendix. If the ERT/Endpoint/Transmitter is disturbed, it shall be re-installed and returned to its original installation with the end points pointed upwards as shown below in Photo 5.

The PUD's code compliance staff will issue citations and invoices to you for any damaged AMI devices that are not re-installed as discussed in the Contract Document Photo 5 below shows a typical installation of an AMI endpoint on a water meter.

Photo 5

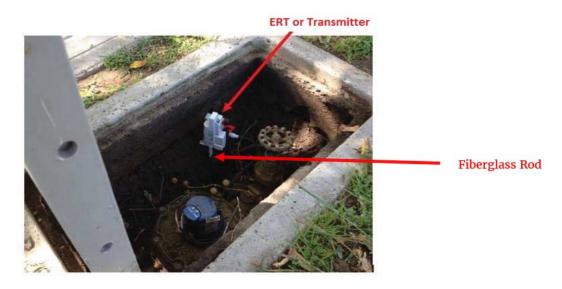


Photo 6 below is an example of disturbance that shall be avoided:

Photo 6



You are responsible when working in and around meter boxes. If you encounter these endpoints, use proper care and do not disconnect them from the registers on top of the water meter. If the lid has an antenna drilled through, do not change or tamper with the lid and inform the Resident Engineer immediately about the location of that lid. Refer to Photo 7 below:

Photo 7



Another component of the AMI system are the Network Devices. The Network Devices are strategically placed units (mainly on street light poles) that collect interval meter reading data from multiple meters for transmission to the Department Control Computer. If you come across any of these devices on street lights that will be removed or replaced (refer to Photos 8 and 9 below), notify AMI Project Manager Arwa Sayed at (619) 362-0121 immediately.

Photo 8 shows an installed network device on a street light. On the back of each Network Device is a sticker with contact information. See Photo 9. **Call PUD Water Emergency Repairs at 619-515-3525 if your work will impact these street lights.** These are assets that belong to the City of San Diego and you shall be responsible for any costs of disruption of this network.

Photo 8



Network Device

Photo 9



If you encounter any bad installations, disconnected/broken/buried endpoints, or inadvertently damage any AMI devices or cables, notify the Resident Engineer immediately. The Resident Engineer will then immediately contact the AMI Project Manager, Arwa Sayed, at (619) 362-0121.

EXHIBIT Q

SAMPLE CITY INVOICE

City of San Diego, CM&FS Div., 9753 Chesapeake Drive, SD CA 92123

Project Name:

Work Order No or Job Order No.

City Purchase Order No.

Resident Engineer (RE):

RE Phone#: Fax#:

Contractor's Name:

Contractor's Address:

Invoice No.

Invoice No.

Invoice Date:

Billing Period: (To)

This Estimate Previous Totals To Date Item Description Contract Authorization Totals to Date Item # % / QTY Unit Price Qty Extension Amount % / QTV Amount Amount 0.00 \$ 1 \$ 2 \$ \$ 0.00% \$ \$ 0.00% 3 _ \$ \$ 0.00% 4 \$ 0.00% 5 \$ 0.00% 6 \$ \$ 0.00% 8 \$ \$ \$ 0.00% \$ 0.00% 5 0.00% 6 \$ \$ \$ \$ \$ 0.00% \$ 8 \$ \$ 0.00% 9 \$ \$ 0.00% \$ \$ 0.00% 10 \$ 11 \$ \$ 0.00% \$ \$ 0.00% 12 \$ 13 \$ \$ 0.00% 14 \$ \$ 0.00% --0.00% 15 \$ \$ \$ 0.00% 16 \$ \$ _ _ **Field Orders** \$ \$ 0.00% -\$ 0.00% -\$ **CHANGE ORDER No.** \$ \$ 0.00% \$ 0.00% \$ \$ Total Authorized Amount (including approved Change Order) \$ Total Billed

SUMMARY A. Original Contract Amount I certify that the materials Retention and/or Escrow Payment Schedule \$ have been received by me in \$0.00 B. Approved Change Order #00 Thru #00 Total Retention Required as of this billing (Item E) Total Authorized Amount (A+B) the quality and quantity specified Previous Retention Withheld in PO or in Escrow \$0.00 D. Total Billed to Date \$0.00 Add'l Amt to Withhold in PO/Transfer in Escrow: **Resident Engineer** Less Total Retention (5% of D) Amt to Release to Contractor from PO/Escrow: Less Total Previous Payments **Construction Engineer** G. Payment Due Less Retention \$0.00 Contractor Signature and Date: \$0.00 H. Remaining Authorized Amount

NOTE: CONTRACTOR TO CALCULATE TO THE 2ND DECIMAL PLACE.

EXHIBIT R

SCOPE OF WORK

SCOPE OF WORK

1. SCOPE OF WORK: The Work consists of but is not limited to the repair and reconstruction of a sinkhole and failed storm drain system located adjacent to 3405 Kite Street. The failed storm drain pipe is an 18-inch corrugated metal pipe (CMP) that is approximately 180 -feet in length and starts from a Type C curb inlet adjacent to 3405 Kite Street. The CMP traverses east within the City right-of-way and discharges to a cleanout located in front of 3410 Jackdaw Street.

Repairs will include but is not limited to replace approximately 180 linear feet of existing deteriorated 18-inch CMP storm drain with new 18-inch fusible HDPE pipe within 24-Inch casing, including design and utilization of trenchless installation methods. Repairs will also include restoration to the slope to pre emergency conditions and any necessary street repairs.

- **1.1.** The Work shall be performed in accordance with:
 - **1.1.1. Project Close Out & As-Builts:** Consultant to provide as-built plans, supporting documents, and project files to the City as requested.
 - **1.1.2. Deliverables:** The deliverables for this task as-built drawings and other documents final consultant documents shall be delivered four weeks after project completion.
- **2. LOCATION OF WORK:** The location of the Work is as follows:

3405 Kite Street, San Diego, CA 92103

3. CONTRACT TIME: The Contract Time for completion of the Work, including the Plant Establishment Period shall be completed within **260 Working Days** from the date of issuance of the Notice to Proceed. Design shall be completed concurrent with construction and shall be completed within the first 70 working days.
